






Jamie Browder
Project Manager

Eltham Bridge Master Schedule

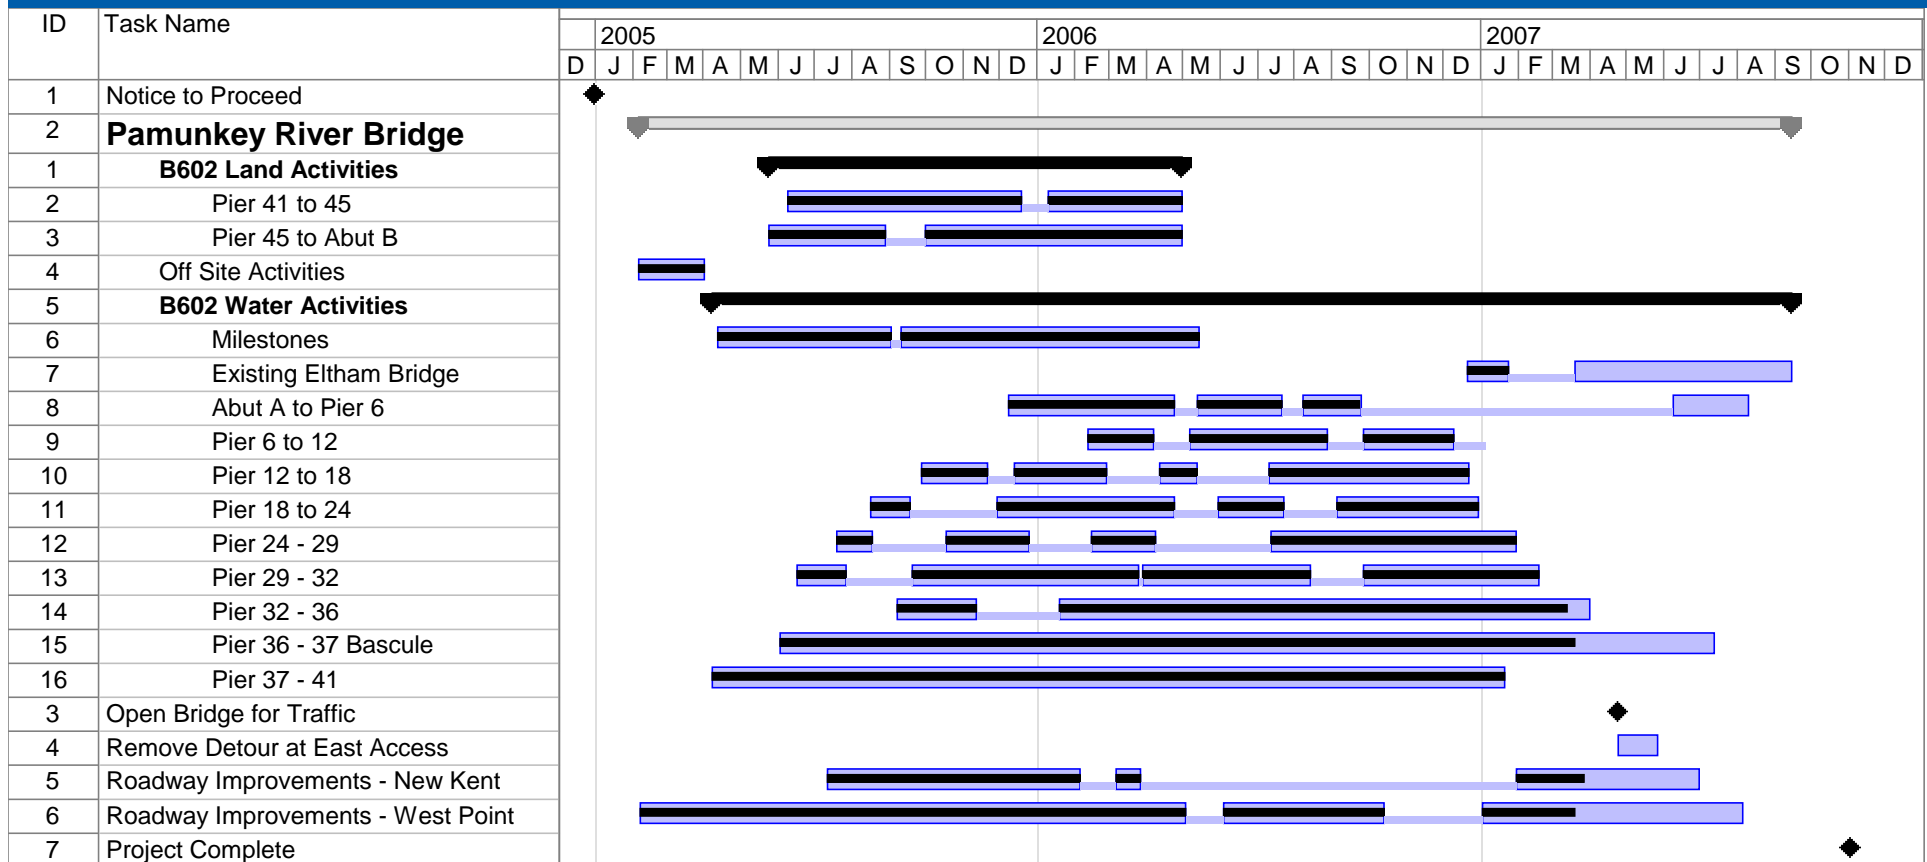

Maintenance of Traffic

- F Street will continue to be closed for another week or so until we get brick pavers complete.
- Temporary lane closures will be used during daytime as required by construction.

Eltham Bridge Current Activities

- Working on aligning the racks & pinions and machinery for bascule.
- Installing wiring and light poles on the bridge.
- Building brick pilasters.
- Forming and pouring fixed decks at 37 & 36 and forming and pouring Kansas Corral railing.
- Installing pedestrian railing.

Eltham Bridge Current Activities

- Installing the barrier/warning gates on Town side.
- Paving F Street, commercial entrances, & Kirby Street.
- Planting trees and other landscaping.
- Grading the Eltham approach & Kentwood Ave.

Eltham Bridge Progress



Operator's Tower



West view of bridge

Eltham Bridge Progress



Bascule span center joint



Westward view of bridge from
bascule span

Eltham Bridge Progress



Westward view from Chelsea Road
– landscaping, rip rap ditch



Entrance to West Point shopping
center with brick pavers

Eltham Bridge Progress



Commercial entrances off Rte 33



West Point Glass entrance

Eltham Bridge Progress



F Street pavement



South view of Kirby Street from
Rte 33

Eltham Bridge Progress



North view of Kirby Street from
13th Street



West view towards Eltham
approach of new Eltham bridge

Eltham Bridge 30-day Look Ahead

- Continue to align racks & pinions, aligning machinery, and begin testing of bascule.
- Installing light poles on bridge and in Town.
- Grade and pave the Town approach of Rte. 33.
- Complete grading, placing stone, & paving the Eltham approach and Kentwood Ave.
- Install the barrier on MSE wall and complete approach slab on Town side.

Eltham Bridge 30-day Look Ahead

- Energizing the electrical system for the Bascule machinery and spans.
- Completing the landscaping that can be done during this planting season.
- Installing brick pavers at F Street and the crosswalks that are ready.
- Continue with Kansas Corral railing and pedestrian railing.

Eltham Bridge 30-day Look Ahead

- Will complete the brick pilasters and remaining brick work on bascule.
- Will groove the bridge decks and stripe the two lanes across the bridge

Questions?

Jamie Browder
Project Manager

(804) 843-3641

