



Price Proposal

A DESIGN-BUILD PROJECT

Route 606 Loudoun County Parkway/Old Ox Road Reconstruction and Widening

From: 0.265 Miles South of Route 621 Evergreen Mills Road
To: 0.073 Miles South of Route 267 Dulles Greenway



Loudoun County, Virginia

State Project No.: 0606-053-983

Federal Project No.: FPN 5A01(165)

Contract ID No.: C00097529DB64

Date: April 21, 2014

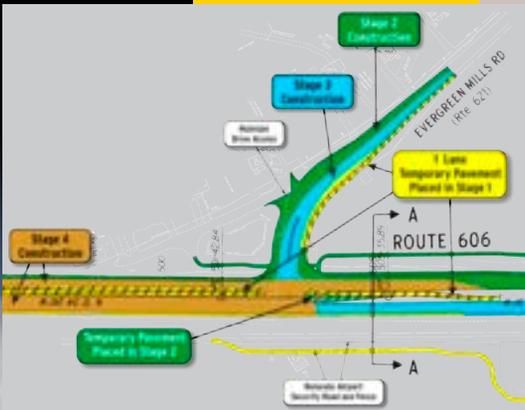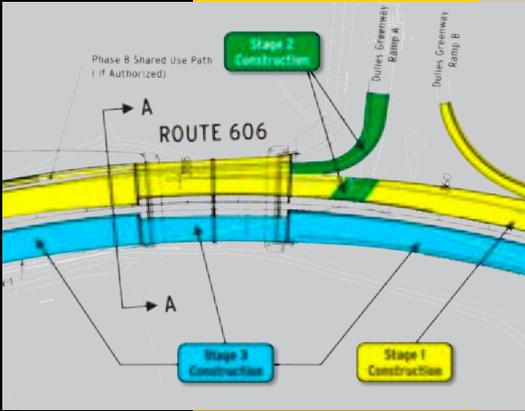

4.0.1.2 Price Proposal Checklist

ATTACHMENT 4.0.1.2

**DESIGN-BUILD PRICE PROPOSAL
CHECKLIST**

**Project Name: Route 606 Loudoun County Parkway/Old Ox Road
Reconstruction and Widening
Contract ID Number: C00097529C64**

➤ **Contents of Price Proposal:**

- Proposal Price for Phase A and Phase B, in both numbers and words (Attachment 4.8.1)**
- Schedule of Items for Phase A and Phase B Price Proposal itemized in accordance with Part 1, Section 4.8.2, including material quantities and costs of each proposed work package**
- Proposed Monthly Payment Schedule for Phase A and Phase B Price Proposal showing the anticipated schedule on which funds will be required and associated value of work in accordance with Part 1, Section 4.8.3**
- Phase A and B Price Adjustment Information and Forms for Fuel, Asphalt and Steel, including identification of pay items and associated quantities eligible for adjustment (Part 3, Section 6.3, Attachments 6.3) for the Phase A and Phase B Price Proposal**
- Proposal Guaranty (C-24) required by Section 102.07 of Part 5, Division I Amendments to the Standard Specifications for both the Phase A and Phase B Price Proposal**
- Sworn Statement Forms (C-104, C-105, Attachments 4.8.6(a) and 4.8.6(b))**
- Phase A and Phase B DBE Requirements Forms (C-111, C-49 and C-112) as applicable (Attachments 4.8.7(a), 4.8.7(b) and 4.8.7(c))**
- CD-ROM containing the entire Price Proposal in a single cohesive Adobe PDF file**

American Infrastructure-VA, Inc.

4.8.1 Price Proposal

ATTACHMENT 4.8.1


PHASE A and B PRICE PROPOSAL FORM

4.8.1 Offeror shall specify the pricing information for the items below, the dollars amount shall be in whole numbers:

Price Proposal Cost Breakdown Summary:	Phase A	Phase B
Design Services, LS	\$ 15,459,519	\$ 10,000
Mobilization (Construction), LS	\$ 4,397,362	\$ 34,378
Quality Assurance (QA) (Construction), LS	\$ 1,045,465	\$ 25,000
Quality Control (QC) (Construction), LS	\$ 1,320,065	\$ 25,000
Earthwork (Roadway), LS	\$ 17,556,879	\$ 440,000
Earthwork (Dam Modification), LS	\$ 554,058	\$ 0
Roadway Incidentals, LS	\$ 839,958	\$ 81,510
Bridge (Structures), LS	\$ 5,177,384	\$ 211,814
Drainage (Structures), LS	\$ 9,337,317	\$ 75,000
Principal Spillway Extension, LS	\$ 840,951	\$ 0
Retaining Walls, LS	\$ 2,442,813	\$ 0
Dam Riser Structure, LS	\$ 51,209	\$ 0
Sampling Building, LS	\$ 107,994	\$ 0
Utilities, LS	\$ 13,523,336	\$ 100,101
Pavement, LS	\$ 9,407,807	\$ 0
Permanent Traffic Control/Signage, LS	\$ 898,883	\$ 9,360
Maintenance of Traffic, LS	\$ 1,187,950	\$ 20,000
Shared Use Path	\$ 0	\$ 686,813
All Others Costs, LS	\$ 3,809,851	\$ 0
Subtotal	\$ 87,958,801	\$ 1,718,976

Phase A and Phase B Total Proposal Price; (Specify the Total Lump Sum price in both numbers and words, this price shall equal to the total sum of Phase A and Phase B of the items listed above)

Lump Sum (LS): EIGHTY NINE MILLION SIX HUNDRED SEVENTY SEVEN THOUSAND SEVEN HUNDRED SEVENTY SEVEN dollars and ZERO cents (\$89,677,777⁰⁰)

Signature:  Date: 04/21/14
Aaron T. Myers, Vice President/CM

Design-Builder: American Infrastructure-VA, Inc.

Vendor No.: G303

4.8.2

Schedules of Items

Attachment 4.8.2(a)
State Project 0606-053-093
SCHEDULE OF ITEMS Phase A

This schedule of items shall identify the material quantities and costs of each proposed work package, using the WBS established in the Proposal Schedule submitted by the Offeror. The material quantities and costs listed for

Activity ID ¹	Work Package Description ²	Fuel (F) or Price (P) Adjustment	VDOT Item Number ³	VDOT Material Item Description ³	Quantity	Unit	Budgeted Cost (\$)
VARIOUS	CONSTRUCTION SERVICES		00100	MOBILIZATION	1	LS	\$ 2,285,045
VARIOUS	SEGMENT A, B, C, D, & E CONSTRUCTION		00101	CONSTRUCTION SURVEYING (CONSTR.)	1	LS	\$ 281,651
VARIOUS	PROJECT SERVICES		00105	NS PUBLIC RELATIONS	1	LS	\$ 76,578
CAG001020, CBG001020, CCG001020, CDG001020, CEG001020	SEGMENT A, B, C, D, & E CONSTRUCTION		00110	CLEARING & GRUBBING	1	LS	\$ 2,134,969
CA011R010, CD101R010, CD111R010, CD121R010, CA021R010, CA031R010, CB041R010, CB051R010, CC061R010, CC071R020, CC081R020, CD091R010, CA012R010, CD102R010, CD112R010, CD122R010, CE152R020, CA022R010, CA032R010, CB042R010, CB052R010, CC062R010, CC072R010, CC082R010, CD092R010, CA013R010, CE131R020, CE151R020, CE132R010, CE153R020	SEGMENT A, B, C, D, & E CONSTRUCTION	(F)	00120	REGULAR EXCAVATION	282,232	CY	\$ 4,571,811
SAME AS VDOT #00120	SEGMENT A, B, C, D, & E CONSTRUCTION	(F)	00150	EMBANKMENT	272,358	CY	\$ 4,408,532
CE131S040, CE131S030, CE131S020, CE131D010, CE131S050, CE131S010	SEGMENT E CONSTRUCTION		00520	NS BOX CULVERT	1	EA	\$ 840,951
CA011R050, CD101R050, CD111R050, CD121R050, CE131R060, CE151R060, CA021R050, CA031R050, CB041R050, CB051R050, CC061R050, CC071R060, CC081R060, CD091R050, CA012R050, CD102R050, CD112R050, CD122R050, CE132R050, CE152R060, CA022R050, CA032R050, CB042R050, CB052R050, CC062R050, CC072R050, CC082R050, CD092R050,	SEGMENT A, B, C, D, & E CONSTRUCTION		00588	UNDERDRAIN UD-4	82,475	LF	\$ 285,722
CAG001030, CBG001030, CCG001030, CDG001030, CEG001030	SEGMENT A, B, C, D, & E CONSTRUCTION		02111	NS CONSTRUCTION ENTRANCE	20	EA	\$ 1,060,435
CAG001030, CBG001030, CCG001030, CDG001030, CEG001030	SEGMENT A, B, C, D, & E CONSTRUCTION		02111	NS TEMP. SUPER SILT FENCE	18,000	LF	\$ 189,614
VARIOUS	CONSTRUCTION SERVICES		02111	NS EROSION CONTROL MAINTENANCE	1	LS	\$ 324,802
CAG001040, CBG001040, CCG001040, CDG001040, CEG001040	SEGMENT A, B, C, D, & E CONSTRUCTION		02111	NS GALV. STEEL WIRE ROPE	132,157	LF	\$ 270,376
CE152R020, CE131R020, CE151R020, CE132R00, CE153R020	SEGMENT E CONSTRUCTION	(F)	02111	NS DAM FILTER BLANKET	16,280	TN	\$ 554,058
CD101R020, CD111R020, CD121R020, CC061R020, CC071R030, CC081R030, CD091R020, CD102R020, CD112R020, CD122R020, CC062R020, CC072R020, CC082R020, CD092R020	SEGMENT C & D CONSTRUCTION		02111	NS FILTERRA STRUCTURE	8	EA	\$ 244,638
SAME AS VDOT #01156	SEGMENT A, B, C, D, & E CONSTRUCTION	(F)	09150	EROS. CONTR. STONE CL. I, EC-1	39,612	TN	\$ 366,957

Activity ID ¹	Work Package Description ²	Fuel (F) or Price (P) Adjustment	VDOT Item Number ³	VDOT Material Item Description ³	Quantity	Unit	Budgeted Cost (\$)
CA011R030, CD101R030, CD111R030, CD121R030, CE131R040, CE151R040, CA021R030, CA031R030, CB041R030, CB051R030, CC061R030, CC071R040, CC081R040, CD091R030, CA012R030, CD102R030, CD112R030, CD122R030, CE132R030, CE152R040, CA022R030, CA032R030, CB042R030, CB052R030, CC062R030, CC072R030, CC082R030, CD092R030, CA013R030, CE153R040, CA011R040, CD101R040, CD111R040, CD121R040, CE131R050, CE151R050, CA021R040, CA031R040, CB051R040, CC061R040, CC071R050, CC081R050, CD091R040, CA012R040, CD102R040, CD112R040, CD122R040, CE132R040, CE152R050, CA022R040, CA032R040, CB042R040, CB052R040, CC062R040, CC072R040, CC082R040, CD092R040, CA013R040, CE153R050	SEGMENT A, B, C, D, & E CONSTRUCTION	(F)	10013	CEM. STAB. AGGR. MATL. NO. 21A	95,790	TON	\$ 2,717,915
CA011R040, CD101R040, CD111R040, CD121R040, CE131R050, CE151R050, CA021R040, CA031R040, CB051R040, CC061R040, CC071R050, CC081R050, CD091R040, CA012R040, CD102R040, CD112R040, CD122R040, CE132R040, CE152R050, CA022R040, CA032R040, CB042R040, CB052R040, CC062R040, CC072R040, CC082R040, CD092R040, CA013R040, CE153R050	SEGMENT A, B, C, D, & E CONSTRUCTION		10062	ASPH-STAB. OPEN GRADED-MATERIAL	12,500	TON	\$ 683,007
SAME AS VDOT #10062	SEGMENT A, B, C, D, & E CONSTRUCTION	(F)	10113	AGGR. BASE MAT. TY. I NO. 21A OR 21B	24,546	TON	\$ 775,203
CD101R080, CD111R080, CD121R080, CE131R090, CE151R070, CA021R060, CA031R060, CB041R060, CB051R080, CC061R080, CC071R090, CC081R090, CD091R060, CD102R080, CD112R080, CD122R080, CE132R080, CE152R090, CA022R060, CA032R060, CB042R060, CB052R060, CC062R060, CC072R080, CC082R080, CD092R060, CA013R080, CE153R090, CA012R080, CA011R060	SEGMENT A, B, C, D, & E CONSTRUCTION	(F) & (P)	10610	ASPHALT CONCRETE TY. IM-19.0A	13,600	TON	\$ 893,742
SAME AS VDOT #10635	SEGMENT A, B, C, D, & E CONSTRUCTION	(F) & (P)	10636	ASPHALT CONCRETE TY. SM-9.5D	13,900	TON	\$ 995,346
SAME AS VDOT #10610	SEGMENT A, B, C, D, & E CONSTRUCTION	(F) & (P)	10642	ASPHALT CONCRETE TY. BM-25.0A	60,000	TON	\$ 3,342,594

Activity ID ¹	Work Package Description ²	Fuel (F) or Price (P) Adjustment	VDOT Item Number ³	VDOT Material Item Description ³	Quantity	Unit	Budgeted Cost (\$)
CD101R070, CD111R070, CD121R070, CE131R080, CB051R070, CC061R070, CC071R080, CC081R080, CA012R070, CD102R070, CD112R070, CD122R070, CE132R070, CE152R080, CC072R070, CC082R070, CA013R070, CE153R080, CD101R060, CD111R060, CD121R060, CE131R070, CB051R060, CC061R060, CC071R070, CC081R070, CA012R060, CD102R060, CD112R060, CD122R060, CE132R060, CE152R070, CC072R060, CC082R060,	SEGMENT A, B, C, D, & E CONSTRUCTION		12030	STD. CURB CG-3	30,550	LF	\$ 353,118
SAME AS VDOT #10710	SEGMENT A, B, C, D, & E CONSTRUCTION		12700	STD. COMB. CURB CG-7	19,795	LF	\$ 191,090
CA011R080, CE151R090, CD122R100, CE132R100, CE152R120, CB052R080, CC062R080, CC072R100, CE153R110	SEGMENT A, B, C, D, & E CONSTRUCTION		13320	GUARDRAIL GR-2	4,550	LF	\$ 32,338
CE132W130, CE131W330, CE131W430, CE132W120, CE131W320, CE131W420	SEGMENT E CONSTRUCTION		13555	NS RETAINING WALL	11,920	SF	\$ 1,352,341
CE132W110, CE131W210, CE131W310, CE131W410, CE131W510	SEGMENT E CONSTRUCTION	(F)	13565	RETAINING WALL EXCAVATION	10,010	CY	\$ 786,341
SAME AS VDOT #11070	SEGMENT A, B, C, D, & E CONSTRUCTION		14100	REMOVAL OF SIDEWALK	538	SY	\$ 15,801
SAME AS VDOT #11070	SEGMENT A, B, C, D, & E CONSTRUCTION		14120	REMOVAL OF COMB. CURB & GUTTER	10,774	LF	\$ 244,041
CDG002020	SEGMENT D CONSTRUCTION		22643	FENCE FE-CL	10,600	LF	\$ 72,404
CAG001010, CBG001010, CCG001010, CDG001010, CEG001010, CAG002010, CBG002010, CCG002010, CDG002010, CEG002010	SEGMENT A, B, C, D, & E CONSTRUCTION		24160	CONSTRUCTION SIGNS	7,000	SF	\$ 218,583
SAME AS VDOT #24160	SEGMENT A, B, C, D, & E CONSTRUCTION		24278	GROUP 2 CHANNELIZING DEVICES	300,000	DAY	\$ 362,087
SAME AS VDOT #24160	SEGMENT A, B, C, D, & E CONSTRUCTION		24297	TRAF.BARR.SER.CONC.DOUBLE FACE	4,320	LF	\$ 218,583
SAME AS VDOT #11070	SEGMENT A, B, C, D, & E CONSTRUCTION		24600	REMOVE GUARDRAIL	2,003	LF	\$ 9,995
SAME AS VDOT #11070	SEGMENT A, B, C, D, & E CONSTRUCTION		24602	REMOVE EX. FENCE	15,000	LF	\$ 99,535
VARIOUS	PROJECT SERVICES		25505	NS FIELD OFFICE TY. I	30	MO	\$ 76,578
VARIOUS	PROJECT SERVICES		25565	PROGRESS SCHEDULE BASELINE	1	LS	\$ 750,160
VARIOUS	PROJECT SERVICES		25567	PROGRESS SCHEDULE UPDATES	38	EA	\$ 574,145
GO4000000 thru GO4010160	Pre-construction Activities - Design		25591	DESIGN ENGINEERING	1	LS	\$ 15,459,519
VARIOUS	CONSTRUCTION SERVICES		25593	QUALITY ASSURANCE (QA)(CONSTRUCTION)	1	LS	\$ 1,045,465
VARIOUS	CONSTRUCTION SERVICES		25593	QUALITY CONTROL (QC)(CONSTRUCTION)	1	LS	\$ 1,320,065
CA011R070, CD101R100, CD111R100, CD121R100, CE131R110, CE151R080, CA021R080, CA031R080, CB041R080, CB051R100, CC061R100, CC071R110, CC081R110, CD091R080, CA012R100, CD102R090, CD112R090, CD122R090, CE132R090, CE152R110, CA022R070, CA032R070, CB042R070, CB052R070, CC062R070, CC072R090, CC082R090, CD092R070, CA013R090, CE153R100	SEGMENT A, B, C, D, & E CONSTRUCTION		27012	TOPSOIL CLASS A 2"	61	AC	\$ 163,279
SAME AS VDOT #27012	SEGMENT A, B, C, D, & E CONSTRUCTION		27326	SOIL STABILIZATION MAT EC-3 TYPE B	21,052	SY	\$ 611,594
SAME AS VDOT #27012	SEGMENT A, B, C, D, & E CONSTRUCTION		27410	CHECK DAM, ROCK TY. I	118	EA	\$ 244,041
VARIOUS	CONSTRUCTION SERVICES		27451	INLET PROTECTION, TYPE A	112	EA	\$ 108,853
VARIOUS	CONSTRUCTION SERVICES		27461	INLET PROTECTION, TYPE B	196	EA	\$ 244,041

Activity ID ¹	Work Package Description ²	Fuel (F) or Price (P) Adjustment	VDOT Item Number ³	VDOT Material Item Description ³	Quantity	Unit	Budgeted Cost (\$)
CAG001030, CBG001030, CCG001030, CDG001030, CEG001030	SEGMENT A, B, C, D, & E CONSTRUCTION		27505	TEMP. SILT FENCE	190,000	LF	\$ 983,185
CAG001040, CBG001040, CCG001040, CDG001040, CEG001040	SEGMENT A, B, C, D, & E CONSTRUCTION		27545	STORM WATER MAN. BASIN EXCAV.	84,586	CY	\$ 1,908,433
SAME AS VDOT #27550	SEGMENT A, B, C, D, & E CONSTRUCTION		27550	STORM WATER MAN. DRAIN. STR. SWM	78	LF	\$ 619,998
SAME AS VDOT #27550	SEGMENT A, B, C, D, & E CONSTRUCTION		27580	TEMP. SEDIMENT BASIN EXCAVATION	13,000	CY	\$ 677,696
CCG001020	SEGMENT C CONSTRUCTION		27600	CLOSE AND CAP EXISTING WELLS	2	EA	\$ 6,970
GO8000010 thru GO8000600	SEGMENT A, B, C, D, & E CONSTRUCTION		40012	DESIGN BUILD UTILITIES	1	LS	\$ 13,523,336
CAG001010, CBG001010, CCG001010, CDG001010, CEG001010, CAG002010, CBG002010, CCG002010, CDG002010, CEG002010	SEGMENT A, B, C, D, & E CONSTRUCTION		50006	ERADICATION OF PAVEMENT MARKING	35,000	LF	\$ 19,955
CAG001010, CBG001010, CCG001010, CDG001010, CEG001010, CAG002010, CBG002010, CCG002010, CDG002010, CEG002010	SEGMENT A, B, C, D, & E CONSTRUCTION		51950	TEMP. SIGNALIZATION	1	LS	\$ 145,761
CAG009030, CDG009030, CCG009030, CCG009040, CDG009040	SEGMENT A, C, & D CONSTRUCTION		52000	PERMANENT TRAFFIC SIGNALIZATION	1	LS	\$ 593,353
CAG009020, CBG009020, CCG009020, CDG009020, CEG009020	SEGMENT A, B, C, D, & E CONSTRUCTION		54032	TYPE B CLASS I PAVEMENT LINE MARKING 4"	5,430	LF	\$ 6,292
SAME AS VDOT #54032	SEGMENT A, B, C, D, & E CONSTRUCTION		54034	TYPE B CLASS I PAVEMENT LINE MARKING 6"	300	LF	\$ 629
SAME AS VDOT #54032	SEGMENT A, B, C, D, & E CONSTRUCTION		54042	TYPE B CLASS I PAVEMENT LINE MARKING 24"	6,350	LF	\$ 18,787
SAME AS VDOT #54032	SEGMENT A, B, C, D, & E CONSTRUCTION		54075	TYPE B CLASS VI PAVEMENT LINE MARKING 4"	139,600	LF	\$ 62,562
SAME AS VDOT #54032	SEGMENT A, B, C, D, & E CONSTRUCTION		54100	TYPE B CLASS VI CONTRAST PAVEMENT LINE MARKING 4"	1,500	LF	\$ 3,775
SAME AS VDOT #54032	SEGMENT A, B, C, D, & E CONSTRUCTION		54217	SNOW PLOW. RAISED PAVE. MARKER ASHP. CONC	1,120	EA	\$ 8,719
SAME AS VDOT #54032	SEGMENT A, B, C, D, & E CONSTRUCTION		54218	SNOW PLOW. RAISED PAVE. MARKER HYD. CONC	50	EA	\$ 989
SAME AS VDOT #54032	SEGMENT A, B, C, D, & E CONSTRUCTION		54300	PAVEMENT MESSAGE MARK. ELONGATED ARROW SINGLE	75	EA	\$ 18,787
SAME AS VDOT #54032	SEGMENT A, B, C, D, & E CONSTRUCTION		54310	PAVEMENT MESSAGE MARK. ELONGATED ARROW DOUBLE	282	EA	\$ 24,989
CAG001010, CBG001010, CCG001010, CDG001010, CEG001010, CAG002010, CBG002010, CCG002010, CDG002010, CEG002010	SEGMENT A, B, C, D, & E CONSTRUCTION		54552	CONSTR. PAVE. MARK. (TY. F, CL. II) 4"	366,928	LF	\$ 242,936
CE14B2C090, CE14B1C090, CE14B2C100, CE14B1C100	SEGMENT E CONSTRUCTION	(F)	60404	CONCRETE CLASS A4	891	CY	\$ 657,528
CE14B2C160, CE14B1C160, CE15B2C180, CE14B1C180	SEGMENT E CONSTRUCTION		60450	CONCRETE CLASS A4 BRIDGE APPR. SLAB	80	CY	\$ 16,568
SAME AS VDOT #60450	SEGMENT E CONSTRUCTION	(P)	60452	REINF. STEEL BRIDGE APPROACH SALB	13,200	LB	\$ 9,837
CE14B2C010, CE14B1C010, CE14B2C020, CE14B1C020	SEGMENT E CONSTRUCTION	(P)	61812	STR. STEEL PLATE GIRDER ASTM A709 GRADE 50W	1	LS	\$ 447,844
CE14B2C140, CE14B1C140	SEGMENT E CONSTRUCTION		62041	RAILING, BR27C, 1 RAIL	898	LF	\$ 64,717
CE14B2C140, CE14B1C140	SEGMENT E CONSTRUCTION		62043	RAILING, BR27C, 3 RAILS	296	LF	\$ 28,993
CE14B2C140, CE14B1C140	SEGMENT E CONSTRUCTION		62044	RAILING, BR27C, 4 RAILS	296	LF	\$ 29,511
CE151R050, CE152R050, CE153R050	SEGMENT E CONSTRUCTION		64005	SELECT MATERIAL TYPE-1 MIN CBR-30	20,960	TN	\$ 652,868
CE14B2BA00, CE14B1BA00, CE15B2BB00, CE15B1BB00, CE14B2BP10, CE14B1BP10	SEGMENT E CONSTRUCTION	(F)	64011	STRUCTURE EXCAVATION	9,500	CY	\$ 869,801
CE14B2C130, CE14B1C130, CE14B2BP70, CE14B1BP70, CE14B2BP50, CE14B1BP50, CE14B2C030, CE14B1C030, CE14B2C050, CE14B1C050, CE14B2BA20, CE14B1BA20, CE14B2BB20, CE14B1BB20, CE14B2BP30, CE14B1BP30, CE14B2BA40, CE14B1BA40, CE14B2BB40, CE14B1BB40	SEGMENT E CONSTRUCTION	(F)	65013	CONCRETE CLASS A3	1,916	CY	\$ 1,180,444
SAME AS VDOT #65013	SEGMENT E CONSTRUCTION	(P)	65200	REINFORCING STEEL	156,773	LB	\$ 296,664

Activity ID ¹	Work Package Description ²	Fuel (F) or Price (P) Adjustment	VDOT Item Number ³	VDOT Material Item Description ³	Quantity	Unit	Budgeted Cost (\$)
SAME AS VDOT #65013	SEGMENT E CONSTRUCTION	(P)	65211	CORROSION RESISTANT REINFORCING STEEL, CLASS I	132,030	LB	\$ 224,181
CE14B1BA70, CE14B2BA70, CE14B2BB70, CE14B1BB70	SEGMENT E CONSTRUCTION		66238	DRY RIPRAP CLASS II 38"	1,715	TN	\$ 125,293
CE14B2BA10, CE14B1BA10, CE14B2BB10, CE14B1BB10, CE14B2BP20, CE14B1BP20	SEGMENT E CONSTRUCTION		66924	MICROPILE	8,012	LF	\$ 573,136
VARIOUS	PROJECT SERVICES		85130	BOND COST	1	LS	\$ 1,830,666
CA011R020, CD101R020, CD111R020, CD121R020, CE131R030, CE151R030, CA021R020, CA031R020, CB041R020, CB051R020, CC061R020, CC071R030, CC081R030, CD091R020, CA012R020, CD102R020, CD112R020, CD122R020, CE132R020, CE152R030, CA022R020, CA032R020, CB042R020, CB052R020, CC062R020, CC072R020, CC082R020, CD092R020,	SEGMENT A, B, C, D, & E CONSTRUCTION		01156 thru 01726, 02222 thru 02292	STORM SEWER PIPE - VARIOUS SIZES	39,650	LF	\$ 4,945,043
SAME AS VDOT #01156	SEGMENT A, B, C, D, & E CONSTRUCTION		06151 thru 09057	STORM SEWER STRUCTURES	366	LF	\$ 2,263,366
CE132W130, CE131W330, CE131W430, CE132W120, CE131W320, CE131W420	SEGMENT E CONSTRUCTION		62041, 62043	RAILING, BR27C 1 RAIL, RETAINING WALLS	2,098	LF	\$ 304,130
CCG001050, CDG001050	SEGMENT A, B, C, D, & E CONSTRUCTION		ITS SP	ITS CONDUIT (PVC 1.25")	31,550	LF	\$ 70,023
CAG001050, CBG001050, CCG001050, CDG001050, CEG001050	SEGMENT A, B, C, D, & E CONSTRUCTION		ITS SP	ELECTRICAL CONDUIT (2")	31,550	LF	\$ 70,023
CC082R100, CAG001110, CBG001060	SEGMENT A, B, & C CONSTRUCTION		NS	AIRPORT SECURITY FENCE	12,500	LF	\$ 81,476
CE131D040, CE131D020	SEGMENT E CONSTRUCTION		NS	DAM RISER STRUCTURE	1	LS	\$ 51,209
CE131X010, CE131X100	SEGMENT E CONSTRUCTION		NS	SAMPLING BUILDING	1	LS	\$ 107,994
CC081S110, CC081S210, CC071S310	SEGMENT C CONSTRUCTION		NS	NOISE WALLS	5,500	SF	\$ 112,391
VARIOUS	PROJECT SERVICES		NS	NS ENVIRONMENTAL CREDITS	1	LS	\$ 2,220,000

¹ Activity ID should correspond to the Activity ID provided in the Offeror's Proposal Schedule.

² Work Package Description should correspond to the Work Package designation included in the Offeror's Proposal Schedule.

³ VDOT Item Number and Description should correspond to VDOT's Standard and Non-Standard Item Code Tables, as provided on VDOT's Construction (Scheduling and Contracts) webpage.

\$ 87,958,801

Attachment 4.8.2(b)
State Project 0606-053-093
SCHEDULE OF ITEMS Phase B

This schedule of items shall identify the material quantities and costs of each proposed work package, using the WBS established in the Proposal Schedule submitted by the Offeror. The material quantities and costs listed for each proposed work package shall, to the extent possible, correspond to VDOT's list of standard and non-standard pay items. Any items considered for price adjustments shall be identified. The value associated with each work task shall be inclusive of all direct and indirect costs, overhead, profit and any other expenses of any kind. The values and quantities shall be clearly supported by the escrowed pricing documents.

Activity ID ¹	Work Package Description ²	Fuel (F) or Price (P) Adjustment	Revised Bid Number (HIDE THIS)	VDOT Item Number ³	VDOT Material Item Description ³	Quantity	Unit	Budgeted Cost (\$)
VARIOUS	CONSTRUCTION SERVICES		14020	00100	MOBILIZATION (CONSTRUCTION)	1	LS	\$ 34,378
CA011R010, CD101R010, CD111R010, CD121R010, CA021R010, CA031R010, CB041R010, CB051R010, CC061R010, CC071R020, CC081R020, CD091R010, CE131R020, CE151R020	SEGMENT A, B, C, D, & E CONSTRUCTION	(F)	14110	00120	REGULAR EXCAVATION	12793	CY	\$ 220,000
SAME AS VDOT #00120	SEGMENT A, B, C, D, & E CONSTRUCTION	(F)	14120	00150	EMBANKMENT	24637	CY	\$ 211,200
CA011R050, CD101R050, CD111R050, CD121R050, CE131R060, CE151R060, CA021R050, CA031R050, CB041R050, CB051R050, CC061R050, CC071R060, CC081R060, CD091R050	SEGMENT A, B, C, D, & E CONSTRUCTION		15310	00700	POST INSTALLATION INSPECTION	345	LF	\$ 302
SAME AS VDOT #01156	SEGMENT A, B, C, D, & E CONSTRUCTION		15380	02111	NS BIORETENTION EXCAVATION	275	CY	\$ 1,475
SAME AS VDOT #01156	SEGMENT A, B, C, D, & E CONSTRUCTION		15390	02111	NS BIORETENTION SOIL MEDIA	206	CY	\$ 16,327
CD101R090, CD111R090, CD121R090, CE131R100, CA021R070, CA031R070, CB041R070, CB051R090, CC061R090, CC071R100, CC081R100, CD091R070	SEGMENT A, B, C, D, & E CONSTRUCTION		17410	10113	AGGR. BASE MAT. TY. I NO. 21A OR 21B	10938	TON	\$ 224,651
SAME AS VDOT #10113	SEGMENT A, B, C, D, & E CONSTRUCTION	(F) & (P)	17420	10635	ASPHALT CONCRETE TY. SM-9.5A	3315	TON	\$ 234,284
CD101R070, CD111R070, CD121R070, CE131R080, CB051R070, CC061R070, CC071R080, CC081R080, CD101R060, CD111R060, CD121R060, CE131R070, CB051R060, CC061R060, CC071R070, CC081R070	SEGMENT A, B, C, D, & E CONSTRUCTION		14510	13108	CG-12 DETECTABLE WARNING SURFACE	95	SY	\$ 4,502
CA011R080, CE151R090	SEGMENT A, B, C, D, & E CONSTRUCTION		14610	13315	GUARDRAIL TERMINAL GR-11	4	EA	\$ 1,090
SAME AS VDOT #13315	SEGMENT A, B, C, D, & E CONSTRUCTION		14600	13320	GUARDRAIL GR-2	1225	LF	\$ 9,579
SAME AS VDOT #13315	SEGMENT A, B, C, D, & E CONSTRUCTION		14620	13400	GUARDRAIL TERMINAL GR-12	4	EA	\$ 1,090
CE131W220, CE131W320, CE131W420, CE131W520, CE131W230, CE131W530, CE131W220, CE131W520	SEGMENT E CONSTRUCTION		17430	25000	HANDRAIL HR-1	2000	LF	\$ 227,879
GO4000000 thru GO4010160	Pre-construction Activities - Design		14011	25591	DESIGN ENGINEERING	1	LS	\$ 10,000
VARIOUS	CONSTRUCTION SERVICES		14050	25593	QUALITY ASSURANCE (QA)(CONSTRUCTION)	1	LS	\$ 25,000
VARIOUS	CONSTRUCTION SERVICES		14060	25593	QUALITY CONTROL (QC)(CONSTRUCTION)	1	LS	\$ 25,000
CA011R070, CD101R100, CD111R100, CD121R100, CE131R110, CE151R080, CA021R080, CA031R080, CB041R080, CB051R100, CC061R100, CC071R110, CC081R110, CD091R080	SEGMENT A, B, C, D, & E CONSTRUCTION		14130	27012	TOPSOIL CLASS A 2"	3	AC	\$ 8,800
SAME AS VDOT #27012	SEGMENT A, B, C, D, & E CONSTRUCTION		14700	27023	REGULAR SEED	3392	LB	\$ 13,149
SAME AS VDOT #27012	SEGMENT A, B, C, D, & E CONSTRUCTION		14710	27103	OVERSEEDING	2120	LB	\$ 5,646
SAME AS VDOT #27012	SEGMENT A, B, C, D, & E CONSTRUCTION		14730	27104	LEGUME SEED	256	LB	\$ 867
SAME AS VDOT #27012	SEGMENT A, B, C, D, & E CONSTRUCTION		14720	27105	LEGUME OVERSEEDING	160	LB	\$ 465
SAME AS VDOT #27012	SEGMENT A, B, C, D, & E CONSTRUCTION		14760	27210	FERTILIZER	5	TON	\$ 3,633
SAME AS VDOT #27012	SEGMENT A, B, C, D, & E CONSTRUCTION		14740	27250	LIME	72	TON	\$ 26,156

Activity ID ¹	Work Package Description ²	Fuel (F) or Price (P) Adjustment	Revised Bid Number (HIDE THIS)	VDOT Item Number ³	VDOT Material Item Description ³	Quantity	Unit	Budgeted Cost (\$)
SAME AS VDOT #27012	SEGMENT A, B, C, D, & E CONSTRUCTION		14750	27288	EROSION CONTROL MULCH	19	ACRE	\$ 15,334
GO8000010 thru GO8000600	SEGMENT A, B, C, D, & E CONSTRUCTION		16310	40012	DESIGN BUILD UTILITIES	1	LS	\$ 100,101
CAG009040, CBG009030, CCG009050, CDG009050, CEG009030	SEGMENT A, B, C, D, & E CONSTRUCTION		17010	50108	SIGN PANEL	160	SF	\$ 1,859
SAME AS VDOT #50108	SEGMENT A, B, C, D, & E CONSTRUCTION		17020	50432	SIGN POST STP-1, 2 3/16"	170	LF	\$ 1,264
SAME AS VDOT #50108	SEGMENT A, B, C, D, & E CONSTRUCTION		17030	50490	CONCRETE FOUNDATION STP-1	15	EA	\$ 1,045
CAG009020, CBG009020, CCG009020, CDG009020, CEG009020	SEGMENT A, B, C, D, & E CONSTRUCTION		17040	54034	TYPE B CLASS I PAVEMENT LINE MARKING 6"	3300	LF	\$ 3,450
SAME AS VDOT #54032	SEGMENT A, B, C, D, & E CONSTRUCTION		17050	54042	TYPE B CLASS I PAVEMENT LINE MARKING 24"	500	LF	\$ 1,742
CE14B1C090, CE14B1C100	SEGMENT E CONSTRUCTION		14910	60404	CONCRETE A4	118	CY	\$ 12,112
CE14B1C010, CE14B1C020	SEGMENT E CONSTRUCTION	(P)	14920	61812	STR STEEL PLATE GIRDER ASTM A709 GRADE 50	1	LS	\$ 164,524
CA011R020, CD101R020, CD111R020, CD121R020, CE131R030, CE151R030, CA021R020, CA031R020, CB041R020, CB051R020, CC061R020, CC071R030, CC081R030, CD091R020	SEGMENT A, B, C, D, & E CONSTRUCTION		15321	01156 thru 01726, 02222 thru 02292	STORM SEWER PIPE - VARIOUS SIZES	345	LF	\$ 56,896
CE132W120, CE131W220, CE131W320, CE131W420, CE131W520, CE131W230, CE131W530, CE131W220, CE131W520	SEGMENT E CONSTRUCTION		14930	NS	PED FENCE TYPE C	296	LF	\$ 35,177
VARIOUS	PROJECT SERVICES		17200	NS	MAINTENANCE OF TRAFFIC	1	LS	\$ 20,000

¹ Activity ID should correspond to the Activity ID provided in the Offeror's Proposal Schedule.

² Work Package Description should correspond to the Work Package designation included in the Offeror's Proposal Schedule.

³ VDOT Item Number and Description should correspond to VDOT's Standard and Non-Standard Item Code Tables, as provided on VDOT's Construction (Scheduling and Contracts) webpage.

\$ 1,718,976

4.8.3 Proposed Payment Schedules



Loudoun County, Virginia

Project No. 0606-053-983

Contract ID # C00097528DB64

PHASE A
MONTHLY PAYMENT SCHEDULE

Period Ending (Month)	Projected Monthly Total	Projected Cumulative Total
June 2014	\$ 4,900,000	\$ 4,900,000
July 2014	\$ 4,100,000	\$ 9,000,000
August 2014	\$ 1,900,000	\$ 10,900,000
September 2014	\$ 1,900,000	\$ 12,800,000
October 2014	\$ 1,200,000	\$ 14,000,000
November 2014	\$ 1,000,000	\$ 15,000,000
December 2014	\$ 1,000,000	\$ 16,000,000
January 2015	\$ 1,000,000	\$ 17,000,000
February 2015	\$ 1,000,000	\$ 18,000,000
March 2015	\$ 1,000,000	\$ 19,000,000
April 2015	\$ 1,000,000	\$ 20,000,000
May 2015	\$ 1,000,000	\$ 21,000,000
June 2015	\$ 3,600,000	\$ 24,600,000
July 2015	\$ 3,700,000	\$ 28,300,000
August 2015	\$ 3,800,000	\$ 32,100,000
September 2015	\$ 3,900,000	\$ 36,000,000
October 2015	\$ 3,000,000	\$ 39,000,000
November 2015	\$ 3,161,660	\$ 42,161,660
December 2015	\$ 2,800,000	\$ 44,961,660
January 2016	\$ 2,112,880	\$ 47,074,540
February 2016	\$ 2,175,129	\$ 49,249,669
March 2016	\$ 3,900,000	\$ 53,149,669
April 2016	\$ 3,900,000	\$ 57,049,669
May 2016	\$ 3,213,104	\$ 60,262,773
June 2016	\$ 3,169,907	\$ 63,432,680
July 2016	\$ 2,089,537	\$ 65,522,216
August 2016	\$ 2,089,537	\$ 67,611,753
September 2016	\$ 3,030,317	\$ 70,642,070
October 2016	\$ 2,658,564	\$ 73,300,634
November 2016	\$ 2,413,810	\$ 75,714,445
December 2016	\$ 3,117,533	\$ 78,831,977
January 2017	\$ 2,229,126	\$ 81,061,103
February 2017	\$ 960,880	\$ 82,021,984
March 2017	\$ 2,081,437	\$ 84,103,421
April 2017	\$ 2,081,437	\$ 86,184,859
May 2017	\$ 566,598	\$ 86,751,456
June 2017	\$ 512,601	\$ 87,264,057
July 2017	\$ 512,601	\$ 87,776,658
August 2017	\$ 158,488	\$ 87,935,146
September 2017	\$ 23,655	\$ 87,958,801

Loudoun County, Virginia

Project No. 0606-053-983

Contract ID # C00097528DB64

PHASE B
MONTHLY PAYMENT SCHEDULE

Period Ending (Month)	Projected Monthly Total	Projected Cumulative Total
June 2014	\$ 1,500	\$ 1,500
July 2014	\$ 1,500	\$ 3,000
August 2014	\$ 583	\$ 3,583
September 2014	\$ 583	\$ 4,167
October 2014	\$ 583	\$ 4,750
November 2014	\$ 583	\$ 5,333
December 2014	\$ 583	\$ 5,917
January 2015	\$ 583	\$ 6,500
February 2015	\$ 583	\$ 7,083
March 2015	\$ 583	\$ 7,667
April 2015	\$ 583	\$ 8,250
May 2015	\$ 583	\$ 8,833
June 2015	\$ 25,609	\$ 34,442
July 2015	\$ 25,609	\$ 60,050
August 2015	\$ 39,743	\$ 99,793
September 2015	\$ 37,743	\$ 137,537
October 2015	\$ 115,326	\$ 252,863
November 2015	\$ 82,308	\$ 335,171
December 2015	\$ 78,046	\$ 413,217
January 2016	\$ 78,046	\$ 491,263
February 2016	\$ 74,296	\$ 565,559
March 2016	\$ 82,447	\$ 648,006
April 2016	\$ 79,536	\$ 727,541
May 2016	\$ 79,536	\$ 807,077
June 2016	\$ 251,239	\$ 1,058,316
July 2016	\$ 161,563	\$ 1,219,880
August 2016	\$ 161,563	\$ 1,381,443
September 2016	\$ 136,059	\$ 1,517,502
October 2016	\$ 136,059	\$ 1,653,561
November 2016	\$ 7,282	\$ 1,660,843
December 2016	\$ 7,282	\$ 1,668,124
January 2017	\$ 7,282	\$ 1,675,406
February 2017	\$ 7,282	\$ 1,682,687
March 2017	\$ 9,622	\$ 1,692,309
April 2017	\$ 9,622	\$ 1,701,931
May 2017	\$ 8,842	\$ 1,710,773
June 2017	\$ 3,602	\$ 1,714,374
July 2017	\$ 3,602	\$ 1,717,976
August 2017	\$ 500	\$ 1,718,476
September 2017	\$ 500	\$ 1,718,976

4.8.4

Price Adjustments

EXHIBIT 6.3(a)
ADJUSTMENT FOR ASPHALT

SPECIAL PROVISION FOR
ASPHALT MATERIAL PRICE ADJUSTMENT
DESIGN-BUILD PROJECTS

August 9, 2013

All asphalt material listed in the attached “Master Listing of Asphalt Material Items Eligible for Price Adjustment” will be adjusted in accordance with the provisions as set forth herein. Other items will not be adjusted, except as otherwise specified in the contract. Any item added through a Work Order which contains Asphalt Material will not be subject to Price Adjustment unless specifically designated in the Work Order to be subject to Price Adjustment.

Each month, the Department will publish an average state-wide PG 64-22 f.o.b. price per ton developed from the average terminal prices provided to the Department from suppliers of asphalt cement to contractors doing work in Virginia. The Department will collect terminal prices from approximately 12 terminals each month. These prices will be received once each month from suppliers on or about the last weekday of the month. The high and low prices will be eliminated and the remaining values averaged to establish the average statewide price for the following month. That monthly state-wide average price will be posted on the Construction Division website on or about the first weekday of the following month.

This monthly statewide average price will be the Base Index for all contracts on which Price Proposals are received during the calendar month of its posting and will be the Current Index for all asphalt placed during the calendar month of its posting. In the event an index changes radically from the apparent trend, as determined by the Engineer, the Department may establish an index which is determined to best reflect the trend.

The amount of adjustment applied will be based on the difference between the Price Proposal\Contract Base Index and the Current Index for the applicable calendar month during which the work is performed. Calculations must be done for each type of Asphalt Material put in place each month, whether the Current Index is higher or lower than the Base Index. The calculation for the adjustment shall be shown as follows:

$$A = Q \times \%AC \times IC$$

Where: A = Asphalt Adjustment Dollar Amount

Q = Quantity of Asphalt Material put in place during the month

%AC = % of Asphalt Cement in the Asphalt Material as specified in the Job Mix Formula

IC = Numeric Dollar Difference, either positive or negative, between the Base Index and Current Index

Example Calculation for Negative Price Adjustment (Credit back to VDOT):

7,500 Tons of SM-12.5A put in place during the month (Q), Job Mix is 6.1% Asphalt Cement for SM-12.5A (%AC), Base Index for the Contract is \$515/Ton, Current Index is \$500/Ton, Difference of - \$15.00/Ton (IC)

$$7,500 \text{ Tons SM-12.5A} \times 6.1\% \times - \$15.00/\text{Ton} = - \$6,862.50 \text{ Adjustment Amount}$$

Example Calculation for Positive Price Adjustment (Paid to the Design-Builder):

10,000 Tons of BM-25.0A put in place during the month (Q), Job Mix is 5.2% Asphalt Cement for BM-25.0A (%AC), Base Index for the Contract is \$515/Ton, Current Index is \$560/Ton, Difference of + \$45.00/Ton (IC)

$$10,000 \text{ Tons BM-25.0A} \times 5.2\% \times \$45.00/\text{Ton} = + \$23,400.00 \text{ Adjustment Amount}$$

Adjustment of any asphalt material item designated as a price adjustment item which does not contain PG 64-22, except PG 76-22 or PG 70-28, will be based on the indexes for PG 64-22. The quantity of asphalt cement for asphalt concrete pavement to which adjustment will be applied will be the quantity based on the percent of asphalt cement shown on the appropriate approved job mix formula.

The quantity of asphalt emulsion for surface treatments to which adjustment will be applied will be the quantity based on 65 percent residual asphalt.

Price adjustment will be shown as a separate entry on the monthly application of payment for work packages completed; however, such adjustment will not be included in the total cost of the work for progress determination or for extension of contract time. Items the Design-Builder claims in its application of payment for asphalt adjustments must include supporting calculations certified by the Quality Assurance Manager (QAM). These calculations must be completed relative to the calendar month under which the work was performed and shall be submitted for either positive or negative adjustment.

Any apparent attempt to unbalance bids in favor of items subject to price adjustment or failure to submit required cost and price data as noted hereinbefore may result in rejection of items for asphalt adjustment.

VIRGINIA DEPARTMENT OF TRANSPORTATION
MASTER LISTING OF
ASPHALT MATERIAL ITEMS ELIGIBLE FOR PRICE ADJUSTMENT
(10-27-09)

ITEM	DESCRIPTION	UNITS	SPECIFICATION
10062	Asphalt-Stab. Open-Graded Material	Ton	313
10416	Liquid Asphalt	Gal	311 312
10420	Blotted Seal Coat Ty. B	Sy	ATTD
10422	Blotted Seal Coat Ty. C	Sy	ATTD
10423	Blotted Seal Coat Ty. C-1	Sy	ATTD
10424	Blotted Seal Coat Ty. D	Sy	ATTD
10598	Ns Asphalt Concrete	Ton	315
10606	Asphalt Concrete Ty. SM-9.5	Ton	315
10607	Asphalt Concrete Ty. SM-12.5A	Ton	315
10608	Asphalt Concrete Ty. SM-12.5D	Ton	315
10609	Asphalt Concrete Ty. SM-12.5E (76-22)	Ton	315
10610	Asphalt Concrete Ty. IM-19.0A	Ton	315
10611	Asphalt Concrete Ty. IM-19.0D	Ton	315
10612	Asphalt Conc. Base Cr. Ty. BM-25.0	Ton	315
10613	Asphalt Concrete Ty. BM-37.5	Ton	315
10635	Asphalt Concrete Ty. SM-9.5A	Ton	315
10636	Asphalt Concrete Ty. SM-9.5D	Ton	315
10637	Asphalt Concrete Ty. SM-9.5E (76-22)	Ton	315
10639	Asphalt Concrete Ty. SM-19.0	Ton	315
10642	Asphalt Concrete Ty. BM-25.0A	Ton	315
10643	Asphalt Concrete Ty. BM-25.0D	Ton	315
10650	Stone Matrix Asphalt SMA-9.5(70-22)	Ton	317
10651	Stone Matrix Asphalt SMA-9.5(76-22)	Ton	317
10652	Stone Matrix Asphalt SMA-12.5(70-22)	Ton	317
10653	Stone Matrix Asphalt SMA-12.5(76-22)	Ton	317
10654	Stone Matrix Asphalt SMA-19.0(70-22)	Ton	317
10655	Stone Matrix Asphalt SMA-19.0(76-22)	Ton	317
10701	Liquid Asphalt Coating	Sy	ATTD
12505	Asphalt Concrete Curb Backup Material	Ton	315
13240	Asphalt Concrete Sidewalk	Ton	504
16110	Emul. Asph. Slurry Seal Type A	Sy	ATTD
16120	Emul. Asph. Slurry Seal Type B	Sy	ATTD
16130	Emul. Asph. Slurry Seal Type C	Sy	ATTD
16144	Latex Mod. Emul. Treat. Type B	Ton	ATTD
16145	Latex Mod. Emul. Treat. Type C	Ton	ATTD
16146	Latex Mod. Emul. Treat. Rutfilling	Ton	ATTD
16161	Modified Single Seal	Sy	ATTD
16162	Modified Double Seal	Sy	ATTD
16249	Nontracking Tack Coat	Gal.	ATTD
16250	Liquid Asphalt Matl. CMS-2 (Mod)	Gal	ATTD
16251	Liquid Asphalt Matl. CMS-2	Gal	ATTD
16252	Liquid Asphalt Matl. CRS-2	Gal	ATTD
16253	Liquid Asphalt Matl. CRS-2H	Gal.	ATTD.
16254	Liquid Asphalt Matl. RC-250	Gal	ATTD
16256	Liquid Asphalt Matl. RC-800	Gal	ATTD
16257	Ns Liquid Asphalt Matl.	Gal	ATTD
16260	Liquid Asphalt Matl. CRS-2L	Gal	ATTD
16325	NS Asphalt Concrete	Ton	N/A

16330	Asphalt Concrete Ty. SM-9.0A	Ton	315
16335	Asphalt Concrete Ty. SM-9.5A	Ton	315
16337	Asph. Conc. Ty. SM-9.5ASL (Spot Level)	Ton	315
16340	Asphalt Concrete Ty. SM-9.5D	Ton	315
16342	Asph. Conc. Ty. SM-9.5DSL (Spot Level)	Ton	315
16345	Asphalt Concrete Ty. SM-9.5E (76-22)	Ton	315
16350	Asphalt Concrete Ty. SM-12.5A	Ton	315
16352	Asph. Con. Ty. SM-12.5ASL (Spot Level)	Ton	315
16355	Asphalt Concrete Ty. SM-12.5D	Ton	315
16357	Asph. Con. Ty. SM-12.5DSL (Spot Level)	Ton	315
16360	Asphalt Concrete Ty. SM-12.5E (76-22)	Ton	315
16365	Asphalt Concrete Ty. IM-19.0A	Ton	315
16370	Asphalt Concrete Ty. IM-19.0D	Ton	315
16373	Asphalt Concrete Ty. IM-19.0A (T)	Ton	315
16374	Asphalt Concrete Ty. IM-19.0D (T)	Ton	315
16377	Asphalt Concrete Ty. BM-37.5	Ton	315
16379	Asphalt Concrete Ty. IM-19.0T	Ton	315
16390	Asphalt Concrete Ty. BM-25.0A	Ton	315
16392	Asphalt Concrete Ty. BM-25.0D	Ton	315
16395	Asphalt Concrete Ty. BM-25.0A (T)	Ton	315
16397	Asphalt Concrete Ty. BM-25.0D (T)	Ton	315
16400	Stone Matrix Asphalt SMA-9.5(70-22)	Ton	ATTD
16401	Stone Matrix Asphalt SMA-9.5(76-22)	Ton	ATTD
16402	Stone Matrix Asphalt SMA-12.5(70-22)	Ton	ATTD
16403	Stone Matrix Asphalt SMA-12.5(76-22)	Ton	ATTD
16404	Stone Matrix Asphalt SMA-19.0(70-22)	Ton	ATTD
16405	Stone Matrix Asphalt SMA-19.0(76-22)	Ton	ATTD
16490	Hot Mix Asphalt Treatment	Ton	ATTD
16500	Surf.Preparation & Restoration Type I	Ton	ATTD
16502	Surf.Preparation & Restoration Type li	Ton	ATTD
16504	Surf.Preparation & Restoration Type lii	Ton	ATTD
67201	NS Asphalt Concrete Overlay	Ton	315
67210	NS Asphalt Concrete	Ton	315
68240	NS Asphalt Concrete	Ton	315

**EXHIBIT 6.3 (c)
ADJUSTMENT FOR FUEL**

**VIRGINIA DEPARTMENT OF TRANSPORTATION
SPECIAL PROVISION FOR
OPTIONAL ADJUSTMENT FOR FUEL
DESIGN-BUILD PROJECTS**

June 30, 2011
(Revised) November 5, 2012

In the event the Design-Builder elects to seek adjustment for fuel items designated in the Price Proposal/Contract as Price Adjustment Items such items will be subject to price adjustment as set forth herein. Other items will not be adjusted, except as otherwise specified in the contract.

The Design-Builder will submit their monthly application for payment associated with eligible work packages with an adjustment up or down as appropriate for cost changes in fuel used on specific items of work identified in this provision. A master listing of standard items eligible for fuel adjustment is provided by the Department on its website at the following link <http://www.virginiadot.org/business/resources/masteroptionalfuelitems.pdf>. The listing on the web site also includes the corresponding fuel factor for each item. The fuel usage factor for each item is considered inclusive of all fuel usage.

The amount of adjustment will be computed from the change in the indexes and the on-site fuel use as shown in the Department's master listing of eligible items.

In order to be eligible for fuel adjustment under this provision, the Design-Builder shall clearly identify in within the Schedule of Values those pay items and the associated quantities it chooses to have fuel adjustment applied to in its work packages. Items the Design-Builder claims in its application of payment for fuel adjustments must be properly designated in order to be considered for adjustment. Items not properly designated or left out of the Design-Builder's Schedule of Values will automatically not be considered for adjustment.

The monthly index price to be used in the administration of this provision will be calculated by the Department from the Diesel fuel prices published by the U. S. Department of Energy, Energy Information Administration on highway diesel prices, for the Lower Atlantic region. The monthly index price will be the price for diesel fuel calculated by averaging each of the weekly posted prices for that particular month.

For the purposes of this provision, the base index price will be calculated using the data from the month preceding the receipt of bids. The base index price will be posted by the Department at the beginning of the month for all bids received during that month.

The current index price will be posted by the Department and will be calculated using the data from the month preceding the particular estimate being vouchered for payment.

The current monthly quantity for eligible items of work selected by the Design-Builder for fuel adjustment in its work packages will be multiplied by the appropriate fuel factor to determine the gallons of fuel to be cost adjusted. The amount of adjustment per gallon will be the net difference between the current index price and the base index price. Computation for adjustment will be made as follows:

$$S = (E - B) QF$$

Where; S = Monetary amount of the adjustment (plus or minus)
B = Base index price

E = Current index price
Q = Quantity of individual units of work
F = Appropriate fuel factor

Adjustments will not be made for work performed beyond the original contract time limit unless the original time limit has been changed by an executed Work Order.

If new pay items are added to this contract by Work Order and they are listed in the Department's master listing of eligible items, the Work Order must indicate which of these individual items will be fuel adjusted; otherwise, those items will not be fuel adjusted. If applicable, designating which new pay items will be added for fuel adjustment must be determined during development of the Work Order and clearly shown on the Work Order form. The Base Index price on any new eligible pay items added by Work Order will be the Base Index price posted for the month in which bids were received for that particular project. The Current Index price for any new eligible pay items added by Work Order will be the Index price posted for the month preceding the estimate on which the Work Order is paid.

When quantities differ between the last monthly application of payment prepared upon final acceptance and the final application of payment, adjustment will be made using the appropriate current index for the period in which that specific item of work was last performed.

In the event any of the base fuel prices in this contract increase more than 100 percent (i.e. fuel prices double), the Department will review each affected item of work and give the Design-Builder written notice if work is to stop on any affected item of work. The Department reserves the right to reduce, eliminate or renegotiate the price for remaining portions of affected items of work.

Any amounts resulting from fuel adjustment will not be included in the total cost of work for determination of progress or for extension of contract time.

I elect to use this provision

I elect not to use this provision

Date: 04/21/14

Signature: 

Aaron T. Myers, VP/GM

Design-builder: American Infrastructure-VA, Inc.

Vendor No.: G303

EXHIBIT 6.3(d)
ADJUSTMENT FOR STEEL

VIRGINIA DEPARTMENT OF TRANSPORTATION
SPECIAL PROVISION FOR
PRICE ADJUSTMENT FOR STEEL
DESIGN-BUILD PROJECTS

June 30, 2011

In the event the Design-Builder elects to seek adjustment for steel items designated in the Price Proposal/Contract as Price Adjustment Items such items will be subject to price adjustment as set forth herein. If new pay items which involve steel are established by Work Order, they will not be subject to Price Adjustment unless specifically designated in the Work Order to be subject to Price Adjustment.

The Design-Builder will submit their monthly application for payment associated with eligible work packages with an adjustment up or down as appropriate for cost changes in steel used on specific items of work identified in the Price Proposal/contract in accordance with this provision. Provided at the end of this provision is a master listing of standard bid items the Department has determined are eligible for steel price adjustment. Inventoried materials from the listing of eligible items are specifically excluded for consideration. In addition, concrete items where reinforcing steel is normally included in the unit bid price for the item such as (but not limited to) drop inlets, median barriers, sound barrier walls, bridge railing and parapets, are not eligible for consideration under this provision.

The requirements of this provision shall apply only to material cost changes that occur between the date of the opening of the Price Proposal and the date the material is shipped to the fabricator. To be eligible for this price adjustment, Design-Builder is required to fill out the accompanying Form for Price Adjustment for Eligible Steel Items on Design-Build Projects and submit the same with its Price Proposal for the Project. By signing the Form and submitting it with its Price Proposal Design-Builder declares its intention to participate in the price adjustment in its contract with the Department. For the purposes of this provision, the prices listed on the Form for Price Adjustment for Eligible Steel Items on Design-Build projects are fixed for cost and adjustment calculations regardless of quantities incorporated into final design. Further, in order for steel items to be eligible for adjustment, once shipped to the fabricator, the items shall be specifically stored, labeled, or tagged, recognizable by color marking, and identifiable by project for inspection and audit verification.

Design-Builder shall upon request furnish documentation supporting the price per pound for eligible steel items as shown on the Form for Price Adjustment for Eligible Steel Items on Design-Build Projects furnished with its Price Proposal. Design-Builder must use the format as shown with this Form; no other format for presenting this information will be permitted. Design-Builder shall certify that all items of documentation are original and were used in the computation of the price per pound amount for the represented eligible pay items for the month the Price Proposal was opened. This documentation shall support the base line material price ("Base Price") of the steel item only. Base price per pound shall not include the following cost components: fabrication, shipping, storage, handling, and erection.

Failure to submit all documentation required or requested supporting the per pound prices on eligible steel items will result in Design-Builder being ineligible for a price adjustment of any or all steel items.

Price adjustment of each qualifying item under consideration will be subject to the following condition:

There is an increase or decrease in the cost of eligible steel materials in excess of 10 percent up to a maximum of 60 percent from the Base Price when compared with the latest published price index ("Price Index") in effect at the time material is shipped to the fabricator.

The Price Index the Department is using is based on The U.S. Department of Labor, Bureau of Labor Statistics, Producers Price Index (PPI) which measures the average price change over time of the specific steel eligible item from the perspective of the seller of goods. The Master List table provided at the end of this provision indicates the Producers Price Index (PPI) steel category index items and the corresponding I.D. numbers to which VDOT items will be compared. **Please note:** The Producers Price Index (PPI) is subject to revision 4 months after original publication, therefore, price adjustments and payments will not be made until the index numbers are finalized.

The price adjustment will be determined by computing the percentage of change in index value beyond 10 percent above or below the index on the date of opening of Design-Builder's Price Proposal to the index value on the date the steel material is shipped to the fabricator (Please see included sample examples). Weights and date of shipment must be documented by a bill of lading provided to the Department. The final price adjustment dollar value will be determined by multiplying this percent increase or decrease in the index (after 10%) by the represented quantity of steel shipped, by the Base Price per pound subject to the limitations herein.

Price increase/decrease will be computed as follows:

$$A = B \times P \times Q$$

- Where;
- A = Steel price adjustment in lump sum dollars
 - B = Average weighted price of steel submitted in Design-Builder's Price Proposal for project in price per pound as listed on the Form for Price Adjustment for Eligible Steel Items on Design-Build Project
 - P = Adjusted percentage change in PPI average from shipping date to date of opening of Price Proposal minus 10% (0.10) threshold
 - Q = Total quantity of steel in pounds shipped to fabricator for specific project

The need for application of the adjustments herein to extra work will be determined by the Engineer on an individual basis and, if appropriate, will be specified on the Work Order.

This price adjustment is capped at 60 percent. This means the maximum "P" value for increase or decrease that can be used in the above equation is 50% (60%-10% threshold).

Calculations for price adjustment shall be shown separate from the monthly progress payment for work packages and will not be included in the total cost of work for determination of progress or for extension of contract time.

Upon Department review and due process consideration for redress by Design-Builder, any apparent evidence to unbalance the price supplied by Design-Builder in favor of items subject to price adjustment will result in ineligibility for Department participation under this provision.

Sample Calculation of a Price Adjustment (increase)

Project bid on April 28, 2004.

Project has 450,000 lb. of eligible structural steel.

Design Builder's *f.o.b. supplier price for structural steel submitted in the Price Proposal is \$0.2816 per pound. *free on board

Adjusted** BLS Producers Price Index (PPI) most recently published average at time of opening of the Price Proposal is 139.6.

All eligible steel shipped to fabricator in same month, October 2004.

Adjusted BLS Producers Price Index (PPI) most recently published average for month of October is 161.1

Adjustment formula is as follows:

$$A = B \times P \times Q$$

- Where;
- A = Steel price adjustment in lump sum dollars
 - B = Average weighted price of steel submitted in the Price Proposal for Design-Build project in \$ per pound
 - P = Adjusted percentage change in PPI average from shipping date to date of submitted Price Proposal minus 10% (0.10) threshold
 - Q = Total quantity of eligible steel shipped to fabricator in October 2004 for this project in pounds

$$B = \$0.2816$$

$$P = (161.1 - 139.6) / 139.6 - 0.10 = 0.054$$

$$Q = 450,000 \text{ lb.}$$

$$A = 0.2816 \times 0.054 \times 450,000$$

$$A = \$6,842.88 \text{ pay adjustment to Design-Builder}$$

Sample Calculation of a Price Adjustment (decrease)

Project bid on April 28, 2004.

Project has 450,000 lb. of eligible structural steel.

Design-Builder's *f.o.b. supplier price for structural steel submitted in the Price Proposal is \$0.2816 per pound. *free on board

Adjusted BLS Producers Price Index (PPI) most recently published average at time of opening of the Price Proposal is 156.6.

All eligible steel shipped to fabricator in same month, October 2004.

Adjusted BLS Producers Price Index (PPI) most recently published average for month of October is 136.3

Adjustment formula is as follows:

$$A = B \times P \times Q$$

- Where;
- A = Steel price adjustment in lump sum dollars
 - B = Average weighted price of steel submitted in the Price Proposal for Design-Build project in \$ per pound
 - P = Adjusted percentage change in PPI average from shipping date to date of submitted Price Proposal minus 10% (0.10) threshold
 - Q = Total quantity of eligible steel shipped to fabricator in October 2004 for this project in pounds

$$B = \$0.2816$$

$$P = (156.6 - 136.3)/156.6 - 0.10 = 0.030$$

$$Q = 450,000 \text{ lb.}$$

$$A = 0.2816 \times 0.030 \times 450,000$$

$$A = \$3,801.60 \text{ credit to Department}$$

MASTER LISTING

STANDARD BID ITEMS ELIGIBLE FOR STEEL PRICE ADJUSTMENT

March 18, 2009

BLS Series I. D.

ITEM NUMBER	ITEM DESCRIPTION	UNITS	Number WPU used in \$ adjust.
00519	SHEET PILE, STEEL	SF	avg. 1017 & 101
00540	REINF. STEEL	LB	101704
00542	EPOXY COATED REINF. STEEL	LB	101704
00560	STRUCTURAL STEEL JB-1	LB	avg. 1017 & 101
11030	REINF. STEEL BRIDGE APPR. SLAB	LB	101704
11181	PATCH.HYDR.CEM.CONC. PAVE.	SY	101704
13290	GUARDRAIL GR-8 (NCHRP 350 TL-3)	LF	avg. 1017 & 101
13292	GUARDRAIL GR-8A (NCHRP 350 TL-3)	LF	avg. 1017 & 101
13294	GUARDRAIL GR-8B (NCHRP 350 TL-3)	LF	avg. 1017 & 101
13310	GUARDRAIL TERMINAL GR-6 (NCHRP 350)	LF	avg. 1017 & 101
13320	GUARDRAIL GR-2	LF	avg. 1017 & 101
13323	GUARDRAIL GR-2A	LF	avg. 1017 & 101
13331	RAD. GUARDRAIL GR-2	LF	avg. 1017 & 101
13333	RAD. GUARDRAIL GR-2A	LF	avg. 1017 & 101
13335	GUARDRAIL GR-3	LF	avg. 1017 & 101
13341	GUARDRAIL TER. GR-6(WEATHERING STEEL	LF	avg. 1017 & 101
13351	GUARDRAIL GR-8	LF	avg. 1017 & 101
13352	GUARDRAIL GR-8A	LF	avg. 1017 & 101
13353	GUARDRAIL GR-8B	LF	avg. 1017 & 101
13355	GUARDRAIL GR-10	LF	avg. 1017 & 101
13421	MEDIAN BARRIER MB-3	LF	avg. 1017 & 101
13450	MEDIAN BARRIER MB-5	LF	avg. 1017 & 101
13451	MEDIAN BARRIER MB-5A	LF	avg. 1017 & 101
13452	MEDIAN BARRIER MB-5B	LF	avg. 1017 & 101
13545	REINF. STEEL	LB	101704
14502	REINFORCING STEEL	LB	101704
15290	PATCH.CEM.CONC.PAVE.TY.CRCP-A	SY	101704
15302	PATCH.CEM.CONC.PAVE. TY. II	SY	101704
15305	PATCH.CEM.CONC.PAVE.TY. IV-A	SY	101704
17323	GUARDRAIL BEAM *	LF	avg. 1017 & 101
17325	RADIAL GUARDRAIL BEAM *	LF	avg. 1017 & 101
17327	RUB RAIL	LF	avg. 1017 & 101
17353	CABLE GR-3	LF	avg. 1017 & 101
17521	GUARDRAIL BEAM (WEATHERING STEEL)	LF	avg. 1017 & 101
17523	RADIAL GUARDRAIL BEAM (WEATHERING STEEL)	LF	avg. 1017 & 101
17525	RUB RAIL (WEATHERING STEEL)	LF	avg. 1017 & 101
22501	FENCE FE-W1	LF	avg. 1017 & 101
22643	FENCE FE-CL	LF	avg. 1017 & 101
22645	FENCE FE-CL VINYL COATED	LF	avg. 1017 & 101
23043	WATER GATE FE-4 TY.III	LF	avg. 1017 & 101
23501	FENCE FE-W1 (FABRIC ONLY)	LF	avg. 1017 & 101
45522	4" STEEL ENCASE. PIPE	LF	101706
45532	6" STEEL ENCASE. PIPE	LF	101706
45562	16" STEEL ENCASE. PIPE	LF	101706

45572	18" STEEL ENCASE. PIPE	LF	101706
45582	24" STEEL ENCASE. PIPE	LF	101706
45584	24" JACKED STEEL ENCASEMENT PIPE	LF	101706
45592	30" STEEL ENCASE. PIPE	LF	101706
50402	SIGN POST STEEL 3"	LF	101706
50404	SIGN POST STEEL 4"	LF	101706
50406	SIGN POST STEEL 6"	LF	101706
50410	SIGN POST STEEL 10"	LF	101706
50412	SIGN POST STEEL 12"	LF	101706
50414	SIGN POST STEEL 14"	LF	101706
50416	SIGN POST STEEL 16"	LF	101706
50418	SIGN POST STEEL 18"	LF	101706
51317	SIG. POLE MP-1 20' ONE ARM 30'	EA	101706
51319	SIG. POLE MP-1 20' ONE ARM 32'	EA	101706
51325	SIG. POLE MP-1 20' ONE ARM 38'	EA	101706
51327	SIG. POLE MP-1 20' ONE ARM 40'	EA	101706
51329	SIG. POLE MP-1 20' ONE ARM 42'	EA	101706
51331	SIG. POLE MP-1 20' ONE ARM 44'	EA	101706
51337	SIG. POLE MP-1 20' ONE ARM 50'	EA	101706
51339	SIG. POLE MP-1 20' ONE ARM 52'	EA	101706
51341	SIG. POLE MP-1 20' ONE ARM 54'	EA	101706
51344	SIG. POLE MP-1 20' ONE ARM 56'	EA	101706
51346	SIG. POLE MP-1 20' ONE ARM 58'	EA	101706
51347	SIG. POLE MP-1 20' ONE ARM 60'	EA	101706
51348	SIG. POLE MP-1 20' ONE ARM 62'	EA	101706
51368	SIG.POLE MP-1 20'TWO ARMS 36'& 42'	EA	101706
51400	SIG.POLE MP-1 CO.LU.ONE ARM 38	EA	101706
51402	SIG.POLE MP-1 CO.LU.ONE ARM 40	EA	101706
51408	SIG.POLE MP-1 CO.LU.ONE ARM 46	EA	101706
51412	SIG.POLE MP-1 CO.LU.ONE ARM 50	EA	101706
51414	SIG.POLE MP-1 CO.LU.ONE ARM 52	EA	101706
51416	SIG.POLE MP-1 CO.LU.ONE ARM 54	EA	101706
51418	SIG.POLE MP-1 CO.LU.ONE ARM 56	EA	101706
51420	SIG.POLE MP-1 CO.LU.ONE ARM 58	EA	101706
51422	SIG.POLE MP-1 CO.LU.ONE ARM 60	EA	101706
55162	LIGHTING POLE LP-1 30'-4'	EA	101706
55163	LIGHTING POLE LP-1 30'-6'	EA	101706
55166	LIGHTING POLE LP-1 30'-12'	EA	101706
55169	LIGHTING POLE LP-1 35'-6'	EA	101706
55171	LIGHTING POLE LP-1 35'-10'	EA	101706
55176	LIGHTING POLE LP-1 40'-8'	EA	101706
55185	LIGHTING POLE LP-2 TYPE A	EA	101706
55186	LIGHTING POLE LP-2 TYPE B	EA	101706
55187	LIGHTING POLE LP-2 TYPE C	EA	101706
55188	LIGHTING POLE LP-2 TYPE D	EA	101706
55189	LIGHTING POLE LP-2 TYPE E	EA	101706
55190	LIGHTING POLE LP-2 TYPE F	EA	101706
55192	LIGHTING POLE LP-2 TYPE H	EA	101706
60452	REINF. STEEL BRIDGE APPR. SLAB	LB	101704
61700	REINF. STEEL	LB	101704
61704	CORROSION RESISTANT REINF. STEEL	LB	101704
61705	EPOXY COATED REINF. STEEL	LB	101704
61750	STRUCT.STEEL HIGH STRG.PLT.GIRDERS	LB	avg. 1017 & 101
61811	STR.STEEL PLATE GIRDER ASTM A709 GRADE50	LB	avg. 1017 & 101
61812	STR.STEEL PLATE GIRDER ASTM A709 GRADE50	LB	avg. 1017 & 101
61813	STR.STEEL PLATE GIRDER ASTM A709 GRADEHPS50W	LB	avg. 1017 & 101

61814	STR.STEEL PLATE GIRDER ASTM A709 GRADEHPS70W	LB	avg. 1017 & 101
61820	STR.STEEL ROLLED BEAM ASTM A709 GRADE 36	LB	avg. 1017 & 101
61821	STR.STEEL ROLLED BEAM ASTM A709 GRADE50	LB	avg. 1017 & 101
61822	STR.STEEL ROLLED BEAM ASTM A709 GRADE50W	LB	avg. 1017 & 101
61990	STEEL GRID FLOOR	SF	avg. 1017 & 101
64110	STEEL PILES 10"	LF	avg. 1017 & 101
64112	STEEL PILES 12"	LF	avg. 1017 & 101
64114	STEEL PILES 14"	LF	avg. 1017 & 101
64768	DRIVING TEST FOR 12" STEEL PILE	LF	avg. 1017 & 101
64778	DRIVING TEST FOR 14" STEEL PILE	LF	avg. 1017 & 101
65200	REINF. STEEL	LB	101704
65204	CORROSION RESISTANT REINF. STEEL	LB	101704
65205	EPOXY COATED REINF. STEEL	LB	101704
67086	PED. FENCE 6'	LF	avg. 1017 & 101
67088	PED. FENCE 8'	LF	avg. 1017 & 101
67089	PED. FENCE 10'	LF	avg. 1017 & 101
68100	REINF. STEEL	LB	101704
68104	CORROSION RESISTANT REINF. STEEL	LB	101704
68105	EPOXY COATED REINF. STEEL	LB	101704
68107	STR.STEEL PLATE GIRDER ASTM A709 GRADE50	LB	avg. 1017 & 101
68108	STR. STEEL PLATE GIRDER ASTM A709 GR50W	LB	avg. 1017 & 101
68109	STR. STEEL PLATE GIRDER ASTM A709 GR.HPS50W	LB	avg. 1017 & 101
68110	STR. STEEL PLATE GIRDER ASTM A709 GR.HPS70W	LB	avg. 1017 & 101
68112	STR.STEEL ROLLED BEAM ASTM A709 GR.36	LB	avg. 1017 & 101
68113	STR.STEEL ROLLED BEAM ASTM A709 GR.50	LB	avg. 1017 & 101
68114	STR.STEEL ROLLED BEAM ASTM A709 GR. 50W	LB	avg. 1017 & 101
68115	STRUCT. STEEL	LB	avg. 1017 & 101
68270	REINF. STEEL BRIDGE APPR. SLAB	LB	101704
69060	SHEET PILES, STEEL	SF	avg. 1017 & 101
69100	REINF. STEEL	LB	101704
69104	CORROSION RESISTANT REINF. STEEL	LB	101704
69105	EPOXY COATED REINF. STEEL	LB	101704
69110	STEEL PILES 10"	LF	avg. 1017 & 101
69112	STEEL PILE 12"	LF	avg. 1017 & 101
69113	DRIVING TEST FOR 12" STEEL PILE	LF	avg. 1017 & 101

I elect to use this provision

I elect not to use this provision

Date: 04/21/14

Signature: 
Aaron T. Myers, Vice President/General Mgr.

Design-Builder: American Infrastructure-VA, Inc.

Vendor No.: G303

4.8.5 Proposal Guaranty Form C-24

COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
PROPOSAL GUARANTY

KNOW ALL MEN BY THESE PRESENTS, THAT WE American Infrastructure-VA, Inc. As principal, and (*) Surety, are held and firmly bound unto the Commonwealth of Virginia as obligee, in the amount of FIVE PERCENT OF THE DOLLAR VALUE OF THE BID, lawful money of the United States of America, for the payment of which, well and truly to be made, we bind ourselves, our heirs, executors, administrators, successors and assigns, jointly and severally and firmly by these presents.

(*) Fidelity and Deposit Company of Maryland and Zurich American Insurance Company
SIGNED, sealed and dated this 21st Day of April, 20 14

WHEREAS, the above said principal is herewith submitting its proposal for:

PROJECT NUMBER: **0606-053-983, P101, R201, C501, B687, B686**
Route 606 Loudoun County Parkway/Old Ox Road Reconstruction
Contract ID #C00097529DB64

NOW, THEREFORE, the condition of the above obligee is such, that if the aforesaid principal shall be awarded the contract upon said proposal and shall within the time specified in the Specifications after the notice of such award enter into a contract and give bond for the faithful performance of the contract, then this obligation shall be null and void; otherwise to remain in full force and effect and the principal and surety will pay unto the obligee the difference in money between the amount of the bid of the said principal and the amount for which the obligee may legally contract with another party to perform the said work if the latter amount be in excess of the former; but in no event shall the liability exceed the penal sum hereof.

American Infrastructure-VA, Inc.
(Principal*)

By: [Signature]
(Officer, Partner or Owner) (Seal)
Aaron T. Myers, Vice President/General Manager

(Principal*)

By: _____
(Officer, Partner or Owner) (Seal)

(Principal*)

By: _____
(Officer, Partner or Owner) (Seal)

Fidelity and Deposit Company of Maryland
(Surety Company)

By: [Signature]
Christine A. Dunn (Attorney-In-Fact**) (Seal)

600 Red Brook Blvd., 4th Fl., Owings Mills MD 21117
(Address)

By: Zurich American Insurance Company
(Surety Company)

[Signature]
Christine A. Dunn (Attorney-In-Fact**) (Seal)

1400 American Lane, Schaumburg IL 60196
(Address)

*Note: If the principal is a joint venture, each party thereof must be named and execution made by same hereon. If there is more than one surety to the bid bond, each surety must be named and execution shall be made by same hereon.
Electronic Bid Only: In lieu of completing the above section of the Contract Performance Bond, the Principal shall file an Electronic Bid Bond when bidding electronically. By signing below the Principal is ensuring the identified electronic bid bond has been executed and the Principal and Surety are firmly bound unto the Commonwealth of Virginia under the same conditions of the bid bond as shown above.

Electronic Bid Bond ID# _____ Company/Bidder Name _____ Signature and Title _____
**Attach copy of Power of Attorney

**ZURICH AMERICAN INSURANCE COMPANY
COLONIAL AMERICAN CASUALTY AND SURETY COMPANY
FIDELITY AND DEPOSIT COMPANY OF MARYLAND
POWER OF ATTORNEY**

KNOW ALL MEN BY THESE PRESENTS: That the ZURICH AMERICAN INSURANCE COMPANY, a corporation of the State of New York, the COLONIAL AMERICAN CASUALTY AND SURETY COMPANY, a corporation of the State of Maryland, and the FIDELITY AND DEPOSIT COMPANY OF MARYLAND a corporation of the State of Maryland (herein collectively called the "Companies"), by **GEOFFREY DELISIO, Vice President**, in pursuance of authority granted by Article V, Section 8, of the By-Laws of said Companies, which are set forth on the reverse side hereof and are hereby certified to be in full force and effect on the date hereof, do hereby nominate, constitute, and appoint **Harry C. ROSENBERG, David C. ROSENBERG, Matthew J. ROSENBERG, Christine A. DUNN, Denise M. BRUNO, Julia R. BURNET, Kimberly G. RIVELY, Michelle G. HIGGINS, Joyce M. HOFFMAN and Jonathan F. BLACK**, all of **King of Prussia, Pennsylvania**, EACH its true and lawful agent and Attorney-in-Fact, to make, execute, seal and deliver, for, and on its behalf as surety, and as its act and deed: **any and all bonds and undertakings**, and the execution of such bonds or undertakings in pursuance of these presents, shall be as binding upon said Companies, as fully and amply, to all intents and purposes, as if they had been duly executed and acknowledged by the regularly elected officers of the ZURICH AMERICAN INSURANCE COMPANY at its office in New York, New York, the regularly elected officers of the COLONIAL AMERICAN CASUALTY AND SURETY COMPANY at its office in Owings Mills, Maryland, and the regularly elected officers of the FIDELITY AND DEPOSIT COMPANY OF MARYLAND at its office in Owings Mills, Maryland, in their own proper persons.

The said Vice President does hereby certify that the extract set forth on the reverse side hereof is a true copy of Article V, Section 8, of the By-Laws of said Companies, and is now in force.

IN WITNESS WHEREOF, the said Vice-President has hereunto subscribed his/her names and affixed the Corporate Seals of the said ZURICH AMERICAN INSURANCE COMPANY, COLONIAL AMERICAN CASUALTY AND SURETY COMPANY, and FIDELITY AND DEPOSIT COMPANY OF MARYLAND, this 7th day of February, A.D. 2013.

ATTEST:

**ZURICH AMERICAN INSURANCE COMPANY
COLONIAL AMERICAN CASUALTY AND SURETY COMPANY
FIDELITY AND DEPOSIT COMPANY OF MARYLAND**



Gerald F. Haley

By: _____

*Assistant Secretary
Gerald F. Haley*

Geoffrey Delisio

*Vice President
Geoffrey Delisio*

State of Maryland
City of Baltimore

On this 7th day of February, A.D. 2013, before the subscriber, a Notary Public of the State of Maryland, duly commissioned and qualified, **GEOFFREY DELISIO, Vice President, and GERALD F. HALEY, Assistant Secretary**, of the Companies, to me personally known to be the individuals and officers described in and who executed the preceding instrument, and acknowledged the execution of same, and being by me duly sworn, depose and saith, that he/she is the said officer of the Company aforesaid, and that the seals affixed to the preceding instrument are the Corporate Seals of said Companies, and that the said Corporate Seals and the signature as such officer were duly affixed and subscribed to the said instrument by the authority and direction of the said Corporations.

IN TESTIMONY WHEREOF, I have hereunto set my hand and affixed my Official Seal the day and year first above written.

Maria D. Adamski



*Maria D. Adamski, Notary Public
My Commission Expires: July 8, 2015*

EXTRACT FROM BY-LAWS OF THE COMPANIES

"Article V, Section 8, Attorneys-in-Fact. The Chief Executive Officer, the President, or any Executive Vice President or Vice President may, by written instrument under the attested corporate seal, appoint attorneys-in-fact with authority to execute bonds, policies, recognizances, stipulations, undertakings, or other like instruments on behalf of the Company, and may authorize any officer or any such attorney-in-fact to affix the corporate seal thereto; and may with or without cause modify or revoke any such appointment or authority at any time."

CERTIFICATE

I, the undersigned, Vice President of the ZURICH AMERICAN INSURANCE COMPANY, the COLONIAL AMERICAN CASUALTY AND SURETY COMPANY, and the FIDELITY AND DEPOSIT COMPANY OF MARYLAND, do hereby certify that the foregoing Power of Attorney is still in full force and effect on the date of this certificate; and I do further certify that Article V, Section 8, of the By-Laws of the Companies is still in force.

This Power of Attorney and Certificate may be signed by facsimile under and by authority of the following resolution of the Board of Directors of the ZURICH AMERICAN INSURANCE COMPANY at a meeting duly called and held on the 15th day of December 1998.

RESOLVED: "That the signature of the President or a Vice President and the attesting signature of a Secretary or an Assistant Secretary and the Seal of the Company may be affixed by facsimile on any Power of Attorney...Any such Power or any certificate thereof bearing such facsimile signature and seal shall be valid and binding on the Company."

This Power of Attorney and Certificate may be signed by facsimile under and by authority of the following resolution of the Board of Directors of the COLONIAL AMERICAN CASUALTY AND SURETY COMPANY at a meeting duly called and held on the 5th day of May, 1994, and the following resolution of the Board of Directors of the FIDELITY AND DEPOSIT COMPANY OF MARYLAND at a meeting duly called and held on the 10th day of May, 1990.

RESOLVED: "That the facsimile or mechanically reproduced seal of the company and facsimile or mechanically reproduced signature of any Vice-President, Secretary, or Assistant Secretary of the Company, whether made heretofore or hereafter, wherever appearing upon a certified copy of any power of attorney issued by the Company, shall be valid and binding upon the Company with the same force and effect as though manually affixed.

IN TESTIMONY WHEREOF, I have hereunto subscribed my name and affixed the corporate seals of the said Companies, this 21st day of April, 2014.



A handwritten signature in cursive script that reads "James M. Carroll".

James M. Carroll, Vice President

4.8.6

Sworn Statements



**COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION**

PROJECT: Route 606 Loudoun County Parkway/Old Ox Road Reconstruction and Widening

FHWA: FPN 5A01 (165)

This form must be completed, signed and returned with bid; and failure to do so may result in the rejection of your bid. **THE CONTRACTOR SHALL AFFIRM THE FOLLOWING STATEMENT EITHER BY SIGNING THE AFFIDAVIT AND HAVING IT NOTARIZED OR BY SIGNING THE UNSWORN DECLARATION UNDER PENALTY OF PERJURY UNDER THE LAWS OF THE UNITED STATES. A SEPARATE FORM MUST BE SUBMITTED BY EACH PRINCIPAL OF A JOINT VENTURE BID.**

STATEMENT In preparation and submission of this bid, I, the firm, corporation or officers, agents or employees thereof did not, either directly or indirectly, enter into any combination or arrangement with any persons, firm or corporation or enter into any agreement, participate in any collusion, or otherwise take any action in the restraint of free, competitive bidding in violation of the Sherman Act (15 U.S.C. Section 1) or Article 1.1 or Chapter 12 of Title 18.2 (Virginia Governmental Frauds Act), Sections 59.1-9.1 through 59.1-9.17 or Sections 59.1-68.6 through 59.1-68.8 of the Code of Virginia.

AFFIDAVIT

The undersigned is duly authorized by the bidder to make the foregoing statement to be filed with bids submitted on behalf of the bidder for contracts to be let by the Commonwealth Transportation Board.

Signed at Henrico (Glen Allen), VA this 15th day of APRIL, 20 14
County (City), STATE
American Infrastructure-VA, Inc. By: [Signature] VICE PRESIDENT (GM)
(Name of Firm) (Signature) Title (print)
STATE of Virginia COUNTY (CITY) of Henrico (Glen Allen)

To-wit: I Madelyn Ruth Treadwell, a Notary Public in and for the State and County(City) aforesaid, hereby certify that this day Aaron T. Myers


personally appeared before me and made oath that he is duly authorized to make the above statements and that such statements are true and correct.

Subscribed and sworn to before me this 15th day of April, 20 14
Madelyn Ruth Treadwell My Commission expires October 31, 2017
Notary Public

**OR
UNSWORN DECLARATION**

The undersigned is duly authorized by the bidder to make the foregoing statement to be filed with bids submitted on behalf of the bidder for contracts to be let by the Commonwealth Transportation Board.

Signed at _____, this _____ day of _____, 20 ____
County (City), STATE
(Name of Firm) By: _____ (Signature) _____ Title (print)



**COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
AFFIDAVIT**

PROJECT:

Route 606 Loudoun County Parkway/Old Ox Road Reconstruction and Widening

FHWA: FPN 5A01 (165)

This form must be completed, signed, notarized and returned with bid; and failure to do so, may result in the rejection of your bid. A separate form must be submitted by each principal of a joint venture bid.

- I, the firm, corporation or officers, agents or employees thereof have neither directly nor indirectly entered into any combination or arrangement with any person, firm or corporation or entered into any agreement, participated in any collusion, or otherwise taken any action in restraint of free competitive bidding in connection with such contract, the effect of which is to prevent competition or increase the cost of construction or maintenance of roads or bridges.

During the preceding twelve months, I (we) have been a member of the following Highway Contractor's Associations, as defined in Section 33.1-336 of the Code of Virginia (1970). (If none, so state).

NAME	Location of Principal Office
N/A	

- I (we) have , have not , participated in a previous contract or subcontract subject to the equal opportunity clause, as required by Executive Orders 10925, 11114, or 11246, and that I/We have , have not , filed with the joint Reporting Committee, the Director of the Office of Federal Contract Compliance, a Federal Government contracting or administering agency, or the former President's Committee on Equal Employment Opportunity, all reports due under the applicable filing requirements.

Note: The above certification is required by the Equal Employment Opportunity Regulations of the Secretary of Labor [41 CFR 60-1.7(b)(1)], and must be submitted by bidders and proposed subcontractors only in connection with contracts and subcontracts which are subject to the equal opportunity clause. Contracts and subcontracts which are exempt from the equal opportunity clause are set forth in 41 CFR 60-1.5. (Generally only contract or subcontracts of \$10,000 or under are exempt.)

Currently, Standard Form 100 (EEO-1) is the only report required by the Executive Orders or their implementing regulations.

Proposed prime contractors and subcontractors who have participated in a previous contract or subcontract subject to the Executive Orders and have not filed the required reports should note that 41 CFR 60-1.7(b) (1) prevents the award of contract and subcontract unless such contractor submits a report covering the delinquent period or such other period specified by the Federal Highway Administration or by the Director, Office of Federal Contract Compliance, U.S. Department of Labor.

(Continued)

ORDER NO.:
CONTRACT ID. NO.:

Form C-105
page 2

3. The bidder certifies to the best of its knowledge and belief, that it and its principals:
- (a) Are not presently debarred, suspended, proposed for debarment, declared ineligible or voluntarily excluded from covered transactions by any Federal department or agency;
 - (b) Have not within a three year period preceding this proposal been convicted of or had a civil judgement rendered against them for commission of fraud or a criminal offence in connection with obtaining, attempting to obtain, or performing a public (Federal, State or local) transaction or contract under a public transaction; violation of Federal or State antitrust statutes or commission of embezzlement, theft, forgery, bribery, falsification or destruction of records, making false statements, or receiving stolen property;
 - (c) Are not presently indicted for or otherwise criminally or civilly charged by a governmental entity (Federal, State or local) with commission of any of the offenses enumerated above; and
 - (d) Where the bidders is unable to certify to any of the statements in this certification, the bidder shall show an explanation below.

Explanations will not necessarily result in denial of award, but will be considered in determining bidder responsibility. For any explanation noted, indicate below to whom it applies, initiating agency, and dates of action. Providing false information may result in federal criminal prosecution or administration sanctions. The bidder shall provide immediate written notice to the Department if at any time the bidder learns that its certification was erroneous when submitted or has become erroneous by reason of change circumstances.

The undersigned is duly authorized by the bidder to make the foregoing statements to be filed with bids submitted on behalf of the bidder for contracts to be let by the Commonwealth Transportation Board.

Signed at Henrico (Glen Allen), VA, this 5th day of APRIL, 20 14
County (City), STATE
American Infrastructure-VA, Inc. By: [Signature] VICE PRESIDENT / GM
(Name of Firm) (Signature) Title (print)
STATE of Virginia COUNTY (CITY) of Henrico (Glen Allen)
To-wit:

I Madelyn Ruth Treadwell, a Notary Public in and for the State and County(City) aforesaid, hereby certify that this day Aaron T. Myers

personally appeared before me and made oath that he is duly authorized to make the above statements and that such statements are true and correct.

Subscribed and sworn to before me this 15th day of April, 20 14
[Signature] My Commission expires October 31, 2017
Notary Public



4.8.7 DBE Requirements Forms



COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
MINIMUM DBE REQUIREMENTS

PROJECT NO. 0606-053-983 (Phase A and Phase B)
FHWA NO. FPN 5A01 (165)

*** INSTRUCTIONS ***

THIS FORM CAN BE USED BY THE CONTRACTOR TO SUBMIT THE NAMES OF DBE FIRMS TO BE UTILIZED ON THE PROJECT. THE CONTRACTOR SHALL INDICATE THE DESCRIPTION OF THE CATEGORY (S, M, SP or H) AND THE TYPE OF WORK THAT EACH DBE WILL PERFORM AND THE ALLOWABLE CREDIT PER ITEM(S). ADDITIONAL SHEETS TO SHOW THE ALLOWABLE CREDIT PER ITEM MAY BE ATTACHED IF NECESSARY. PLEASE NOTE: THE AMOUNT OF ALLOWABLE CREDIT FOR A DBE SUPPLIER IS 60% OF THE TOTAL COST OF THE MATERIALS OR SUPPLIES OBTAINED AND 100% FOR A DBE MANUFACTURER OF THE MATERIALS AND SUPPLIES OBTAINED. A CONTRACTOR MAY COUNT 100% OF THE FEES PAID TO A DBE HAULER FOR THE DELIVERY OF MATERIALS AND SUPPLIES TO THE PROJECT SITE, BUT NOT FOR THE COST OF THE MATERIALS AND SUPPLIES THEMSELVES.

DBE REQUIREMENT 14 %
PERCENT ATTAINED BY BIDDER 14.01 %

NAMES(S) AND CERTIFICATION NO. OF DBE(S) TO BE USED	USED AS SUBCONTR. (S) MFG. (M) SUPPLIER (SP) HAULER (H)	TYPE OF WORK AND ITEM NO(S)	\$ AMOUNT OF ALLOWABLE CREDIT PER ITEM
<u>626263 Interlock Steelworkers, Inc.</u>	<u>(S)</u>	<u>238120 Furnish/Inst. Structural Steel/Absor.</u>	<u>\$ 3,936,815⁰⁰</u>
<u>672352 PAK Drilling + Blasting, Inc.</u>	<u>(S)</u>	<u>238910 Drilling + Blasting</u>	<u>\$ 900,000⁰⁰</u>
<u>661689 Toro Concrete, Inc.</u>	<u>(S)</u>	<u>238990 Curb + Gutter Construction</u>	<u>\$ 634,323⁰⁰</u>
<u>DB 2009-0097-2015</u>			
<u>K.D. Jones + Sons Trucking, LLC</u>	<u>(H)</u>	<u>484110 Hauling</u>	<u>\$ 1,031,632⁰⁰</u>
<u>650566 Rojas Linceo Trucking, Inc.</u>	<u>(H)</u>	<u>484220 Dump Trucking</u>	<u>\$ 500,000⁰⁰</u>
		TOTAL	<u>\$ Continual on Page 2</u>

TOTAL CONTRACT VALUE \$ 89,677,777⁰⁰ x REQUIRED DBE 14 % = \$ 12,554,888.78

I/WE CERTIFY THAT THE PROPOSED DBE(S) SUBMITTED WILL BE USED ON THIS CONTRACT AS STATED HEREON AND ASSURE THAT DURING THE LIFE OF THE CONTRACT. I/WE WILL MEET OR EXCEED THE PARTICIPATION ESTABLISHED HEREON BY THE DEPARTMENT.

American Infrastructure-VA, Inc.
BIDDER
VP / GM
TITLE

BY
BY


SIGNATURE
4/21/14
DATE

COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
MINIMUM DBE REQUIREMENTS

PROJECT NO. 0606-053-983 (Phase A and Phase B)

FHWA NO. _____

*** INSTRUCTIONS ***

THIS FORM CAN BE USED BY THE CONTRACTOR TO SUBMIT THE NAMES OF DBE FIRMS TO BE UTILIZED ON THE PROJECT. THE CONTRACTOR SHALL INDICATE THE DESCRIPTION OF THE CATEGORY (S, M, SP or H) AND THE TYPE OF WORK THAT EACH DBE WILL PERFORM AND THE ALLOWABLE CREDIT PER ITEM(S). ADDITIONAL SHEETS TO SHOW THE ALLOWABLE CREDIT PER ITEM MAY BE ATTACHED IF NECESSARY. PLEASE NOTE: THE AMOUNT OF ALLOWABLE CREDIT FOR A DBE SUPPLIER IS 60% OF THE TOTAL COST OF THE MATERIALS OR SUPPLIES OBTAINED AND 100% FOR A DBE MANUFACTURER OF THE MATERIALS AND SUPPLIES OBTAINED. A CONTRACTOR MAY COUNT 100% OF THE FEES PAID TO A DBE HAULER FOR THE DELIVERY OF MATERIALS AND SUPPLIES TO THE PROJECT SITE, BUT NOT FOR THE COST OF THE MATERIALS AND SUPPLIES THEMSELVES.

DBE REQUIREMENT 14 %

PERCENT ATTAINED BY BIDDER 14.01 %

NAMES(S) AND CERTIFICATION NO. OF DBE(S) TO BE USED	USED AS SUBCONTR. (S) MFG. (M) SUPPLIER (SP) HAULER (H)	TYPE OF WORK AND ITEM NO(S)	\$ AMOUNT OF ALLOWABLE CREDIT PER ITEM
<u>DB2014-0174-2015</u> <u>Andre-Adrian, LLC t/a A-A, LLC</u>	<u>(H)</u>	<u>484220 Trucking</u>	<u>\$ 2,600,120.00</u>
<u>DB2000-0224-2014</u> <u>Electrifiers' Inc.</u>	<u>(S)</u>	<u>230210 Electrical</u>	<u>\$ 482,762.00</u>
<u>DB2011-0009-2014</u> <u>S.P. Trucking, LLC</u>	<u>(H)</u>	<u>484220 Trucking</u>	<u>\$ 2,480,000.00</u>
TOTAL			<u>\$12,565,652.00</u>


TOTAL CONTRACT VALUE \$89,677,777.00 x REQUIRED DBE 14 % = \$12,554,888.78

I/WE CERTIFY THAT THE PROPOSED DBE(S) SUBMITTED WILL BE USED ON THIS CONTRACT AS STATED HEREON AND ASSURE THAT DURING THE LIFE OF THE CONTRACT. I/WE WILL MEET OR EXCEED THE PARTICIPATION ESTABLISHED HEREON BY THE DEPARTMENT.

American Infrastructure-VA, Inc.
BIDDER
VP/GM
TITLE

BY

BY


SIGNATURE
4/21/14
DATE

**COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
CERTIFICATION OF BINDING AGREEMENT
WITH
DISADVANTAGED BUSINESS ENTERPRISE FIRMS**

Project No.: 0606-053-983

Federal Project No.: FPN 5A01 (165)

This form is to be submitted in accordance with the Department's Special Provision for Section 107.15.

It is hereby certified by the below signed Contractors that there exists a written quote, acceptable to the parties involved preliminary to a binding subcontract agreement stating the details concerning the work to be performed and the price which will be paid for the aforementioned work. This document is not intended to, nor should it be construed to, contain the entire text of the agreement between the contracting parties. This document does not take the place of, nor may it be substituted for, an official subcontracting agreement in those situations that may require such an agreement. A copy of the fully executed *subcontract agreement* shall be submitted to the Engineer within fourteen (14) business days after contract execution.

It is further certified that the aforementioned mutually acceptable quote and fully executed subcontract agreement represent the entire agreement between the parties involved and that no conversations, verbal agreements, or other forms of non-written representations shall serve to add to, delete, or modify the terms as stated.

The prime Contractor further represents that the aforementioned mutually acceptable quote and fully executed subcontract agreement shall remain on file for a period of not less than one year following completion of the prime's contract with the Department or for such longer period as provisions of governing Federal or State law or regulations may require. For purposes of this form, the term Prime Contractor shall refer to any Contractor utilizing a DBE subcontractor, regardless of tier, in which they are claiming DBE credit toward the contract goal.

Contractors further jointly and severally represent that said binding agreement is for the performance of a "commercially useful function" as that term is employed in 49 C.F.R. Part 26.55 (c), (d).

**TO BE SIGNED BY THE SUBCONTRACTOR TO THE PRIME CONTRACTOR, AND ANY LOWER TIER
SUBCONTRACTORS HAVING A CONTRACT WITH THE BELOW NAMED DBE FIRM**

Prime Contractor American Infrastructure - VA, Inc.

By:  Purchasing Manager
Signature Title

Date: April 21, 2014

First Tier
Subcontractor if
Applicable

By: _____
Signature Title

Date: _____


Second Tier
Subcontractor if
Applicable

By: _____
Signature Title
Date: _____

Third Tier
Subcontractor if
Applicable

By: _____
Signature Title
Date: _____

DBE Contractor

INTERLOCK STEELWORKERS, INC
By: 
Signature Title
Date: 4-18-14

COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
CERTIFICATION OF BINDING AGREEMENT
WITH
DISADVANTAGED BUSINESS ENTERPRISE FIRMS

Project No.: 0606 - 053 - 983

Federal Project No.: FPN 5A01 (165)

This form is to be submitted in accordance with the Department's Special Provision for Section 107.15.

It is hereby certified by the below signed Contractors that there exists a written quote, acceptable to the parties involved preliminary to a binding subcontract agreement stating the details concerning the work to be performed and the price which will be paid for the aforementioned work. This document is not intended to, nor should it be construed to, contain the entire text of the agreement between the contracting parties. This document does not take the place of, nor may it be substituted for, an official subcontracting agreement in those situations that may require such an agreement. A copy of the fully executed *subcontract agreement* shall be submitted to the Engineer within fourteen (14) business days after contract execution.

It is further certified that the aforementioned mutually acceptable quote and fully executed subcontract agreement represent the entire agreement between the parties involved and that no conversations, verbal agreements, or other forms of non-written representations shall serve to add to, delete, or modify the terms as stated.

The prime Contractor further represents that the aforementioned mutually acceptable quote and fully executed subcontract agreement shall remain on file for a period of not less than one year following completion of the prime's contract with the Department or for such longer period as provisions of governing Federal or State law or regulations may require. For purposes of this form, the term Prime Contractor shall refer to any Contractor utilizing a DBE subcontractor, regardless of tier, in which they are claiming DBE credit toward the contract goal.

Contractors further jointly and severally represent that said binding agreement is for the performance of a "commercially useful function" as that term is employed in 49 C.F.R. Part 26.55 (c), (d)

TO BE SIGNED BY THE SUBCONTRACTOR TO THE PRIME CONTRACTOR, AND ANY LOWER TIER
SUBCONTRACTORS HAVING A CONTRACT WITH THE BELOW NAMED DBE FIRM

Prime Contractor American Infrastructure-VA, Inc.

By: Matthew M. Jewett Signature April 21, 2014 Date
Title: Purchasing Manager

First Tier Subcontractor if Applicable PRK Drilling + Blasting, Inc.

By: John Klebeke Signature V.P. Title
Date: 4/18/14

Second Tier
Subcontractor if
Applicable

By: _____
Signature Title
Date: _____

Third Tier
Subcontractor if
Applicable

By: _____
Signature Title
Date: _____

DBE Contractor

PRK Drilling + Blasting, Inc.

By: Frank Klebicko V. P.
Signature Title
Date: 4/18/14

COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
CERTIFICATION OF BINDING AGREEMENT
WITH
DISADVANTAGED BUSINESS ENTERPRISE FIRMS

Project No.: 0606-053-983

Federal Project No.: FPN 5A01 (165)

This form is to be submitted in accordance with the Department's Special Provision for Section 107.15.

It is hereby certified by the below signed Contractors that there exists a written quote, acceptable to the parties involved preliminary to a binding subcontract agreement stating the details concerning the work to be performed and the price which will be paid for the aforementioned work. This document is not intended to, nor should it be construed to, contain the entire text of the agreement between the contracting parties. This document does not take the place of, nor may it be substituted for, an official subcontracting agreement in those situations that may require such an agreement. A copy of the fully executed *subcontract agreement* shall be submitted to the Engineer within fourteen (14) business days after contract execution.

It is further certified that the aforementioned mutually acceptable quote and fully executed subcontract agreement represent the entire agreement between the parties involved and that no conversations, verbal agreements, or other forms of non-written representations shall serve to add to, delete, or modify the terms as stated.

The prime Contractor further represents that the aforementioned mutually acceptable quote and fully executed subcontract agreement shall remain on file for a period of not less than one year following completion of the prime's contract with the Department or for such longer period as provisions of governing Federal or State law or regulations may require. For purposes of this form, the term Prime Contractor shall refer to any Contractor utilizing a DBE subcontractor, regardless of tier, in which they are claiming DBE credit toward the contract goal.

Contractors further jointly and severally represent that said binding agreement is for the performance of a "commercially useful function" as that term is employed in 49 C.F.R. Part 26.55 (c), (d).

TO BE SIGNED BY THE SUBCONTRACTOR TO THE PRIME CONTRACTOR, AND ANY LOWER TIER
SUBCONTRACTORS HAVING A CONTRACT WITH THE BELOW NAMED DBE FIRM

Prime Contractor American Infrastructure - VA, Inc.

By: Matthew M. Smith
Signature

Purchasing Manager
Title

Date: April 21, 2014

First Tier
Subcontractor if
Applicable

By: _____
Signature

_____ Title

Date: _____

Second Tier
Subcontractor if
Applicable

By: _____ Signature _____ Title _____
Date: _____

Third Tier
Subcontractor if
Applicable

By: _____ Signature _____ Title _____
Date: _____

DBE Contractor

TORO Concrete, Inc

By: *[Signature]* Signature _____ Title *Project Manager* _____
Date: _____

COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
CERTIFICATION OF BINDING AGREEMENT
WITH
DISADVANTAGED BUSINESS ENTERPRISE FIRMS

Project No.: 0606-053-983

Federal Project No.: FPN 5A01 (165)

This form is to be submitted in accordance with the Department's Special Provision for Section 107.15.

It is hereby certified by the below signed Contractors that there exists a written quote, acceptable to the parties involved preliminary to a binding subcontract agreement stating the details concerning the work to be performed and the price which will be paid for the aforementioned work. This document is not intended to, nor should it be construed to, contain the entire text of the agreement between the contracting parties. This document does not take the place of, nor may it be substituted for, an official subcontracting agreement in those situations that may require such an agreement. A copy of the fully executed *subcontract agreement* shall be submitted to the Engineer within fourteen (14) business days after contract execution.

It is further certified that the aforementioned mutually acceptable quote and fully executed subcontract agreement represent the entire agreement between the parties involved and that no conversations, verbal agreements, or other forms of non-written representations shall serve to add to, delete, or modify the terms as stated.

The prime Contractor further represents that the aforementioned mutually acceptable quote and fully executed subcontract agreement shall remain on file for a period of not less than one year following completion of the prime's contract with the Department or for such longer period as provisions of governing Federal or State law or regulations may require. For purposes of this form, the term Prime Contractor shall refer to any Contractor utilizing a DBE subcontractor, regardless of tier, in which they are claiming DBE credit toward the contract goal.

Contractors further jointly and severally represent that said binding agreement is for the performance of a "commercially useful function" as that term is employed in 49 C.F.R. Part 26.55 (c), (d).

TO BE SIGNED BY THE SUBCONTRACTOR TO THE PRIME CONTRACTOR, AND ANY LOWER TIER
SUBCONTRACTORS HAVING A CONTRACT WITH THE BELOW NAMED DBE FIRM

Prime Contractor American Infrastructure - VA, Inc.

By: Matthew J. Yemmitt Purchasing Manager
Signature Title

Date: April 21, 2014

First Tier
Subcontractor if
Applicable

By: _____
Signature Title

Date: _____

Second Tier
Subcontractor if
Applicable

By: _____
Signature Title
Date: _____

Third Tier
Subcontractor if
Applicable

By: _____
Signature Title
Date: _____

DBE Contractor

K.D. Jones & Sons Trucking, LLC

By: 
Signature
Administrative Manager
Title
Date: 04/18/2014

COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
CERTIFICATION OF BINDING AGREEMENT
WITH
DISADVANTAGED BUSINESS ENTERPRISE FIRMS

Project No.: 0606-053-983
Federal Project No.: FPN SA01(165)

This form is to be submitted in accordance with the Department's Special Provision for Section 107.15.

It is hereby certified by the below signed Contractors that there exists a written quote, acceptable to the parties involved preliminary to a binding subcontract agreement stating the details concerning the work to be performed and the price which will be paid for the aforementioned work. This document is not intended to, nor should it be construed to, contain the entire text of the agreement between the contracting parties. This document does not take the place of, nor may it be substituted for, an official subcontracting agreement in those situations that may require such an agreement. A copy of the fully executed *subcontract agreement* shall be submitted to the Engineer within fourteen (14) business days after contract execution.

It is further certified that the aforementioned mutually acceptable quote and fully executed subcontract agreement represent the entire agreement between the parties involved and that no conversations, verbal agreements, or other forms of non-written representations shall serve to add to, delete, or modify the terms as stated.

The prime Contractor further represents that the aforementioned mutually acceptable quote and fully executed subcontract agreement shall remain on file for a period of not less than one year following completion of the prime's contract with the Department or for such longer period as provisions of governing Federal or State law or regulations may require. For purposes of this form, the term Prime Contractor shall refer to any Contractor utilizing a DBE subcontractor, regardless of tier, in which they are claiming DBE credit toward the contract goal.

Contractors further jointly and severally represent that said binding agreement is for the performance of a "commercially useful function" as that term is employed in 49 C.F.R. Part 26.55 (c), (d).

**TO BE SIGNED BY THE SUBCONTRACTOR TO THE PRIME CONTRACTOR, AND ANY LOWER TIER
SUBCONTRACTORS HAVING A CONTRACT WITH THE BELOW NAMED DBE FIRM**

Prime Contractor American Infrastructure - VA, Inc.

By:  Purchasing Manager
Signature Title
Date: April 21, 2014

First Tier Subcontractor if Applicable _____

By: _____
Signature Title
Date: _____

Second Tier
Subcontractor if
Applicable

By: _____
Signature Title
Date: _____

Third Tier
Subcontractor if
Applicable

By: _____
Signature Title
Date: _____

DBE Contractor

Rojas Larco Trucking, Inc. _____

By: 
Signature Manager
Date: 04/08/2014

COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
CERTIFICATION OF BINDING AGREEMENT
WITH

DISADVANTAGED BUSINESS ENTERPRISE FIRMS

Project No.: **0606-053-983**

Federal Project No.: **FPN 5A01 (165)**

This form is to be submitted in accordance with the Department's Special Provision for Section 107.15.

It is hereby certified by the below signed Contractors that there exists a written quote, acceptable to the parties involved preliminary to a binding subcontract agreement stating the details concerning the work to be performed and the price which will be paid for the aforementioned work. This document is not intended to, nor should it be construed to, contain the entire text of the agreement between the contracting parties. This document does not take the place of, nor may it be substituted for, an official subcontracting agreement in those situations that may require such an agreement. A copy of the fully executed *subcontract agreement* shall be submitted to the Engineer within fourteen (14) business days after contract execution.

It is further certified that the aforementioned mutually acceptable quote and fully executed subcontract agreement represent the entire agreement between the parties involved and that no conversations, verbal agreements, or other forms of non-written representations shall serve to add to, delete, or modify the terms as stated.

The prime Contractor further represents that the aforementioned mutually acceptable quote and fully executed subcontract agreement shall remain on file for a period of not less than one year following completion of the prime's contract with the Department or for such longer period as provisions of governing Federal or State law or regulations may require. For purposes of this form, the term Prime Contractor shall refer to any Contractor utilizing a DBE subcontractor, regardless of tier, in which they are claiming DBE credit toward the contract goal.

Contractors further jointly and severally represent that said binding agreement is for the performance of a "commercially useful function" as that term is employed in 49 C.F.R. Part 26.55 (c), (d).

**TO BE SIGNED BY THE SUBCONTRACTOR TO THE PRIME CONTRACTOR, AND ANY LOWER TIER
SUBCONTRACTORS HAVING A CONTRACT WITH THE BELOW NAMED DBE FIRM**

Prime Contractor

American Infrastructure - VA, Inc.

By:

Matthew M. Jewett
Signature

Purchasing Manager
Title

Date:

April 21, 2014

First Tier
Subcontractor if
Applicable

By:

Signature

Title

Date:

Second Tier
Subcontractor if
Applicable

By: _____
Signature Title
Date: _____

Third Tier
Subcontractor if
Applicable

By: _____
Signature Title
Date: _____

DBE Contractor

Andre-Adrian, LLC

By: [Signature] Signature Title Field Operation
Date: 4/16/14

COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
CERTIFICATION OF BINDING AGREEMENT
WITH
DISADVANTAGED BUSINESS ENTERPRISE FIRMS

Project No.: 0606-053-983

Federal Project No.: FPN 5A01 (165)

This form is to be submitted in accordance with the Department's Special Provision for Section 107.15.

It is hereby certified by the below signed Contractors that there exists a written quote, acceptable to the parties involved preliminary to a binding subcontract agreement stating the details concerning the work to be performed and the price which will be paid for the aforementioned work. This document is not intended to, nor should it be construed to, contain the entire text of the agreement between the contracting parties. This document does not take the place of, nor may it be substituted for, an official subcontracting agreement in those situations that may require such an agreement. A copy of the fully executed subcontract agreement shall be submitted to the Engineer within fourteen (14) business days after contract execution.

It is further certified that the aforementioned mutually acceptable quote and fully executed subcontract agreement represent the entire agreement between the parties involved and that no conversations, verbal agreements, or other forms of non-written representations shall serve to add to, delete, or modify the terms as stated.

The prime Contractor further represents that the aforementioned mutually acceptable quote and fully executed subcontract agreement shall remain on file for a period of not less than one year following completion of the prime's contract with the Department or for such longer period as provisions of governing Federal or State law or regulations may require. For purposes of this form, the term Prime Contractor shall refer to any Contractor utilizing a DBE subcontractor, regardless of tier, in which they are claiming DBE credit toward the contract goal.

Contractors further jointly and severally represent that said binding agreement is for the performance of a "commercially useful function" as that term is employed in 49 C.F.R. Part 26.55 (c), (d).

TO BE SIGNED BY THE SUBCONTRACTOR TO THE PRIME CONTRACTOR, AND ANY LOWER TIER
SUBCONTRACTORS HAVING A CONTRACT WITH THE BELOW NAMED DBE FIRM

Prime Contractor American Infrastructure - VA, Inc.

By: 
Signature
Date: April 21, 2014
Title: Purchasing Manager

First Tier Subcontractor If Applicable _____

By: _____
Signature Title
Date: _____

Second Tier
Subcontractor if
Applicable

By: _____
Signature Title

Date: _____

Third Tier
Subcontractor if
Applicable

By: _____
Signature Title

Date: _____

DBE Contractor

Electrifies Inc

By: *[Signature]* _____
Signature Title

Date: *04/21/2014*



American Infrastructure
301 Concourse Blvd.
Suite 300
Glen Allen, VA 23059
804-290-8500



Rummer Klepper & Kahl
10306 Eaton Place
Willow Wood II, Suite 240
Fairfax, VA 22030
703-246-0028

