

I-581/Valley View Interchange Phase II D-B



State Project No.: 0581-128-109, P101, RW201, C501, B627
Federal Project No.: NH-581-5 (035)
Contract ID No.: C00016595DB45
I-581 / Valley View Boulevard Interchange Phase II
11/07/12; 4:00PM

LANE

in association with





November 7, 2012

Mr. Joseph A. Clarke, P.E.
Senior Project Delivery Engineer
Alternate Project Delivery Office
Virginia Department of Transportation
1401 East Broad Street
Richmond, Virginia 23219-2000

Subject: I-581/Valley View Boulevard Phase II - Request for Clarification November 1, 2012
State Project No.: 0581-128-109, P101, RW201, C501, B627
Contract ID No.: C00014695DB45

Dear Mr. Clarke:

The LANE Construction Corporation (LANE) is pleased to submit our Price Proposal for the above referenced design-build project with the Virginia Department of Transportation (VDOT). Our response contains all information requested in the RFP dated March 2, 2012, Addenda Nos. 1 and 2, and subsequent multiple correspondence through November 1, 2012. Our team's experience enables us to deliver the kind of high quality and technically-sound projects that VDOT has come to expect from us.

The LANE/STV Team appreciates the opportunity to propose on this critically important project. We look forward to partnering with the Department to make the I-581 Valley View Interchange a landmark success for the citizens of Virginia.

We hereby confirm that our Proposal meets or exceeds all of the RFP requirements.

I can be contacted at our Mid-Atlantic Regional Office by phone at (703) 222-5670 or e-mail at JPLark@laneconstruct.com should you have additional questions.

Respectfully submitted,

Joseph P. Lark
Regional Vice President
Mid-Atlantic Region
The LANE Construction Corporation

The Lane Construction Corporation

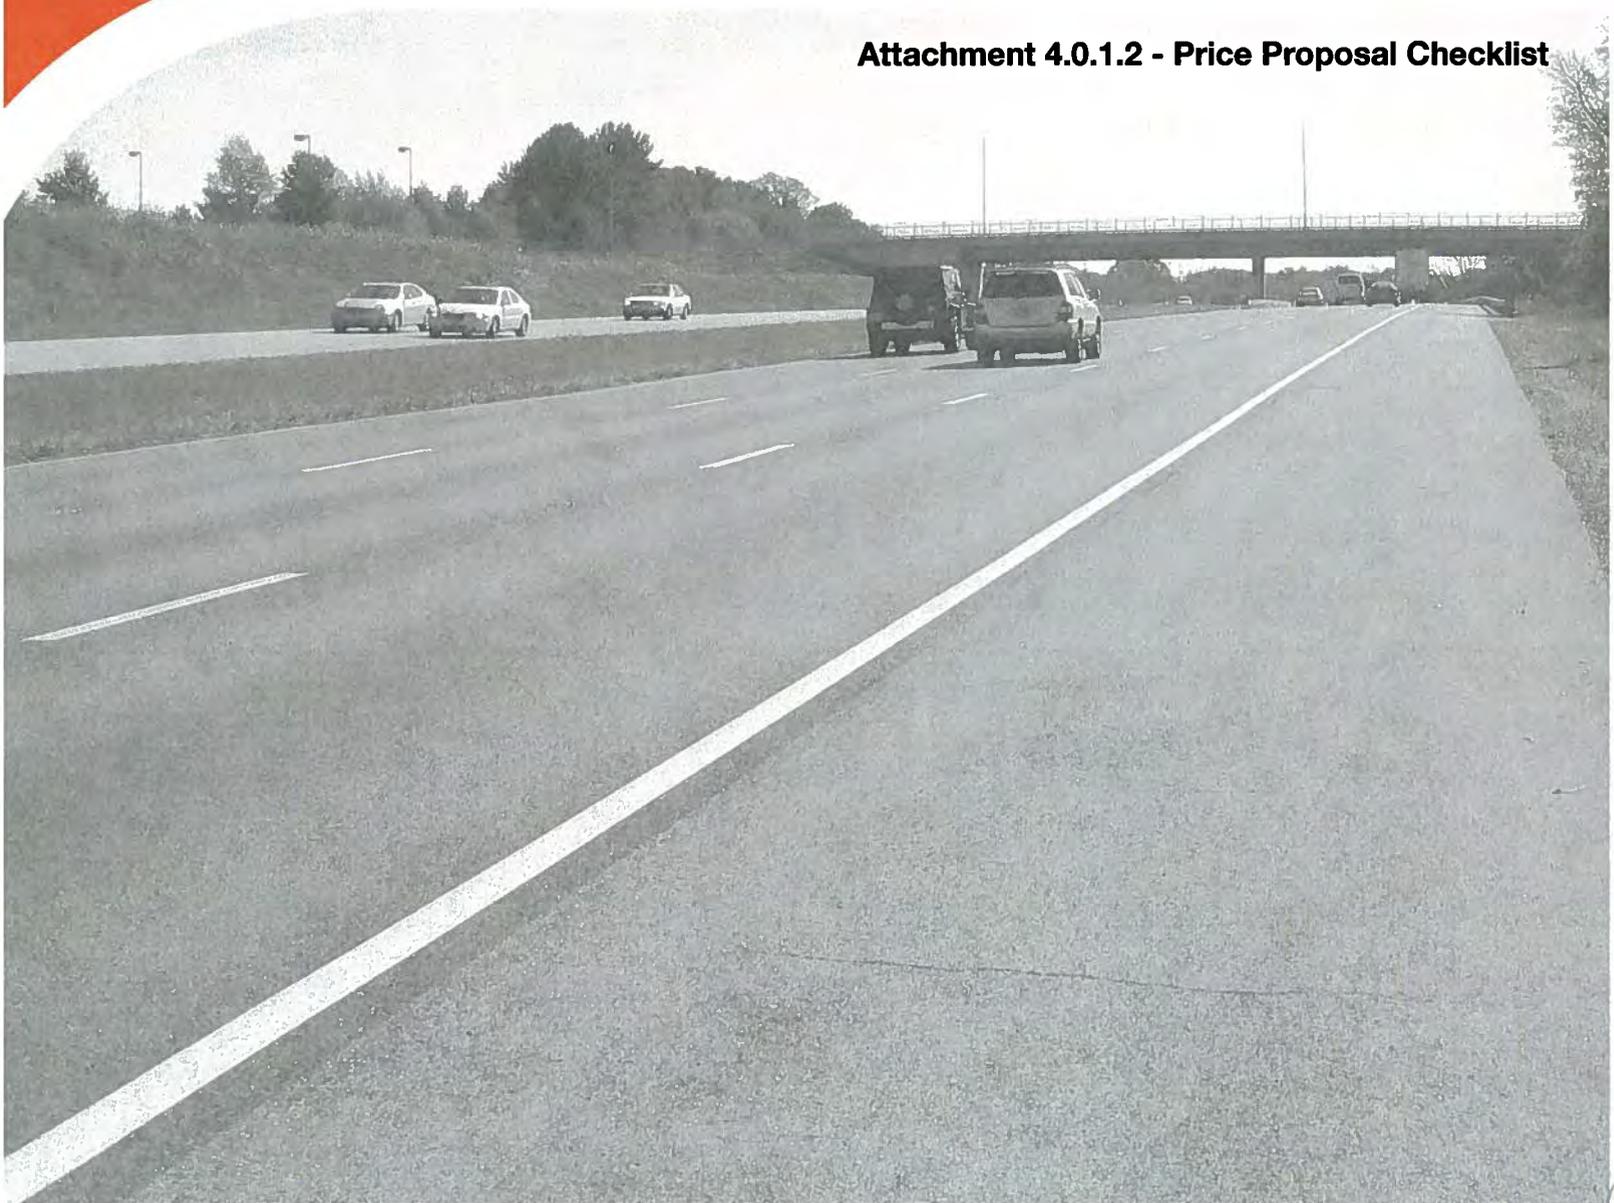
Mid-Atlantic Regional Office
14500 Avion Parkway, Suite 200, Chantilly, VA 20151 USA
An Equal Opportunity Employer M/F/D/V

T 703.222.5670 F 703.222.5960

LaneConstruct.com



Attachment 4.0.1.2 - Price Proposal Checklist



ATTACHMENT 4.0.1.2

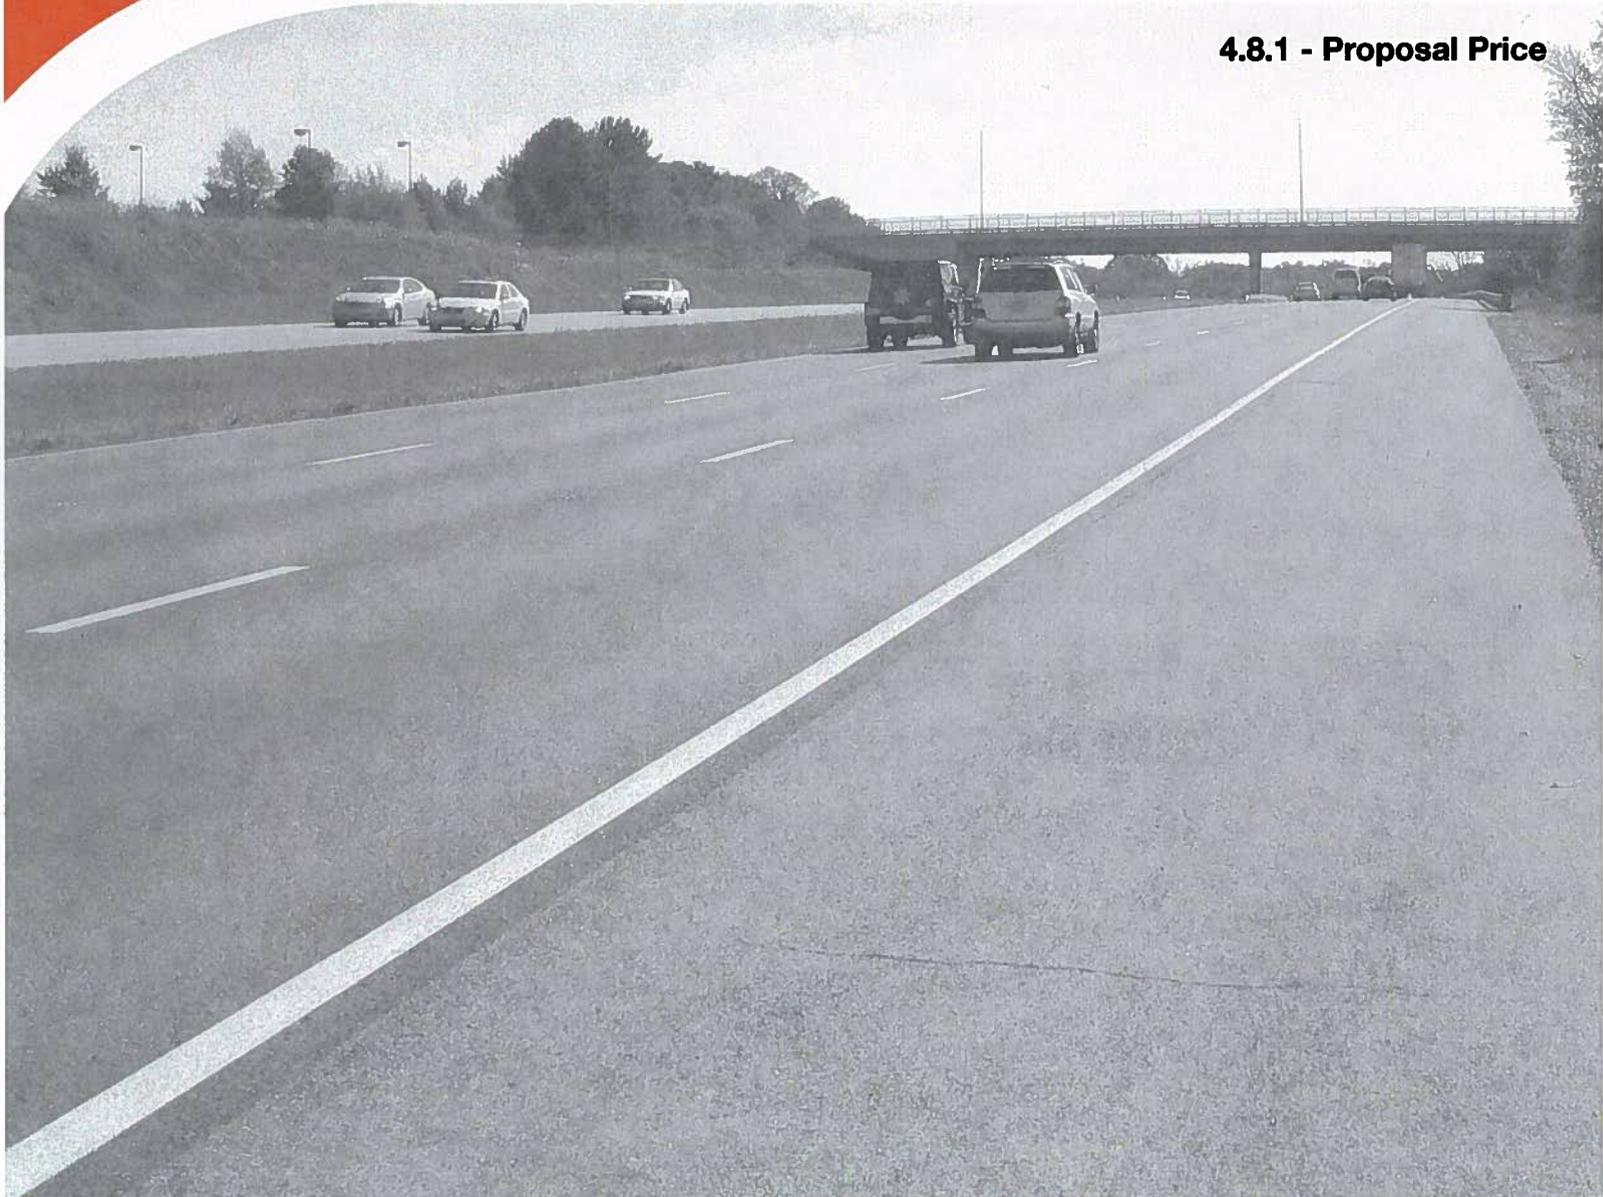
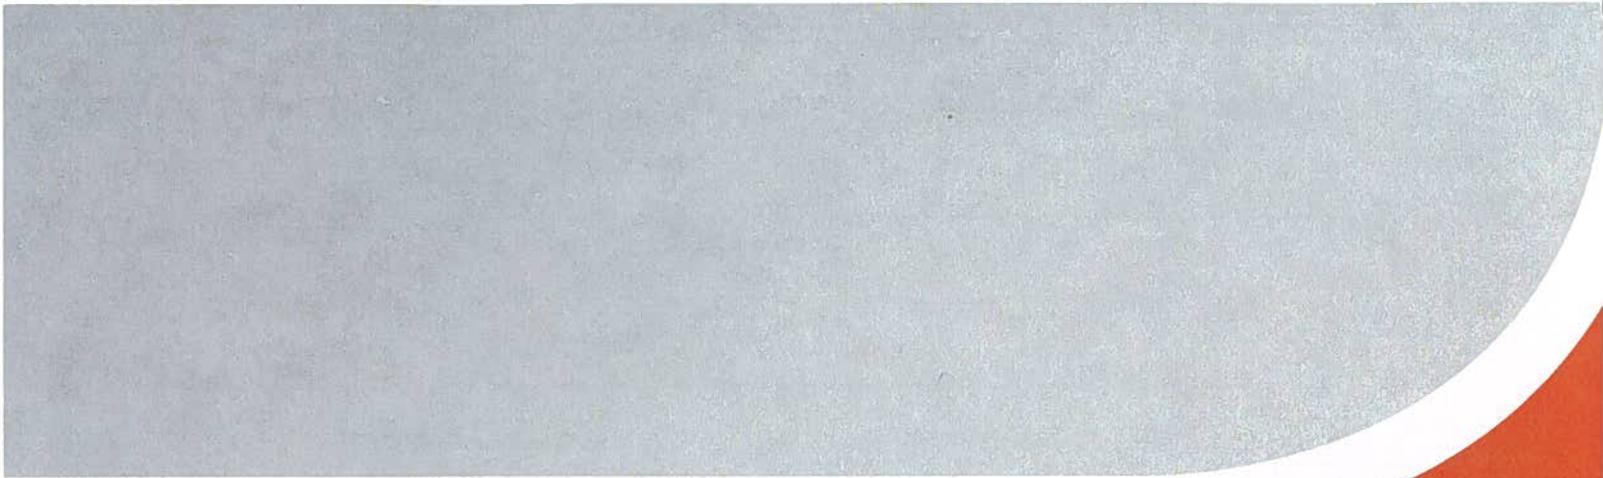
**DESIGN-BUILD PRICE PROPOSAL
CHECKLIST**

**Project Name: I-581/Valley View Boulevard Phase II
Contract ID Number: C00016595DB45**

➤ **Contents of Price Proposal:**

- Proposal Price, in both numbers and words (Attachment 4.8.1)
Acknowledgement of RFP, Revisions and/or Addenda (Attachment 3.6)**
- Schedule of Values itemized in accordance with Part 1, Section 4.8,
including material quantities and costs of each proposed work
package**
- Proposed Monthly Payment Schedule showing the anticipated
schedule on which funds will be required and associated value of
work in accordance with Part 1, Section 4.8**
- Price Adjustment Information and Forms for Fuel, Asphalt and
Steel, including identification of pay items and associated quantities
eligible for adjustment (Part 3, Section 6.3, Attachments 6.3)**
- Proposal Guaranty (C-24) required by Section 102.07 of Part 5,
Division I Amendments to the Standard Specifications**
- Sworn Statement Forms (C-104, C-105, Attachments 4.8.7(a) and
4.8.7(b))**
- DBE Requirements Forms (C-111, C-49 and C-112) as applicable
(Attachments 4.8.8(a), 4.8.8(b) and 4.8.8(c))**
- Debarment Form (Primary) – Attachment 11.8.6(a)**
- Debarment Form(s) (Lower Tier) – Attachment 11.8.6(b)**
- CD-ROM containing the entire Price Proposal in a single cohesive
Adobe PDF file**

The LANE Construction Corporation



4.8.1 - Proposal Price

ATTACHMENT 4.8.1


PRICE PROPOSAL FORM

4.8.1 Offeror shall specify, the following pricing information, in both numbers and words:

.1 Proposal Price;

Lump Sum THIRTY EIGHT MILLION FOUR HUNDRED SEVENTY FIVE THOUSAND
THREE HUNDRED FORTY FIVE DOLLARS (\$ 38,475,745.⁰⁰)

Date: November 5, 2012

Signature: 

Design-Builder: The LANE Construction Corporation

Vendor No.: L 002



4.8.3 - Schedule of Values



The Lane Construction Corporation		I-581 / Valley View Boulevard Interchange Phase II					
90 Fieldstone Court		Project No. 0581-128-109, P101, RW201, C501, 627					
Cheshire, CT 06410		Bid Date November 7, 2012 - REBID					
Sequence No.	VDOT Bid Item No.	Description	Schedule of Values		Extended Amount	Adjustment Item	
			Estimated Quantity	Units		Unit Price	Asphalt
10000	25596	PROJECT DESIGN	1	LS	\$ 4,250,000.00	\$	
10100	25593	QUALITY CONTROL	1	LS	\$ 1,100,000.00	\$	
10200	25595	QUALITY ASSURANCE	1	LS	\$ 2,100,000.00	\$	
10300	107	NS DRY UTILITY RELOCATION COSTS	1	LS	\$ 250,000.00	\$	
10400	108	NS WET UTILITY RELOCATION COSTS	1	LS	\$ 125,000.00	\$	
10500	109	NS TEST PITS FOR UTILITY CONFLICTS	1	LS	\$ 30,000.00	\$	
10600	114	NS WETLAND MITIGATION CREDITS	1	LS	\$ 1.00	\$	
10700	115	NS ENVIRONMENTAL MONITORING	1	LS	\$ 10,000.00	\$	
10800	25507	FIELD OFFICE TYPE III	1	LS	\$ 80,000.00	\$	
10900	25561	FORMAL PARTNERING	1	LS	\$ 30,000.00	\$	
11000	25565	PROGRESS SCHEDULE BASELINE	1	LS	\$ 25,000.00	\$	
11100	100	MOBILIZATION	1	LS	\$ 1,900,000.00	\$	
11200	85130	PERFORMANCE AND PAYMENT BONDS	1	LS	\$ 400,000.00	\$	
11300	101	CONSTRUCTION SURVEYING (CONSTR.)	1	LS	\$ 600,000.00	\$	
11400	111	CLEARING AND GRUBBING	7	AC	\$ 15,000.00	\$	
11450	121	NS EXCAVATION GREENWAY RELOCATION	2,600	CY	\$ 8.50	\$	
11500	120	REGULAR EXCAVATION	120,577	CY	\$ 9.00	\$	Yes
11600	140	BORROW EXCAVATION	170,185	CY	\$ 12.00	\$	Yes
11800	151	NS CLAY LINER	3,500	SY	\$ 32.00	\$	
11900	515	TEMPORARY SHEET PILING	9,000	SF	\$ 40.00	\$	
12000	522	CONCRETE CLASS A4 BOX CULVERT	78	CY	\$ 650.00	\$	Yes
12100	541	REINF. STEEL - BOX CULVERT	11,550	LB	\$ 2.50	\$	
12200	585	UNDERDRAIN UD-2	464	LF	\$ 30.00	\$	
12300	588	UNDERDRAIN UD-4	8,782	LF	\$ 6.00	\$	
12500	591	COMB. UNDERDRAIN CD-2	272	LF	\$ 10.00	\$	
12600	595	OUTLET PIPE	270	LF	\$ 21.00	\$	
12700	596	ENDWALL EW-12	14	EA	\$ 700.00	\$	
12800	700	POST INSTALLATION INSPECTION	11,402	LF	\$ 6.00	\$	
12900	27340	STREAM DIVERSIONS	150	LF	\$ 200.00	\$	
13000	1152	15" CONC. PIPE	7,806	LF	\$ 40.00	\$	
13100	1182	18" CONC. PIPE	2,225	LF	\$ 45.00	\$	
13150	1181	JACKED & BORED 18" PIPE	270	LF	\$ 1,150.00	\$	
13200	1242	24" CONC. PIPE	1,293	LF	\$ 60.00	\$	
13300	1302	30" CONC. PIPE	40	LF	\$ 110.00	\$	
13400	1362	36" CONC. PIPE	8	LF	\$ 190.00	\$	
13600	1542	54" CONC. PIPE	44	LF	\$ 375.00	\$	
13610	1600	NS TEMP. CULVERT PIPE 60" SPECIAL	393	LF	\$ 425.00	\$	
13620	1602	60" CONC. PIPE	684	LF	\$ 425.00	\$	
13625	1601	JACKED & BORED 48" PIPE	280	LF	\$ 2,700.00	\$	
13630	2432	68"X43" ELLIPTICAL CONC. PIPE	16	LF	\$ 550.00	\$	
13650	1000	NS STORM WORK @ COURT STREET	1	LS	\$ 180,000.00	\$	
13700	525-1	NS PRECAST ENDWALL EW-1, 15"	14	EA	\$ 1,100.00	\$	

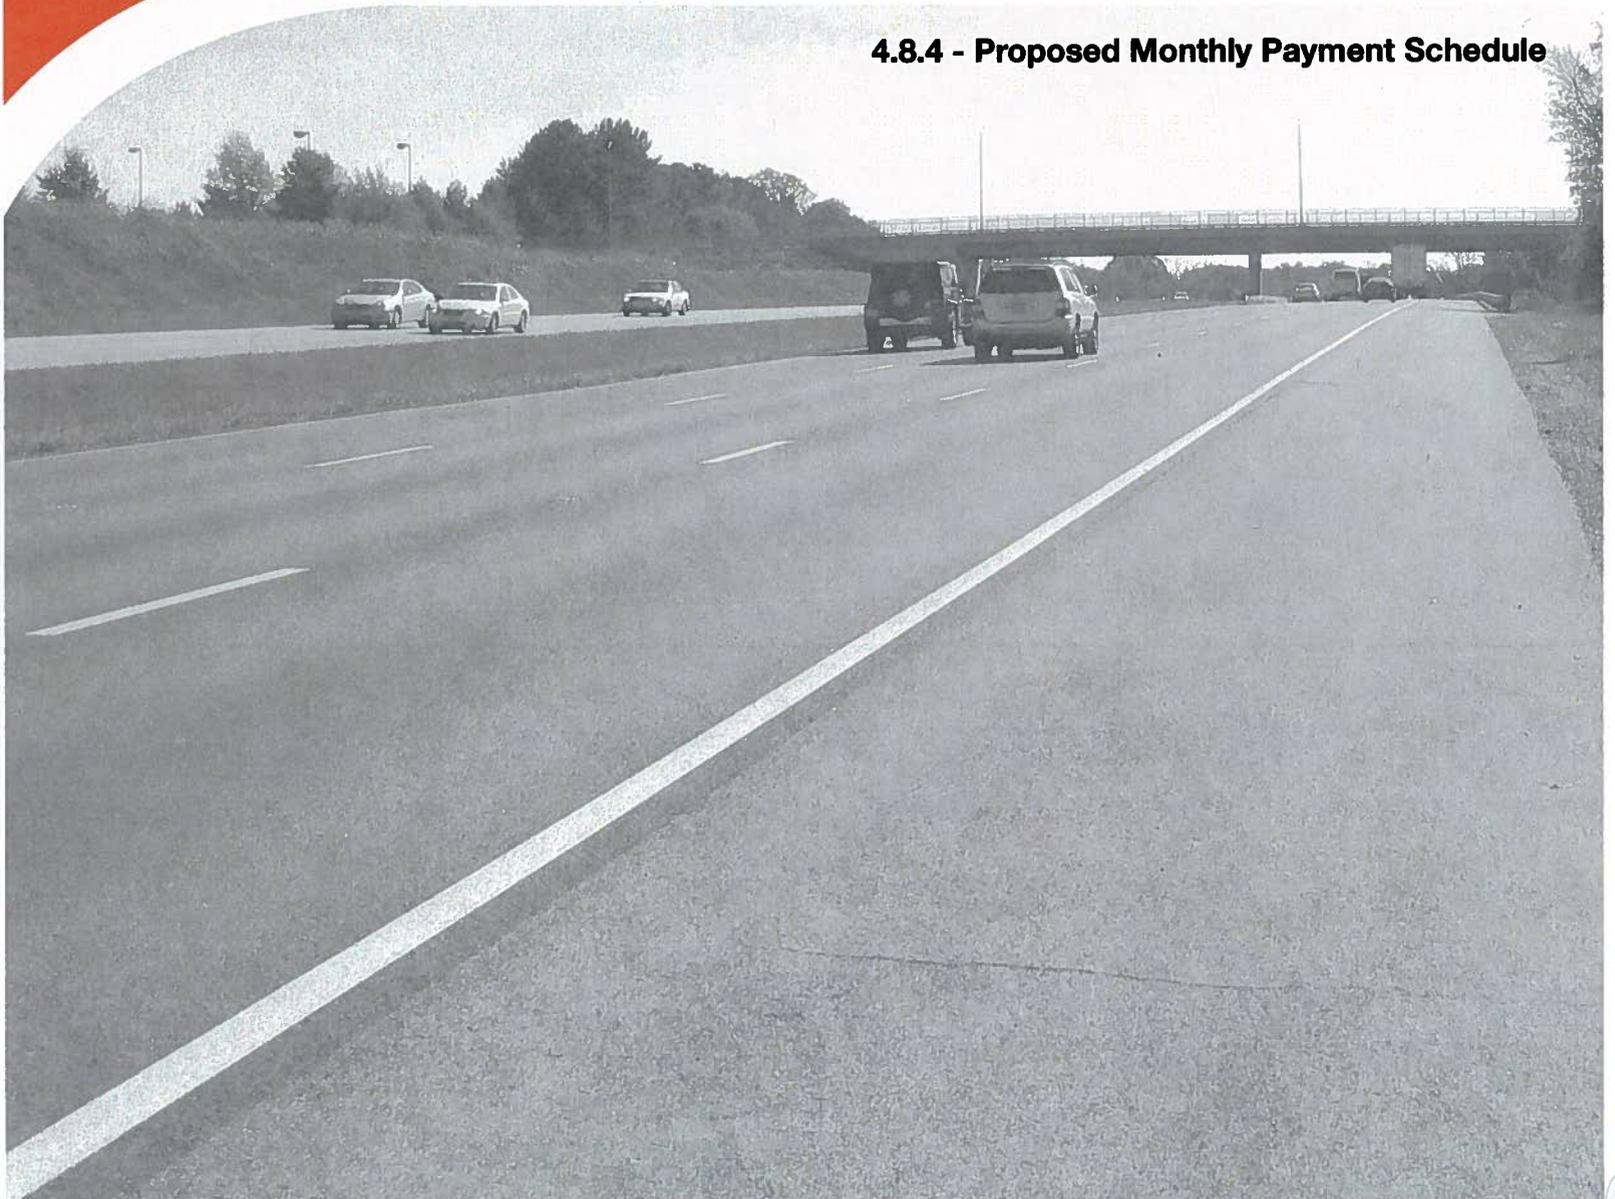
The Lane Construction Corporation		i-581 / Valley View Boulevard Interchange Phase II						
90 Fieldstone Court		Project No. 0581-128-109, P101, RW201, C501, 627						
Cheshire, CT 06410		Bid Date November 7, 2012 - REBID						
Sequence No.	VDOT Bid Item No.	Description	Schedule of Values			Extended Amount	Adjustment Item	
			Estimated Quantity	Units	Unit Price		Asphalt	Fuel
13800	525-2	NS PRECAST ENDWALL EW-1, 18"	6	EA	\$ 1,300.00	\$ 7,800.00		
13900	525-3	NS PRECAST ENDWALL EW-1, 24"	4	EA	\$ 1,500.00	\$ 6,000.00		
14000	525-4	NS PRECAST ENDWALL EW-1, 30"	2	EA	\$ 2,800.00	\$ 5,600.00		
14100	525-5	NS PRECAST ENDWALL EW-1, 36"	1	EA	\$ 2,800.00	\$ 2,800.00		
14300	525-6	NS PRECAST ENDWALL EW-1, 54"	2	EA	\$ 27,000.00	\$ 54,000.00		
14500	7506	DROP INLET DI-5	6	EA	\$ 2,500.00	\$ 15,000.00		
14510	8191	DROP INLET DI-10H	14	EA	\$ 7,000.00	\$ 98,000.00		
14520	8185	DROP INLET DI-10G	1	EA	\$ 8,600.00	\$ 8,600.00		
14530	6751	DROP INLET DI-2B MODIFIED	23	EA	\$ 4,150.00	\$ 95,450.00		
14540	6768	DROP INLET DI-2C MODIFIED	4	EA	\$ 4,250.00	\$ 17,000.00		
14550	7508	DROP INLET DI-7	17	EA	\$ 2,300.00	\$ 39,100.00		
14560	6821	DROP INLET DI-3B	14	EA	\$ 4,300.00	\$ 60,200.00		
14590	27550	OUTLET STRUCTURE SWM-1	2	EA	\$ 11,000.00	\$ 22,000.00		
14600	525-7	NS VDOT STANDARD JB-1	2	EA	\$ 9,800.00	\$ 19,600.00		
14650	1017	NS PIPE LINING	1,145	LF	\$ 425.00	\$ 486,625.00		
14700	1002	NS DRY PONDS RISERS AND ACCESS RD GRADING	1	LS	\$ 30,000.00	\$ 30,000.00		
14900	9056	MANHOLE MH-1 OR 2	9	EA	\$ 4,000.00	\$ 36,000.00		
15000	10628	FLEXIBLE PAVEMENT PLANING 0" -2"	82	SY	\$ 140.00	\$ 11,480.00		Yes
15100	10128	AGGR. BASE MATL. TY. I NO. 21B	28,125	TON	\$ 25.00	\$ 703,125.00		Yes
15200	16320	ASPHALT CONCRETE TY. IM-19.0 D	7,797	TON	\$ 108.00	\$ 842,076.00		Yes
15300	16335	ASPHALT CONCRETE TY. SM-9.5 AL	1,052	TON	\$ 145.00	\$ 152,540.00		Yes
15400	16403	ASPHALT CONCRETE TY. SMA-12.5 (76-22)	3,190	TON	\$ 145.00	\$ 462,550.00		Yes
15500	16340	ASPHALT CONCRETE TY. SM-9.5 D	2,491	TON	\$ 120.00	\$ 298,920.00		Yes
15600	16390	ASPHALT CONCRETE TY. BM-25.0 A	27,391	TON	\$ 90.00	\$ 2,465,190.00		Yes
15700	10700	RUMBLE STRIPS	13,075	LF	\$ 1.60	\$ 20,920.00		
15800	12322	MC-3B WITH BACKUP	12,603	LF	\$ 14.00	\$ 176,442.00		
16000	12030	STD. CURB CG-3	104	LF	\$ 30.00	\$ 3,120.00		
16100	12032	RADIAL CURB CG-3	8	LF	\$ 30.00	\$ 240.00		
16200	12700	STD. COMB. CURB & GUTTER CG-7	1,319	LF	\$ 25.00	\$ 32,975.00		
16300	12710	RAD. COMB. CURB & GUTTER CG-7	114	LF	\$ 25.00	\$ 2,850.00		
16325	12600	STD. COMB. CURB & GUTTER CG-6	2,054	LF	\$ 25.00	\$ 51,350.00		
16350	12610	RAD. COMB. CURB & GUTTER CG-6	272	LF	\$ 25.00	\$ 6,800.00		
16360	13108	STD. CG-12	43	SY	\$ 400.00	\$ 17,200.00		
16400	13212	NS RAW MONUMENT RM-2	30	EA	\$ 250.00	\$ 7,500.00		
16500	13220	HYDR. CEMENT CONC. SIDEWALK 4"	90	SY	\$ 90.00	\$ 8,100.00		
16550	24600	REMOVE EXISTING GUARDRAIL	13,800	LF	\$ 2.00	\$ 27,600.00		Yes
16600	13315	GUARDRAIL TERMINAL GR-11	8	EA	\$ 950.00	\$ 7,600.00		
16700	13320	GUARDRAIL GR-2	9,623	LF	\$ 20.00	\$ 192,460.00		
16800	13331	RAD. GUARDRAIL GR-2	1,146	LF	\$ 20.00	\$ 22,920.00		
16850	13344	GUARDRAIL GR-7	11	EA	\$ 2,500.00	\$ 27,500.00		
16900	13415	NS TL-5 54" BARRIER	278	LF	\$ 175.00	\$ 48,650.00		
17000	13392	FIXED OBJECT ATTACH. GR-FOA-2 TY. I	6	EA	\$ 2,700.00	\$ 16,200.00		

The Lane Construction Corporation		I-581 / Valley View Boulevard Interchange Phase II						
90 Fieldstone Court		Project No. 0581-128-109, P101, RW201, C501, 627						
Cheshire, CT 06410		Bid Date November 7, 2012 - REBID						
Sequence No.	VDOT Bid Item No.	Description	Estimated Quantity	Units	Unit Price	Extended Amount	Adjustment Item	
							Asphalt	Fuel
		Schedule of Values						
17100	13393	FIXED OBJECT ATTACH. GR-FOA-2 TY. II	2	EA	\$ 650.00	\$ 1,300.00		
17125	13383	FIXED OBJECT ATTACH. GR-FOA-1 TY. I	2	EA	\$ 2,400.00	\$ 4,800.00		
17150	13384	FIXED OBJECT ATTACH. GR-FOA-1 TY. II	2	EA	\$ 650.00	\$ 1,300.00		
17200	13530	RETAINING WALL RW-3	803	CY	\$ 500.00	\$ 401,500.00		
17250	9185	PG-2A PAVED DITCH	1,026	LF	\$ 55.00	\$ 56,430.00		
17300	21110	MEDIAN STRIP MS-1A	289	SY	\$ 140.00	\$ 40,460.00		
17400	21215	MEDIAN STRIP MS-2	1,724	LF	\$ 35.00	\$ 60,340.00		
17450	14102	NS DEMO EXISTING MEDIAN BARRIER	2,017	LF	\$ 25.00	\$ 50,425.00		
17500	13460	MB-7D BARRIER	341	LF	\$ 200.00	\$ 68,200.00		
17700	13462	MB-7F BARRIER	6,658	LF	\$ 46.00	\$ 306,268.00		
17725	13461	MB-7E BARRIER	440	LF	\$ 285.00	\$ 125,400.00		
17750	24500	NS REMOVE EXISTING FENCE	3,726	LF	\$ 4.00	\$ 14,904.00		
17800	22645	FENCE FE-CL VINYL COATED	6,890	LF	\$ 18.00	\$ 124,020.00		
17900	22663	CORNER BR.UNIT FE-CL VINYL COATED	12	EA	\$ 210.00	\$ 2,520.00		
18000	22501	FENCE FE-W1	360	LF	\$ 12.00	\$ 4,320.00		
18200	24100	ALLAYING DUST	160	HR	\$ 80.00	\$ 12,800.00		
18300	24152	TYPE III BARRICADE 8'	12	EA	\$ 850.00	\$ 10,200.00		
18400	24160	CONSTRUCTION SIGNS	384	SF	\$ 45.00	\$ 17,280.00		
18500	24272	TRUCK MOUNTED ATTENUATOR	320	HR	\$ 25.00	\$ 8,000.00		
18600	24278	GROUP 2 CHANNELIZING DEVICES	250	EA	\$ 125.00	\$ 31,250.00		
18700	24279	PORT.CHANGEABLE MESS. SIGN	10	EA	\$ 20,000.00	\$ 200,000.00		
18800	24281	ELECTRONIC ARROW	4	EA	\$ 5,500.00	\$ 22,000.00		
18900	24282	FLAGGER SERVICE	360	HR	\$ 44.00	\$ 15,840.00		
19000	24290	TRAFFIC BARRIER SER. CONC.	3,500	LF	\$ 50.00	\$ 175,000.00		
19100	24430	DEMO. OF PAVEMENT (FLEXIBLE)	38,405	SY	\$ 8.00	\$ 307,240.00		Yes
19250	27425	NS CONSTRUCTION ENTRANCE	12	EA	\$ 5,000.00	\$ 60,000.00		
19300	24501	NS REMOVE EXIST. DROP INLET ...	5	EA	\$ 1,200.00	\$ 6,000.00		
19400	24502	NS REMOVE EXIST. MANHOLE ...	2	EA	\$ 1,300.00	\$ 2,600.00		
19450	24503	NS REMOVE EXISTING PIPE (15", 18", 24")	1,059	LF	\$ 30.00	\$ 31,770.00		
19460	24504	NS REMOVE END WALLS	5	EA	\$ 1,500.00	\$ 7,500.00		
19500	27012	TOPSOIL CLASS A	24	ACRE	\$ 430.00	\$ 10,105.00		
19550	27022	TOPSOIL CLASS B	2	ACRE	\$ 27,000.00	\$ 56,700.00		
19600	27288	NS TEMPORARY SEED	26	ACRE	\$ 0.50	\$ 13.00		
19700	27102	REGULAR SEED	3,120	LB	\$ 16.00	\$ 49,920.00		
19800	27103	OVERSEEDING	312	LB	\$ 5.00	\$ 1,560.00		
19900	27215	FERTILIZER(15-30-15)	13	TON	\$ 2,000.00	\$ 26,000.00		
20000	27250	LIME	49	TON	\$ 250.00	\$ 12,150.00		
20125	1157	NS TEMPORARY 15" HDPE PIPE	180	LF	\$ 42.00	\$ 7,560.00		
20150	1247	NS TEMPORARY 24" HDPE PIPE	422	LF	\$ 45.00	\$ 18,990.00		
20200	27321	PROTECTIVE COVERING EC-2	50,658	SY	\$ 2.50	\$ 126,645.00		
20300	27410	CHECK DAM, ROCK TY. I	28	EA	\$ 635.00	\$ 17,780.00		
20400	27406	NS SEDIMENT TRAP	7	EA	\$ 7,500.00	\$ 52,500.00		

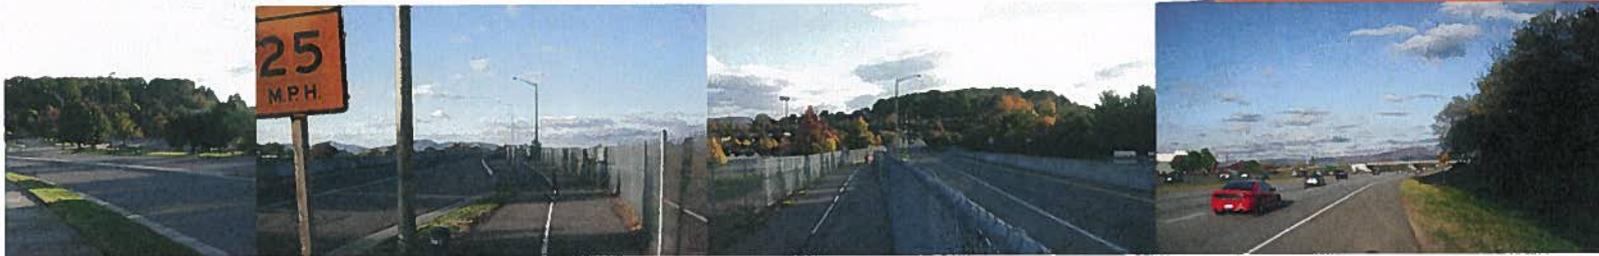
The Lane Construction Corporation		i-581 / Valley View Boulevard Interchange Phase II						
90 Fieldstone Court		Project No. 0581-128-109, P101, RW201, C501, 627						
Cheshire, CT 06410		Bid Date November 7, 2012 - REBID						
Sequence No.	VDOT Bid Item No.	Description	Schedule of Values		Unit Price	Extended Amount	Adjustment Item	
			Estimated Quantity	Units			Asphalt	Fuel
20450	27407	NS SEDIMENT BASIN	1	EA	\$ 8,000.00	\$ 8,000.00		
20475	27422	DEWATERING BASIN	8		\$ 2,500.00	\$ 20,000.00		
20500	27430	SILTATION CONTROL EXCAVATION	5,426	CY	\$ 11.00	\$ 59,686.00		
20600	27451	INLET PROTECTION , TYPE A	63	EA	\$ 190.00	\$ 11,970.00		
20700	27400	NS E&S MAINTENANCE CREW	36	MO	\$ 5,000.00	\$ 180,000.00		
20800	27460	INLET PROTECTION , TYPE B	50	EA	\$ 190.00	\$ 9,500.00		
20850	27470	NS OUTLET PROTECTION	780	SY	\$ 45.00	\$ 35,100.00		
20875	27507	NS DIVERSION DIKE	5,090	LF	\$ 3.50	\$ 17,815.00		
20885	27508	NS DIVERSION DITCH (EC-3 IF NECESSARY)	1,408	LF	\$ 3.50	\$ 4,928.00		
20900	27505	TEMP. SILT FENCE	10,000	LF	\$ 2.50	\$ 25,000.00		
20950	27504	NS SUPER SILT FENCE	10,054	LF	\$ 9.00	\$ 90,486.00		
21000	28810	MULCHING	54,500	SY	\$ 0.25	\$ 13,625.00		
21100	28820	WATERING	10,000	SY	\$ 0.60	\$ 6,000.00		
21150	29000	NS LANDSCAPING	1	LS	\$ 32,000.00	\$ 32,000.00		
21200	50100	NS SIGNAGE	1	LS	\$ 675,000.00	\$ 675,000.00		
21300	55004	NS LIGHTING	1	LS	\$ 1,030,000.00	\$ 1,030,000.00		
21400	51001	NS SIGNALIZATION	1	LS	\$ 325,000.00	\$ 325,000.00		
21500	13755	SOUND BARRIER WALL	137,086	SF	\$ 31.00	\$ 4,249,666.00		
21600	54032	TY.B CL.I PAVE. LINE MARK. 4" THERMO	15,400	LF	\$ 1.50	\$ 23,100.00		
21700	54075	TY.B CL.VI PAVE. LINE MARK. 6"	51,200	LF	\$ 4.00	\$ 204,800.00		
21800	54040	TY.B CL.I PAVE. LINE MARK. 12" THERMO	500	LF	\$ 3.50	\$ 1,750.00		
21900	54033	NS TY.B CL.VI PAVE.LINE MARK.4"CONT	690	LF	\$ 3.00	\$ 2,070.00		
22000	54076	NS TY.B CL.VI PAVE.LINE MARK.6"CONT	1,250	LF	\$ 6.00	\$ 7,500.00		
22100	54217	SNOW PLOW RAISED PAVE.MARK.ASPH. CONC	4,800	EA	\$ 39.00	\$ 187,200.00		
22200	54300	PAVE.MESS.MARK.ELONG.ARROW SIN	11	EA	\$ 190.00	\$ 2,090.00		
22300	54400	PAVEMENT MESSAGE MARK. "ONLY"	11	EA	\$ 390.00	\$ 4,290.00		
22400	54552	CONSTR.PAVE.MARK.(TY.F,CL.II)4"	15,400	LF	\$ 1.00	\$ 15,400.00		
22500	54560	CONSTR.PAVE.MARK.(TY.F,CL.II)12"	329	LF	\$ 2.00	\$ 658.00		
22600	54564	CONSTR.PAVE.MARK.(TY.F,CL.II)24"	155	LF	\$ 5.00	\$ 775.00		
22650	54553	NS CONSTR.PAVE.MARK (TY.F CL.II)6"	18,630	LF	\$ 1.50	\$ 27,945.00		
22675	68300	NS VIBRATION MONITORING	1	LS	\$ 2,500.00	\$ 2,500.00		
22700	68301	NS BRIDGE STRUCTURE REPAIR	1	LS	\$ 65,000.00	\$ 65,000.00		
22725	68302	NS GALVANIC ANODE UNITS	1	LS	\$ 68,000.00	\$ 68,000.00		
22750	68303	NS BRIDGE DEMOLITION	1	LS	\$ 110,000.00	\$ 110,000.00		
22775	68304	NS EXIST ABUTMENT RETROFIT	1	LS	\$ 110,000.00	\$ 110,000.00		
22800	65014	CONCRETE CLASS A4	411	CY	\$ 800.00	\$ 328,800.00		Yes
22900	68265	CONC. CL. A4 BRIDGE APPR. SLAB	186	CY	\$ 350.00	\$ 65,100.00		Yes
23000	68270	REINF. STEEL BRIDGE APPR. SLAB	26,970	LB	\$ 1.00	\$ 26,970.00		
23125	65120	DECK OVERLAY	1,398	SY	\$ 210.00	\$ 293,580.00		
23300	65201	CR RE.STEEL LOW CARBONICHRONIUM	110,010	LB	\$ 2.50	\$ 275,025.00		
23500	65824	RAILING, BR27C-1, 1 RAIL	241	LF	\$ 265.00	\$ 63,865.00		
23600	65826	RAILING, BR27C-10 3 RAILS	241	LF	\$ 475.00	\$ 114,475.00		



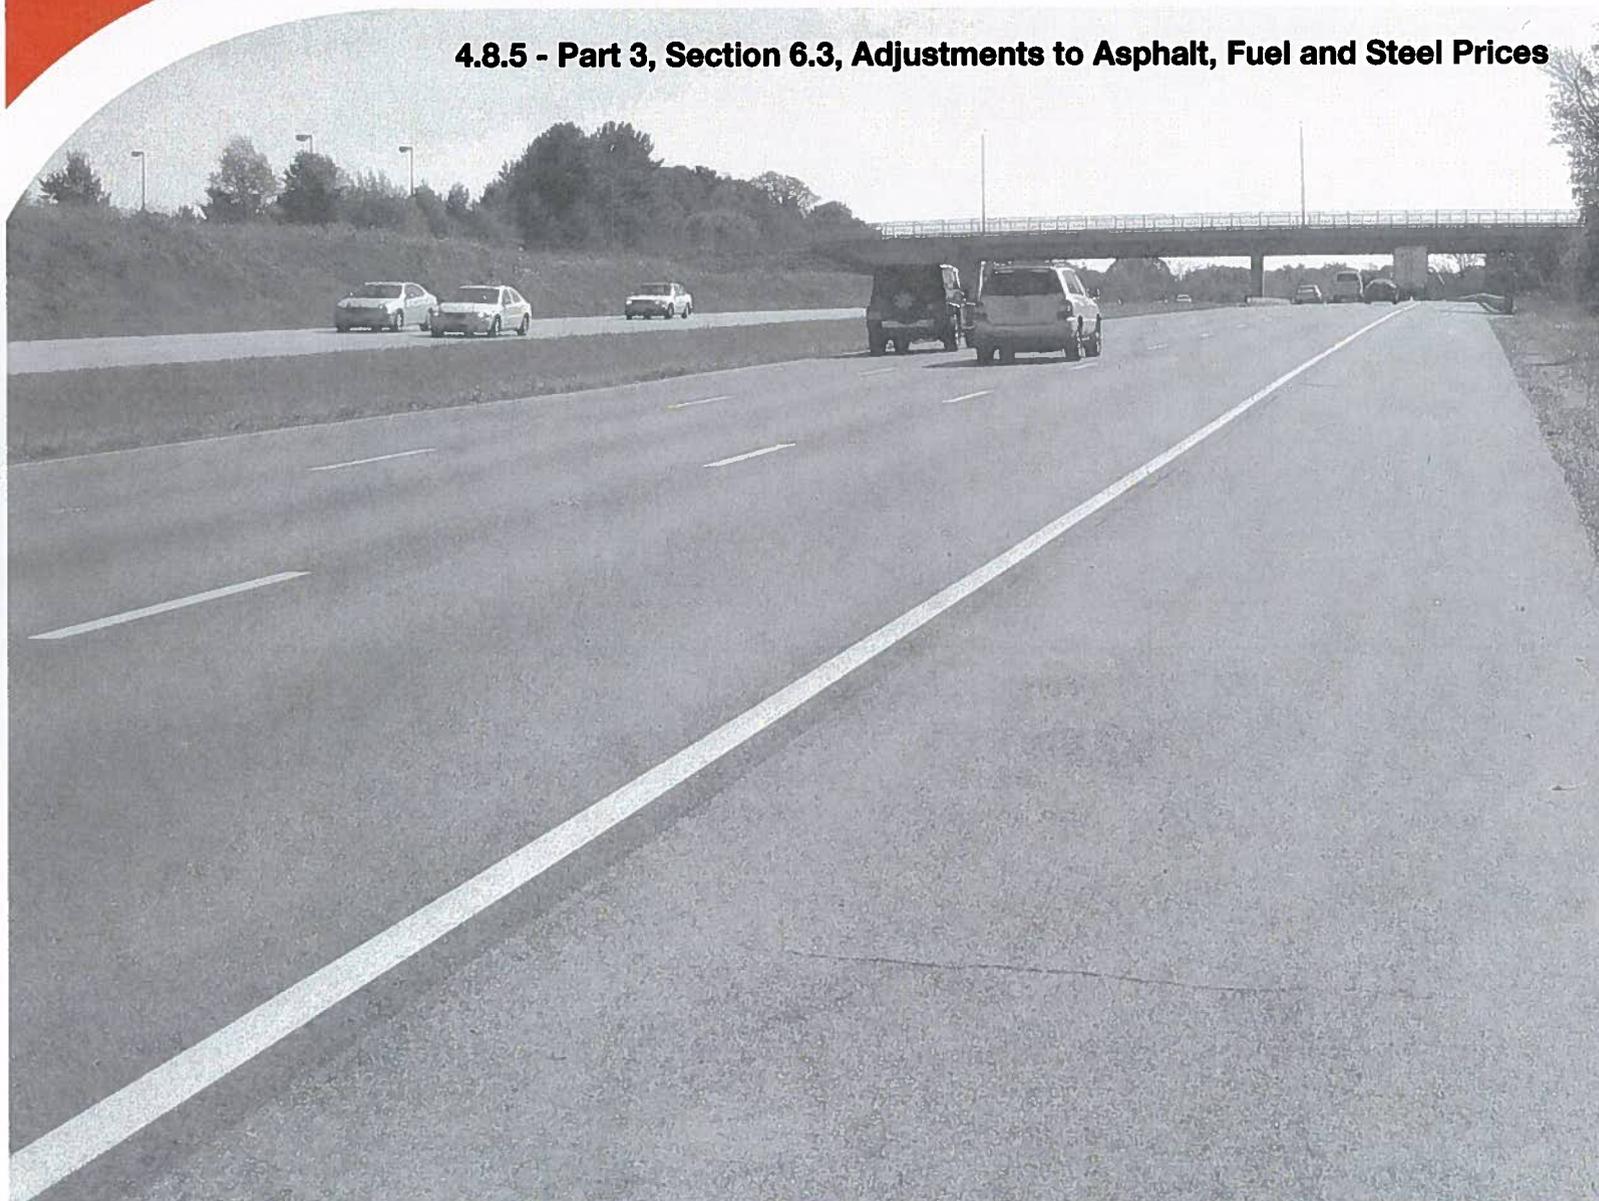
4.8.4 - Proposed Monthly Payment Schedule



The Lane Construction Corporation		I-581 / Valley View Boulevard Interchange Phase II	
90 Fieldstone Court		Project No. 0581-128-109, P101, RW201, C501, 627	
Cheshire, CT 06410		Proposed Monthly Payment Schedule	
		REBID November 7, 2012	
Month	Year	Monthly Draw	Cumulative Draw
January	2013	\$ 848,000	\$ 848,000
February	2013	\$ 1,716,000	\$ 2,564,000
March	2013	\$ 1,528,000	\$ 4,092,000
April	2013	\$ 520,000	\$ 4,612,000
May	2013	\$ 694,000	\$ 5,306,000
June	2013	\$ 1,583,000	\$ 6,889,000
July	2013	\$ 1,628,000	\$ 8,517,000
August	2013	\$ 1,364,000	\$ 9,881,000
September	2013	\$ 2,571,000	\$ 12,452,000
October	2013	\$ 1,266,000	\$ 13,718,000
November	2013	\$ 1,103,000	\$ 14,821,000
December	2013	\$ 2,107,000	\$ 16,928,000
January	2014	\$ 1,018,000	\$ 17,946,000
February	2014	\$ 1,127,000	\$ 19,073,000
March	2014	\$ 1,587,000	\$ 20,660,000
April	2014	\$ 1,595,000	\$ 22,255,000
May	2014	\$ 1,601,000	\$ 23,856,000
June	2014	\$ 772,000	\$ 24,628,000
July	2014	\$ 895,000	\$ 25,523,000
August	2014	\$ 1,156,000	\$ 26,679,000
September	2014	\$ 598,000	\$ 27,277,000
October	2014	\$ 774,000	\$ 28,051,000
November	2014	\$ 502,000	\$ 28,553,000
December	2014	\$ 396,000	\$ 28,949,000
January	2015	\$ 826,000	\$ 29,775,000
February	2015	\$ 675,000	\$ 30,450,000
March	2015	\$ 1,164,000	\$ 31,614,000
April	2015	\$ 1,395,000	\$ 33,009,000
May	2015	\$ 1,524,000	\$ 34,533,000
June	2015	\$ 941,000	\$ 35,474,000
July	2015	\$ 1,008,000	\$ 36,482,000
August	2015	\$ 886,000	\$ 37,368,000
September	2015	\$ 476,000	\$ 37,844,000
October	2015	\$ 84,000	\$ 37,928,000
November	2015	\$ 1,000	\$ 37,929,000
December	2015	\$ 1,000	\$ 37,930,000
January	2016	\$ 1,000	\$ 37,931,000
February	2016	\$ 1,000	\$ 37,932,000
March	2016	\$ 1,000	\$ 37,933,000
April	2016	\$ 249,000	\$ 38,182,000
May	2016	\$ 293,345	\$ 38,475,345
June	2016	\$ -	\$ 38,475,345



4.8.5 - Part 3, Section 6.3, Adjustments to Asphalt, Fuel and Steel Prices




ATTACHMENT 3.6**COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION**RFQ NO. C00016595DB45PROJECT NO.: 0581-128-109, P101, RW201, C501, B627**ACKNOWLEDGEMENT OF RFP, REVISION AND/OR ADDENDA**

Acknowledgement shall be made of receipt of the Request for Proposals (RFP) and/or any and all revisions and/or addenda pertaining to the above designated project which are issued by the Department prior to the Letter of Submittal submission date shown herein. Failure to include this acknowledgement in the Letter of Submittal may result in the rejection of your proposal.

By signing this Attachment 3.6, the Offeror acknowledges receipt of the RFP and/or following revisions and/or addenda to the RFP for the above designated project which were issued under cover letter(s) of the date(s) shown hereon:

1. Cover letter of March 2, 2012 - RFP
(Date)
2. Cover letter of June 21, 2012 - Addendum No. 1
(Date)
3. Cover letter of July 10, 2012 - Addendum No. 2
(Date)
4. E-mail notification October 9, 2012 - Due Date Extension
(Date)


SIGNATURE

November 5, 2012
DATE

Joseph P. Lark
Regional Vice President, Mid-Atlantic Region

PRINTED NAME AND TITLE

The LANE Construction Corporation

**EXHIBIT 6.3(a)
ADJUSTMENT FOR ASPHALT**

**SPECIAL PROVISION FOR
ASPHALT MATERIAL PRICE ADJUSTMENT
DESIGN-BUILD PROJECTS**

June 30, 2011

In the event the Design-Builder elects to seek adjustment for asphalt items designated in the Price Proposal\Contract as Price Adjustment Items such items will be subject to price adjustment as set forth herein. Other items will not be adjusted, except as otherwise specified in the contract. If new pay items which contain Asphalt Material are established by Work Order, they will not be subject to Price Adjustment unless specifically designated in the Work Order to be subject to Price Adjustment.

Each month, the Department will publish an average state-wide PG 64-22 f.o.b. price per ton developed from the average terminal prices provided to the Department from suppliers of asphalt cement to contractors doing work in Virginia. The Department will collect terminal prices from approximately 12 terminals each month. These prices will be received once each month from suppliers on or about the last weekday of the month. The high and low prices will be eliminated and the remaining values averaged to establish the average statewide price for the following month. That monthly state-wide average price will be posted on the Scheduling and Contract Division website on or about the first weekday of the following month.

This monthly statewide average price will be the Base Index for all contracts on which bids are received during the calendar month of its posting and will be the Current Index for all asphalt placed during the calendar month of its posting. In the event an index changes radically from the apparent trend, as determined by the Engineer, the Department may establish an index which is determined to best reflect the trend.

The amount of adjustment applied will be based on the difference between the Price Proposal\Contract Base Index and the Current Index for the applicable calendar month during which the work is performed. Adjustment of any asphalt material item designated as a price adjustment item which does not contain PG 64-22, except PG 76-22, will be based on the indexes for PG 64-22. The quantity of asphalt cement for asphalt concrete pavement to which adjustment will be applied will be the quantity based on the percent of asphalt cement shown on the appropriate approved job mix formula.

The quantity of asphalt emulsion for surface treatments to which adjustment will be applied will be the quantity based on 65 percent residual asphalt.

Price adjustment will be shown as a separate entry on the monthly application of payment for work packages completed; however, such adjustment will not be included in the total cost of the work for progress determination or for extension of contract time.


In order to be eligible for asphalt price adjustment under this provision, the Design-Builder shall clearly identify in its Price Proposal those pay items and the associated quantities it chooses to have asphalt price adjustment applied to in its work packages. Items the Design-Builder claims in its application of payment for asphalt adjustments must be properly designated in order to be considered for adjustment. Items not properly designated or left out of the Design-Builder's Price Proposal will automatically not be considered for adjustment.

Any apparent attempt to unbalance bids in favor of items subject to price adjustment or failure to submit required cost and price data as noted hereinbefore may result in rejection of items for asphalt adjustment.

I elect to use this provision

I elect not to use this provision

Date: November 5, 2012

Signature: 

Design-builder: The LANE Construction Corp.

Vendor No.: L 002

EXHIBIT 6.3(b)

Form C-16a
7-13-05

COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
PRICE ADJUSTMENT

INSTRUCTIONS - This form is to be completed and returned ONLY when asphalt concrete items are designated for price adjustment on the bid price sheets.

PROJECT NUMBER:

DISTRICT:

Bid Prices in this contract for items containing PG 64-22 asphalt cement were developed using an f.o.b. price of \$ 568.33 per **IMPERIAL** ton for **PG 64-22**. This quote will be averaged into the monthly price index.

Bid Prices in this contract for items containing PG 76-22 asphalt cement were developed using an f.o.b. price of \$ 740.00 per **IMPERIAL** ton for **PG 76-22**. This quote is project specific.
(When required by provisions)

Price quotes signed by each supplier from which the Design-Builder proposes to obtain PG 64-22 or PG 76-22 shall be maintained by the successful bidder. These quotes shall be retained on site during the life of the Contract for review by the Engineer upon request.

I elect to use this provision
 I elect not to use this provision

DATE: November 5, 2012

SIGNATURE: 

The LANE Construction Corporation
(Firm or Corporation)

L 002
(Vendor No.)

**EXHIBIT 6.3 (c)
ADJUSTMENT FOR FUEL**

**VIRGINIA DEPARTMENT OF TRANSPORTATION
SPECIAL PROVISION FOR
OPTIONAL ADJUSTMENT FOR FUEL
DESIGN-BUILD PROJECTS**

June 30, 2011

In the event the Design-Builder elects to seek adjustment for fuel items designated in the Price Proposal/Contract as Price Adjustment Items such items will be subject to price adjustment as set forth herein. Other items will not be adjusted, except as otherwise specified in the contract.

The Design-Builder will submit their monthly application for payment associated with eligible work packages with an adjustment up or down as appropriate for cost changes in fuel used on specific items of work identified in this provision. A master listing of standard items eligible for fuel adjustment is provided by the Department on its website at the following link <http://www.virginiadot.org/business/resources/masteroptionalfuelitems.pdf>. The listing on the web site also includes the corresponding fuel factor for each item. The fuel usage factor for each item is considered inclusive of all fuel usage.

The amount of adjustment will be computed from the change in the indexes and the on-site fuel use as shown in the Department's master listing of eligible items.

In order to be eligible for fuel adjustment under this provision, the Design-Builder shall clearly identify in its Price Proposal those pay items and the associated quantities it chooses to have fuel adjustment applied to in its work packages. Items the Design-Builder claims in its application of payment for fuel adjustments must be properly designated in order to be considered for adjustment. Items not properly designated or left out of the Design-Builder's Price Proposal will automatically not be considered for adjustment.

The monthly index price to be used in the administration of this provision will be calculated by the Department from the Diesel fuel prices published by the U. S. Department of Energy, Energy Information Administration on highway diesel prices, for the Lower Atlantic region. The monthly index price will be the price for diesel fuel calculated by averaging each of the weekly posted prices for that particular month.

For the purposes of this provision, the base index price will be calculated using the data from the month preceding the receipt of bids. The base index price will be posted by the Department at the beginning of the month for all bids received during that month.

The current index price will be posted by the Department and will be calculated using the data from the month preceding the particular estimate being vouchered for payment.

The current monthly quantity for eligible items of work selected by the Design-Builder for fuel adjustment in its work packages will be multiplied by the appropriate fuel factor to determine the gallons of fuel to be cost adjusted. The amount of adjustment per gallon will be the net difference between the current index price and the base index price. Computation for adjustment will be made as follows:

$$S = (E - B) QF$$

Where; S = Monetary amount of the adjustment (plus or minus)
B = Base index price
E = Current index price

Q = Quantity of individual units of work
F = Appropriate fuel factor

Adjustments will not be made for work performed beyond the original contract time limit unless the original time limit has been changed by an executed Work Order.

If new pay items are added to this contract by Work Order and they are listed in the Department's master listing of eligible items, the Work Order must indicate which of these individual items will be fuel adjusted; otherwise, those items will not be fuel adjusted. If applicable, designating which new pay items will be added for fuel adjustment must be determined during development of the Work Order and clearly shown on the Work Order form. The Base Index price on any new eligible pay items added by Work Order will be the Base Index price posted for the month in which bids were received for that particular project. The Current Index price for any new eligible pay items added by Work Order will be the Index price posted for the month preceding the estimate on which the Work Order is paid.

When quantities differ between the last monthly application of payment prepared upon final acceptance and the final application of payment, adjustment will be made using the appropriate current index for the period in which that specific item of work was last performed.


In the event any of the base fuel prices in this contract increase more than 100 percent (i.e. fuel prices double), the Department will review each affected item of work and give the Design-Builder written notice if work is to stop on any affected item of work. The Department reserves the right to reduce, eliminate or renegotiate the price for remaining portions of affected items of work.

Any amounts resulting from fuel adjustment will not be included in the total cost of work for determination of progress or for extension of contract time.

I elect to use this provision

I elect not to use this provision

Date: November 5, 2012

Signature: 

Design-builder: The LANE Construction Corp.

Vendor No.: L 002

EXHIBIT 6.3(d)
ADJUSTMENT FOR STEEL

VIRGINIA DEPARTMENT OF TRANSPORTATION
SPECIAL PROVISION FOR
PRICE ADJUSTMENT FOR STEEL
DESIGN-BUILD PROJECTS

June 30, 2011

In the event the Design-Builder elects to seek adjustment for steel items designated in the Price Proposal/Contract as Price Adjustment Items such items will be subject to price adjustment as set forth herein. If new pay items which involve steel are established by Work Order, they will not be subject to Price Adjustment unless specifically designated in the Work Order to be subject to Price Adjustment.

The Design-Builder will submit their monthly application for payment associated with eligible work packages with an adjustment up or down as appropriate for cost changes in steel used on specific items of work identified in the Price Proposal/contract in accordance with this provision. Provided at the end of this provision is a master listing of standard bid items the Department has determined are eligible for steel price adjustment. Inventoried materials from the listing of eligible items are specifically excluded for consideration. In addition, concrete items where reinforcing steel is normally included in the unit bid price for the item such as (but not limited to) drop inlets, median barriers, sound barrier walls, bridge railing and parapets, are not eligible for consideration under this provision.

The requirements of this provision shall apply only to material cost changes that occur between the date of the opening of the Price Proposal and the date the material is shipped to the fabricator. To be eligible for this price adjustment, Design-Builder is required to fill out the accompanying Form for Price Adjustment for Eligible Steel Items on Design-Build Projects and submit the same with its Price Proposal for the Project. By signing the Form and submitting it with its Price Proposal Design-Builder declares its intention to participate in the price adjustment in its contract with the Department. For the purposes of this provision, the prices listed on the Form for Price Adjustment for Eligible Steel Items on Design-Build projects are fixed for cost and adjustment calculations regardless of quantities incorporated into final design. Further, in order for steel items to be eligible for adjustment, once shipped to the fabricator, the items shall be specifically stored, labeled, or tagged, recognizable by color marking, and identifiable by project for inspection and audit verification.

Design-Builder shall upon request furnish documentation supporting the price per pound for eligible steel items as shown on the Form for Price Adjustment for Eligible Steel Items on Design-Build Projects furnished with its Price Proposal. Design-Builder must use the format as shown with this Form; no other format for presenting this information will be permitted. Design-Builder shall certify that all items of documentation are original and were used in the computation of the price per pound amount for the represented eligible pay items for the month the Price Proposal was opened. This documentation shall support the base line material price ("Base Price") of the steel item only. Base price per pound shall not include the following cost components: fabrication, shipping, storage, handling, and erection.

Failure to submit all documentation required or requested supporting the per pound prices on eligible steel items will result in Design-Builder being ineligible for a price adjustment of any or all steel items.

Price adjustment of each qualifying item under consideration will be subject to the following condition:

There is an increase or decrease in the cost of eligible steel materials in excess of 10 percent up to a maximum of 60 percent from the Base Price when compared with the latest published price index ("Price Index") in effect at the time material is shipped to the fabricator.

The Price Index the Department is using is based on The U.S. Department of Labor, Bureau of Labor Statistics, Producers Price Index (PPI) which measures the average price change over time of the specific steel eligible item from the perspective of the seller of goods. The Master List table provided at the end of this provision indicates the Producers Price Index (PPI) steel category index items and the corresponding I.D. numbers to which VDOT items will be compared. **Please note:** The Producers Price Index (PPI) is subject to revision 4 months after original publication, therefore, price adjustments and payments will not be made until the index numbers are finalized.

The price adjustment will be determined by computing the percentage of change in index value beyond 10 percent above or below the index on the date of opening of Design-Builder's Price Proposal to the index value on the date the steel material is shipped to the fabricator (Please see included sample examples). Weights and date of shipment must be documented by a bill of lading provided to the Department. The final price adjustment dollar value will be determined by multiplying this percent increase or decrease in the index (after 10%) by the represented quantity of steel shipped, by the Base Price per pound subject to the limitations herein.

Price increase/decrease will be computed as follows:

$$A = B \times P \times Q$$

- Where;
- A = Steel price adjustment in lump sum dollars
 - B = Average weighted price of steel submitted in Design-Builder's Price Proposal for project in price per pound as listed on the Form for Price Adjustment for Eligible Steel Items on Design-Build Project
 - P = Adjusted percentage change in PPI average from shipping date to date of opening of Price Proposal minus 10% (0.10) threshold
 - Q = Total quantity of steel in pounds shipped to fabricator for specific project

The need for application of the adjustments herein to extra work will be determined by the Engineer on an individual basis and, if appropriate, will be specified on the Work Order.

This price adjustment is capped at 60 percent. This means the maximum "P" value for increase or decrease that can be used in the above equation is 50% (60%-10% threshold).

Calculations for price adjustment shall be shown separate from the monthly progress payment for work packages and will not be included in the total cost of work for determination of progress or for extension of contract time.

Upon Department review and due process consideration for redress by Design-Builder, any apparent evidence to unbalance the price supplied by Design-Builder in favor of items subject to price adjustment will result in ineligibility for Department participation under this provision.

Sample Calculation of a Price Adjustment (increase)

Project bid on April 28, 2004.

Project has 450,000 lb. of eligible structural steel.

Design Builder's *f.o.b. supplier price for structural steel submitted in the Price Proposal is \$0.2816 per pound. *free on board

Adjusted** BLS Producers Price Index (PPI) most recently published average at time of opening of the Price Proposal is 139.6.

All eligible steel shipped to fabricator in same month, October 2004.

Adjusted BLS Producers Price Index (PPI) most recently published average for month of October is 161.1

Adjustment formula is as follows:

$$A = B \times P \times Q$$

- Where;
- A = Steel price adjustment in lump sum dollars
 - B = Average weighted price of steel submitted in the Price Proposal for Design-Build project in \$ per pound
 - P = Adjusted percentage change in PPI average from shipping date to date of submitted Price Proposal minus 10% (0.10) threshold
 - Q = Total quantity of eligible steel shipped to fabricator in October 2004 for this project in pounds

$$B = \$0.2816$$

$$P = (161.1 - 139.6) / 139.6 - 0.10 = 0.054$$

$$Q = 450,000 \text{ lb.}$$

$$A = 0.2816 \times 0.054 \times 450,000$$

$$A = \$6,842.88 \text{ pay adjustment to Design-Builder}$$

Sample Calculation of a Price Adjustment (decrease)

Project bid on April 28, 2004.

Project has 450,000 lb. of eligible structural steel.

Design-Builder's *f.o.b. supplier price for structural steel submitted in the Price Proposal is \$0.2816 per pound.

*free on board

Adjusted BLS Producers Price Index (PPI) most recently published average at time of opening of the Price Proposal is 156.6.

All eligible steel shipped to fabricator in same month, October 2004.

Adjusted BLS Producers Price Index (PPI) most recently published average for month of October is 136.3

Adjustment formula is as follows:

$$A = B \times P \times Q$$

- Where;
- A = Steel price adjustment in lump sum dollars
 - B = Average weighted price of steel submitted in the Price Proposal for Design-Build project in \$ per pound
 - P = Adjusted percentage change in PPI average from shipping date to date of submitted Price Proposal minus 10% (0.10) threshold
 - Q = Total quantity of eligible steel shipped to fabricator in October 2004 for this project in pounds

$$B = \$0.2816$$

$$P = (156.6 - 136.3)/156.6 - 0.10 = 0.030$$

$$Q = 450,000 \text{ lb.}$$

$$A = 0.2816 \times 0.030 \times 450,000$$

$$A = \$3,801.60 \text{ credit to Department}$$

MASTER LISTING

STANDARD BID ITEMS ELIGIBLE FOR STEEL PRICE ADJUSTMENT

March 18, 2009

BLS Series I. D.

ITEM NUMBER	ITEM DESCRIPTION	UNITS	Number WPU used in \$ adjust.
00519	SHEET PILE, STEEL	SF	avg. 1017 & 101
00540	REINF. STEEL	LB	101704
00542	EPOXY COATED REINF. STEEL	LB	101704
00560	STRUCTURAL STEEL JB-1	LB	avg. 1017 & 101
11030	REINF. STEEL BRIDGE APPR. SLAB	LB	101704
11181	PATCH.HYDR.CEM.CONC. PAVE.	SY	101704
13290	GUARDRAIL GR-8 (NCHRP 350 TL-3)	LF	avg. 1017 & 101
13292	GUARDRAIL GR-8A (NCHRP 350 TL-3)	LF	avg. 1017 & 101
13294	GUARDRAIL GR-8B (NCHRP 350 TL-3)	LF	avg. 1017 & 101
13310	GUARDRAIL TERMINAL GR-6 (NCHRP 350)	LF	avg. 1017 & 101
13320	GUARDRAIL GR-2	LF	avg. 1017 & 101
13323	GUARDRAIL GR-2A	LF	avg. 1017 & 101
13331	RAD. GUARDRAIL GR-2	LF	avg. 1017 & 101
13333	RAD. GUARDRAIL GR-2A	LF	avg. 1017 & 101
13335	GUARDRAIL GR-3	LF	avg. 1017 & 101
13341	GUARDRAIL TER. GR-6(WEATHERING STEEL	LF	avg. 1017 & 101
13351	GUARDRAIL GR-8	LF	avg. 1017 & 101
13352	GUARDRAIL GR-8A	LF	avg. 1017 & 101
13353	GUARDRAIL GR-8B	LF	avg. 1017 & 101
13355	GUARDRAIL GR-10	LF	avg. 1017 & 101
13421	MEDIAN BARRIER MB-3	LF	avg. 1017 & 101
13450	MEDIAN BARRIER MB-5	LF	avg. 1017 & 101
13451	MEDIAN BARRIER MB-5A	LF	avg. 1017 & 101
13452	MEDIAN BARRIER MB-5B	LF	avg. 1017 & 101
13545	REINF. STEEL	LB	101704
14502	REINFORCING STEEL	LB	101704
15290	PATCH.CEM.CONC.PAVE.TY.CRCP-A	SY	101704
15302	PATCH.CEM.CONC.PAVE. TY. II	SY	101704
15305	PATCH.CEM.CONC.PAVE.TY. IV-A	SY	101704
17323	GUARDRAIL BEAM *	LF	avg. 1017 & 101
17325	RADIAL GUARDRAIL BEAM *	LF	avg. 1017 & 101
17327	RUB RAIL	LF	avg. 1017 & 101
17353	CABLE GR-3	LF	avg. 1017 & 101
17521	GUARDRAIL BEAM (WEATHERING STEEL)	LF	avg. 1017 & 101
17523	RADIAL GUARDRAIL BEAM (WEATHERING STEEL)	LF	avg. 1017 & 101
17525	RUB RAIL (WEATHERING STEEL)	LF	avg. 1017 & 101
22501	FENCE FE-W1	LF	avg. 1017 & 101
22643	FENCE FE-CL	LF	avg. 1017 & 101
22645	FENCE FE-CL VINYL COATED	LF	avg. 1017 & 101
23043	WATER GATE FE-4 TY.III	LF	avg. 1017 & 101
23501	FENCE FE-W1 (FABRIC ONLY)	LF	avg. 1017 & 101
45522	4" STEEL ENCASE. PIPE	LF	101706
45532	6" STEEL ENCASE. PIPE	LF	101706
45562	16" STEEL ENCASE. PIPE	LF	101706


45572	18" STEEL ENCASE. PIPE	LF	101706
45582	24" STEEL ENCASE. PIPE	LF	101706
45584	24" JACKED STEEL ENCASUREMENT PIPE	LF	101706
45592	30" STEEL ENCASE. PIPE	LF	101706
50402	SIGN POST STEEL 3"	LF	101706
50404	SIGN POST STEEL 4"	LF	101706
50406	SIGN POST STEEL 6"	LF	101706
50410	SIGN POST STEEL 10"	LF	101706
50412	SIGN POST STEEL 12"	LF	101706
50414	SIGN POST STEEL 14"	LF	101706
50416	SIGN POST STEEL 16"	LF	101706
50418	SIGN POST STEEL 18"	LF	101706
51317	SIG. POLE MP-1 20' ONE ARM 30'	EA	101706
51319	SIG. POLE MP-1 20' ONE ARM 32'	EA	101706
51325	SIG. POLE MP-1 20' ONE ARM 38'	EA	101706
51327	SIG. POLE MP-1 20' ONE ARM 40'	EA	101706
51329	SIG. POLE MP-1 20' ONE ARM 42'	EA	101706
51331	SIG. POLE MP-1 20' ONE ARM 44'	EA	101706
51337	SIG. POLE MP-1 20' ONE ARM 50'	EA	101706
51339	SIG. POLE MP-1 20' ONE ARM 52'	EA	101706
51341	SIG. POLE MP-1 20' ONE ARM 54'	EA	101706
51344	SIG. POLE MP-1 20' ONE ARM 56'	EA	101706
51346	SIG. POLE MP-1 20' ONE ARM 58'	EA	101706
51347	SIG. POLE MP-1 20' ONE ARM 60'	EA	101706
51348	SIG. POLE MP-1 20' ONE ARM 62'	EA	101706
51368	SIG.POLE MP-1 20'TWO ARMS 36'& 42'	EA	101706
51400	SIG.POLE MP-1 CO.LU.ONE ARM 38	EA	101706
51402	SIG.POLE MP-1 CO.LU.ONE ARM 40	EA	101706
51408	SIG.POLE MP-1 CO.LU.ONE ARM 46	EA	101706
51412	SIG.POLE MP-1 CO.LU.ONE ARM 50	EA	101706
51414	SIG.POLE MP-1 CO.LU.ONE ARM 52	EA	101706
51416	SIG.POLE MP-1 CO.LU.ONE ARM 54	EA	101706
51418	SIG.POLE MP-1 CO.LU.ONE ARM 56	EA	101706
51420	SIG.POLE MP-1 CO.LU.ONE ARM 58	EA	101706
51422	SIG.POLE MP-1 CO.LU.ONE ARM 60	EA	101706
55162	LIGHTING POLE LP-1 30'-4'	EA	101706
55163	LIGHTING POLE LP-1 30'-6'	EA	101706
55166	LIGHTING POLE LP-1 30'-12'	EA	101706
55169	LIGHTING POLE LP-1 35'-6'	EA	101706
55171	LIGHTING POLE LP-1 35'-10'	EA	101706
55176	LIGHTING POLE LP-1 40'-8'	EA	101706
55185	LIGHTING POLE LP-2 TYPE A	EA	101706
55186	LIGHTING POLE LP-2 TYPE B	EA	101706
55187	LIGHTING POLE LP-2 TYPE C	EA	101706
55188	LIGHTING POLE LP-2 TYPE D	EA	101706
55189	LIGHTING POLE LP-2 TYPE E	EA	101706
55190	LIGHTING POLE LP-2 TYPE F	EA	101706
55192	LIGHTING POLE LP-2 TYPE H	EA	101706
60452	REINF. STEEL BRIDGE APPR. SLAB	LB	101704
61700	REINF. STEEL	LB	101704
61704	CORROSION RESISTANT REINF. STEEL	LB	101704
61705	EPOXY COATED REINF. STEEL	LB	101704
61750	STRUCT.STEEL HIGH STRG.PLT.GIRDERS	LB	avg. 1017 & 101
61811	STR.STEEL PLATE GIRDER ASTM A709 GRADE50	LB	avg. 1017 & 101
61812	STR.STEEL PLATE GIRDER ASTM A709 GRADE50	LB	avg. 1017 & 101
61813	STR.STEEL PLATE GIRDER ASTM A709 GRADEHPS50W	LB	avg. 1017 & 101

61814	STR.STEEL PLATE GIRDER ASTM A709 GRADEHPS70W	LB	avg. 1017 & 101
61820	STR.STEEL ROLLED BEAM ASTM A709 GRADE 36	LB	avg. 1017 & 101
61821	STR.STEEL ROLLED BEAM ASTM A709 GRADE50	LB	avg. 1017 & 101
61822	STR.STEEL ROLLED BEAM ASTM A709 GRADE50W	LB	avg. 1017 & 101
61990	STEEL GRID FLOOR	SF	avg. 1017 & 101
64110	STEEL PILES 10"	LF	avg. 1017 & 101
64112	STEEL PILES 12"	LF	avg. 1017 & 101
64114	STEEL PILES 14"	LF	avg. 1017 & 101
64768	DRIVING TEST FOR 12" STEEL PILE	LF	avg. 1017 & 101
64778	DRIVING TEST FOR 14" STEEL PILE	LF	avg. 1017 & 101
65200	REINF. STEEL	LB	101704
65204	CORROSION RESISTANT REINF. STEEL	LB	101704
65205	EPOXY COATED REINF. STEEL	LB	101704
67086	PED. FENCE 6'	LF	avg. 1017 & 101
67088	PED. FENCE 8'	LF	avg. 1017 & 101
67089	PED. FENCE 10'	LF	avg. 1017 & 101
68100	REINF. STEEL	LB	101704
68104	CORROSION RESISTANT REINF. STEEL	LB	101704
68105	EPOXY COATED REINF. STEEL	LB	101704
68107	STR.STEEL PLATE GIRDER ASTM A709 GRADE50	LB	avg. 1017 & 101
68108	STR. STEEL PLATE GIRDER ASTM A709 GR50W	LB	avg. 1017 & 101
68109	STR. STEEL PLATE GIRDER ASTM A709 GR.HPS50W	LB	avg. 1017 & 101
68110	STR. STEEL PLATE GIRDER ASTM A709 GR.HPS70W	LB	avg. 1017 & 101
68112	STR.STEEL ROLLED BEAM ASTM A709 GR.36	LB	avg. 1017 & 101
68113	STR.STEEL ROLLED BEAM ASTM A709 GR.50	LB	avg. 1017 & 101
68114	STR.STEEL ROLLED BEAM ASTM A709 GR. 50W	LB	avg. 1017 & 101
68115	STRUCT. STEEL	LB	avg. 1017 & 101
68270	REINF. STEEL BRIDGE APPR. SLAB	LB	101704
69060	SHEET PILES, STEEL	SF	avg. 1017 & 101
69100	REINF. STEEL	LB	101704
69104	CORROSION RESISTANT REINF. STEEL	LB	101704
69105	EPOXY COATED REINF. STEEL	LB	101704
69110	STEEL PILES 10"	LF	avg. 1017 & 101
69112	STEEL PILE 12"	LF	avg. 1017 & 101
69113	DRIVING TEST FOR 12" STEEL PILE	LF	avg. 1017 & 101

I elect to use this provision

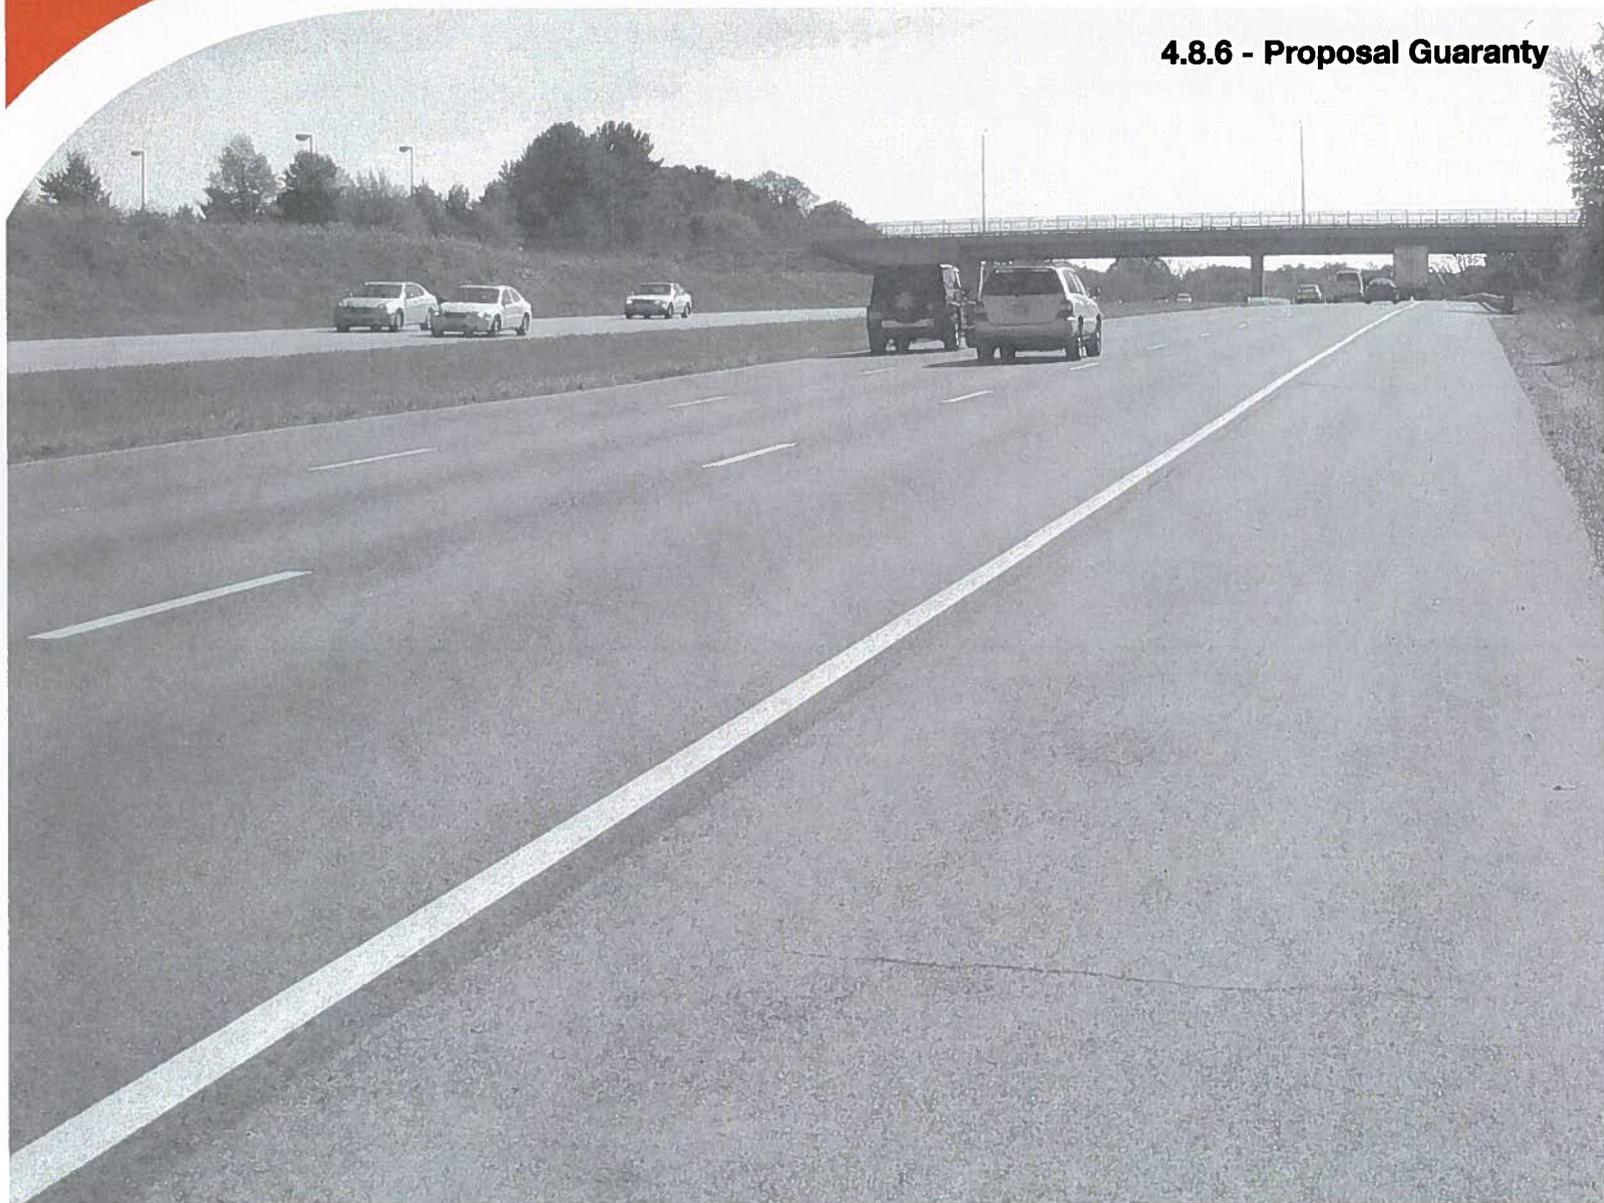
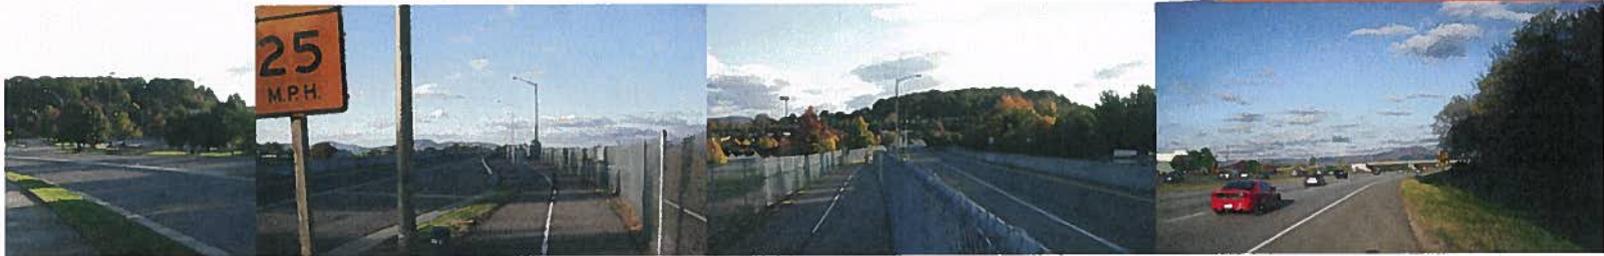
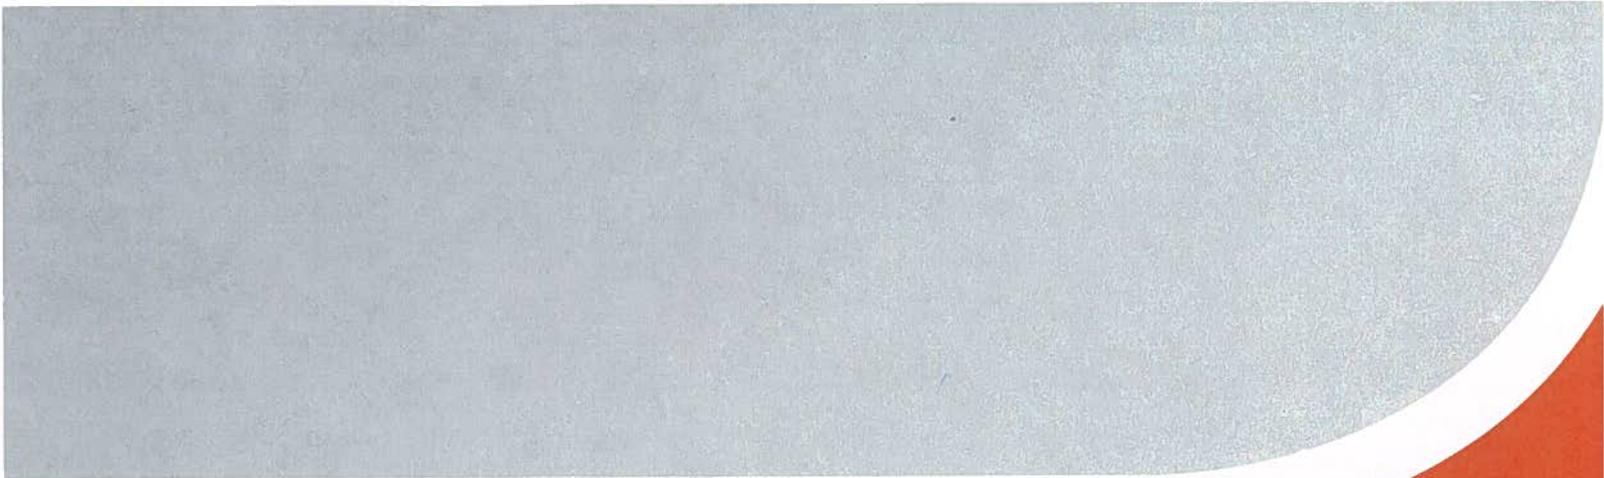
I elect not to use this provision

Date: November 5, 2012

Signature: 

Design-Builder: The LANE Construction Corporation

Vendor No.: L 002



4.8.6 - Proposal Guaranty

COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
PROPOSAL GUARANTY

KNOW ALL MEN BY THESE PRESENTS, THAT WE The Lane Construction Corporation As principal, and Fidelity and Deposit Company of Maryland and Liberty Mutual Insurance Company Surety, are held and firmly bound unto the Commonwealth of Virginia as obligee, in the amount of FIVE PERCENT OF THE DOLLAR VALUE OF THE BID, lawful money of the United States of America, for the payment of which, well and truly to be made, we bind ourselves, our heirs, executors, administrators, successors and assigns, jointly and severally and firmly by these presents.

SIGNED, sealed and dated this 22nd Day of October, 20 12

WHEREAS, the above said principal is herewith submitting its proposal for: I-581 Valley View Boulevard Interchange Phase II
PROJECT NUMBER: Contract ID No.: C00016595DB45 City of Roanoke, VA

NOW, THEREFORE, the condition of the above obligee is such, that if the aforesaid principal shall be awarded the contract upon said proposal and shall within the time specified in the Specifications after the notice of such award enter into a contract and give bond for the faithful performance of the contract, then this obligation shall be null and void; otherwise to remain in full force and effect and the principal and surety will pay unto the obligee the difference in money between the amount of the bid of the said principal and the amount for which the obligee may legally contract with another party to perform the said work if the latter amount be in excess of the former; but in no event shall the liability exceed the penal sum hereof.

The Lane Construction Corporation
(Principal*)

By: JM Ferrell
(Officer, Partner or Owner) (Seal)

JM M. FERRELL
EXEC VICE PRESIDENT
& CFO

By: _____
(Officer, Partner or Owner) (Seal)

(Principal*)

By: _____
(Officer, Partner or Owner) (Seal)

Fidelity and Deposit Company of Maryland
(Surety Company)

By: Theresan E. Rowedder
(Attorney-in-Fact*) (Seal)
Theresan E. Rowedder

1400 American Lane, Schaumburg, IL 60196-1058
(Address)

By: Liberty Mutual Insurance Company
(Surety Company)

Theresan E. Rowedder
(Attorney-in-Fact*) (Seal)
Theresan E. Rowedder

By: 175 Berkeley Street, Boston, MA 02116
(Address)

*Note: If the principal is a *joint venture*, each party thereof must be named and execution made by same hereon. If there is more than one surety to the bid bond, each surety must be named and execution shall be made by same hereon.

Electronic Bid Only: In lieu of completing the above section of the Contract Performance Bond, the Principal shall file an Electronic Bid Bond when bidding electronically. By signing below the Principal is ensuring the identified electronic bid bond has been executed and the Principal and Surety are firmly bound unto the Commonwealth of Virginia under the same conditions of the bid bond as shown above.

Electronic Bid Bond ID# _____ Company/Bidder Name _____ Signature and Title _____

**Attach copy of Power of Attorney

**ZURICH AMERICAN INSURANCE COMPANY
COLONIAL AMERICAN CASUALTY AND SURETY COMPANY
FIDELITY AND DEPOSIT COMPANY OF MARYLAND
POWER OF ATTORNEY**

KNOW ALL MEN BY THESE PRESENTS: That the ZURICH AMERICAN INSURANCE COMPANY, a corporation of the State of New York, the COLONIAL AMERICAN CASUALTY AND SURETY COMPANY, a corporation of the State of Maryland, and the FIDELITY AND DEPOSIT COMPANY OF MARYLAND a corporation of the State of Maryland (herein collectively called the "Companies"), by **THOMAS O. MCCLELLEN, Vice President**, in pursuance of authority granted by Article V, Section 8, of the By-Laws of said Companies, which are set forth on the reverse side hereof and are hereby certified to be in full force and effect on the date hereof, do hereby nominate, constitute, and appoint **Kevin A. WHITE, Mark P. HERENDEEN, Susan M. KEDIAN, Jean CORREIA, Maria CHAVES, Theresan E. ROWEDDER, Jane GILSON and Regina M. MARQUIS**, all of Boston, Massachusetts, EACH its true and lawful agent and Attorney-in-Fact, to make, execute, seal and deliver, for, and on its behalf as surety, and as its act and deed: **any and all bonds and undertakings**, and the execution of such bonds or undertakings in pursuance of these presents, shall be as binding upon said Companies, as fully and amply, to all intents and purposes, as if they had been duly executed and acknowledged by the regularly elected officers of the ZURICH AMERICAN INSURANCE COMPANY at its office in New York, New York., the regularly elected officers of the COLONIAL AMERICAN CASUALTY AND SURETY COMPANY at its office in Owings Mills, Maryland., and the regularly elected officers of the FIDELITY AND DEPOSIT COMPANY OF MARYLAND at its office in Owings Mills, Maryland., in their own proper persons.

The said Vice President does hereby certify that the extract set forth on the reverse side hereof is a true copy of Article V, Section 8, of the By-Laws of said Companies, and is now in force.

IN WITNESS WHEREOF, the said Vice-President has hereunto subscribed his/her names and affixed the Corporate Seals of the said ZURICH AMERICAN INSURANCE COMPANY, COLONIAL AMERICAN CASUALTY AND SURETY COMPANY, and FIDELITY AND DEPOSIT COMPANY OF MARYLAND, this 23rd day of August, A.D. 2012.

ATTEST:

**ZURICH AMERICAN INSURANCE COMPANY
COLONIAL AMERICAN CASUALTY AND SURETY COMPANY
FIDELITY AND DEPOSIT COMPANY OF MARYLAND**



By: *Eric D. Barnes*
Assistant Secretary
Eric D. Barnes

Thomas O. McClellen
Vice President
Thomas O. McClellen

State of Maryland
City of Baltimore

On this 23rd day of August, A.D. 2012, before the subscriber, a Notary Public of the State of Maryland, duly commissioned and qualified, **THOMAS O. MCCLELLEN, Vice President, and ERIC D. BARNES, Assistant Secretary**, of the Companies, to me personally known to be the individuals and officers described in and who executed the preceding instrument, and acknowledged the execution of same, and being by me duly sworn, deposed and saith, that he/she is the said officer of the Company aforesaid, and that the seals affixed to the preceding instrument are the Corporate Seals of said Companies, and that the said Corporate Seals and the signature as such officer were duly affixed and subscribed to the said instrument by the authority and direction of the said Corporations.

IN TESTIMONY WHEREOF, I have hereunto set my hand and affixed my Official Seal the day and year first above written.

Maria D. Adamski
Maria D. Adamski, Notary Public
My Commission Expires: July 8, 2015



EXTRACT FROM BY-LAWS OF THE COMPANIES

"Article V, Section 8, Attorneys-in-Fact. The Chief Executive Officer, the President, or any Executive Vice President or Vice President may, by written instrument under the attested corporate seal, appoint attorneys-in-fact with authority to execute bonds, policies, recognizances, stipulations, undertakings, or other like instruments on behalf of the Company, and may authorize any officer or any such attorney-in-fact to affix the corporate seal thereto; and may with or without cause modify or revoke any such appointment or authority at any time."

CERTIFICATE

I, the undersigned, Vice President of the ZURICH AMERICAN INSURANCE COMPANY, the COLONIAL AMERICAN CASUALTY AND SURETY COMPANY, and the FIDELITY AND DEPOSIT COMPANY OF MARYLAND, do hereby certify that the foregoing Power of Attorney is still in full force and effect on the date of this certificate; and I do further certify that Article V, Section 8, of the By-Laws of the Companies is still in force.

This Power of Attorney and Certificate may be signed by facsimile under and by authority of the following resolution of the Board of Directors of the ZURICH AMERICAN INSURANCE COMPANY at a meeting duly called and held on the 15th day of December 1998.

RESOLVED: "That the signature of the President or a Vice President and the attesting signature of a Secretary or an Assistant Secretary and the Seal of the Company may be affixed by facsimile on any Power of Attorney...Any such Power or any certificate thereof bearing such facsimile signature and seal shall be valid and binding on the Company."

This Power of Attorney and Certificate may be signed by facsimile under and by authority of the following resolution of the Board of Directors of the COLONIAL AMERICAN CASUALTY AND SURETY COMPANY at a meeting duly called and held on the 5th day of May, 1994, and the following resolution of the Board of Directors of the FIDELITY AND DEPOSIT COMPANY OF MARYLAND at a meeting duly called and held on the 10th day of May, 1990.

RESOLVED: "That the facsimile or mechanically reproduced seal of the company and facsimile or mechanically reproduced signature of any Vice-President, Secretary, or Assistant Secretary of the Company, whether made heretofore or hereafter, wherever appearing upon a certified copy of any power of attorney issued by the Company, shall be valid and binding upon the Company with the same force and effect as though manually affixed.

IN TESTIMONY WHEREOF, I have hereunto subscribed my name and affixed the corporate seals of the said Companies, this 20th day of OCTOBER, 2012.



Geoffrey Delisio

Geoffrey Delisio, Vice President

THIS POWER OF ATTORNEY IS NOT VALID UNLESS IT IS PRINTED ON RED BACKGROUND.

This Power of Attorney limits the acts of those named herein, and they have no authority to bind the Company except in the manner and to the extent herein stated.

5400233

Certificate No. _____

American Fire and Casualty Company
The Ohio Casualty Insurance Company
West American Insurance Company

Liberty Mutual Insurance Company
Peerless Insurance Company

POWER OF ATTORNEY

KNOWN ALL PERSONS BY THESE PRESENTS: That American Fire & Casualty Company and The Ohio Casualty Insurance Company are corporations duly organized under the laws of the State of Ohio, that Liberty Mutual Insurance Company is a corporation duly organized under the laws of the State of Massachusetts, that Peerless Insurance Company is a corporation duly organized under the laws of the State of New Hampshire, and West American Insurance Company is a corporation duly organized under the laws of the State of Indiana (herein collectively called the "Companies"), pursuant to and by authority herein set forth, does hereby name, constitute and appoint, **JEAN M. FEENEY, KEVIN A. WHITE, MARK P. HERENDEEN, SUSAN M. KEDIAN, JEAN CORREIA, MARIA CHAVES, BRIAN DRISCOLL, THERESAN E. ROWEDDER, JANE GILSON,**

all of the city of BOSTON, state of MASSACHUSETTS each individually if there be more than one named, its true and lawful attorney-in-fact to make, execute, seal, acknowledge and deliver, for and on its behalf as surety and as its act and deed, any and all undertakings, bonds, recognizances and other surety obligations, in pursuance of these presents and shall be as binding upon the Companies as if they have been duly signed by the president and attested by the secretary of the Companies in their own proper persons.

IN WITNESS WHEREOF, this Power of Attorney has been subscribed by an authorized officer or official of the Companies and the corporate seals of the Companies have been affixed thereto this 23rd day of MAY, 2012.




American Fire and Casualty Company
The Ohio Casualty Insurance Company
Liberty Mutual Insurance Company
Peerless Insurance Company
West American Insurance Company

By: Gregory W. Davenport
Gregory W. Davenport, Assistant Secretary

STATE OF WASHINGTON ss
COUNTY OF KING

On this 23rd day of MAY, 2012, before me personally appeared Gregory W. Davenport, who acknowledged himself to be the Assistant Secretary of American Fire and Casualty Company, Liberty Mutual Insurance Company, The Ohio Casualty Insurance Company, Peerless Insurance Company and West American Insurance Company, and that he, as such, being authorized so to do, execute the foregoing instrument for the purposes therein contained by signing on behalf of the corporations by himself as a duly authorized officer.

IN WITNESS WHEREOF, I have hereunto subscribed my name and affixed my notarial seal at Seattle, Washington, on the day and year first above written.



By: KD Riley
KD Riley, Notary Public

This Power of Attorney is made and executed pursuant to and by authority of the following By-laws and Authorizations of American Fire and Casualty Company, The Ohio Casualty Insurance Company, Liberty Mutual Insurance Company, West American Insurance Company and Peerless Insurance Company, which resolutions are now in full force and effect reading as follows:

ARTICLE IV – OFFICERS – Section 12. Power of Attorney. Any officer or other official of the Corporation authorized for that purpose in writing by the Chairman or the President, and subject to such limitation as the Chairman or the President may prescribe, shall appoint such attorneys-in-fact, as may be necessary to act in behalf of the Corporation to make, execute, seal, acknowledge and deliver as surety any and all undertakings, bonds, recognizances and other surety obligations. Such attorneys-in-fact, subject to the limitations set forth in their respective powers of attorney, shall have full power to bind the Corporation by their signature and execution of any such instruments and to attach thereto the seal of the Corporation. When so executed, such instruments shall be as binding as if signed by the President and attested to by the Secretary. Any power or authority granted to any representative or attorney-in-fact under the provisions of this article may be revoked at any time by the Board, the Chairman, the President or by the officer or officers granting such power or authority.

ARTICLE XIII – Execution of Contracts – SECTION 5. Surety Bonds and Undertakings. Any officer of the Company authorized for that purpose in writing by the chairman or the president, and subject to such limitations as the chairman or the president may prescribe, shall appoint such attorneys-in-fact, as may be necessary to act in behalf of the Company to make, execute, seal, acknowledge and deliver as surety any and all undertakings, bonds, recognizances and other surety obligations. Such attorneys-in-fact subject to the limitations set forth in their respective powers of attorney, shall have full power to bind the Company by their signature and execution of any such instruments and to attach thereto the seal of the Company. When so executed such instruments shall be as binding as if signed by the president and attested by the secretary.

Certificate of Designation – The President of the Company, acting pursuant to the Bylaws of the Company, authorizes Gregory W. Davenport, Assistant Secretary to appoint such attorney-in-fact as may be necessary to act on behalf of the Company to make, execute, seal, acknowledge and deliver as surety any and all undertakings, bonds, recognizances and other surety obligations.

Authorization – By unanimous consent of the Company's Board of Directors, the Company consents that facsimile or mechanically reproduced signature of any assistant secretary of the Company, wherever appearing upon a certified copy of any power of attorney issued by the Company in connection with surety bonds, shall be valid and binding upon the Company with the same force and effect as though manually affixed.

I, David M. Carey, the undersigned, Assistant Secretary, of American Fire and Casualty Company, The Ohio Casualty Insurance Company, Liberty Mutual Insurance Company, West American Insurance Company and Peerless Insurance Company do hereby certify that the original power of attorney of which the foregoing is a full, true and correct copy of the Power of Attorney executed by said Companies, is in full force and effect and has not been revoked.

IN TESTIMONY WHEREOF, I have hereunto set my hand and affixed the seals of said Companies this 22nd day of October, 2012.



By: David M. Carey
David M. Carey, Assistant Secretary

Not valid for mortgage, note, loan, letter of credit, bank deposit, currency rate, interest rate or residual value guarantees.

To confirm the validity of this Power of Attorney call 1-610-832-8240 between 9:00 am and 4:30 pm EST on any business day.



90 Fieldstone Court
 Cheshire, CT 06410-1212
 203-235-3351
 203-237-4260 Fax
www.laneconstruct.com

Resolution unanimously approved by the Board of Directors of The Lane Construction Corporation effective August 23, 2012:

VOTED: That effective August 23, 2012, rescinding all previous authorizations, the following be and hereby are authorized to sign proposals and bid bonds on behalf of this Corporation:

- R. E. Alger, President & Chief Executive Officer
- D. P. Dobbs, Executive Vice President Administration & Secretary
- J. M. Ferrell, Executive Vice President & Chief Financial Officer
- K. D. Junco, Chief Operating Officer & Executive Vice President
- M. M. Cote, Executive Vice President, Northern Division
- D. F. Benton, Executive Vice President, Southern Division
- J. S. Cruickshank, Executive Vice President & General Counsel
- V. J. Caiola, Vice President, CIO, Treasurer & Assistant Secretary
- A. M. Falsey, Tax Director, Assistant Treasurer & Assistant Secretary
- T. R. Larson, Assistant Vice President Engineering
- J. O. Hughes, Regional Vice President Southeast Region & Assistant Secretary
- L. G. Hurley, Regional Vice President South Central Region & Assistant Secretary
- J. P. Lark, Regional Vice President Mid-Atlantic Region & Assistant Secretary
- S. A. Leach, Regional Vice President Northeast Region & Assistant Secretary
- D. J. Rankin, Regional Vice President Mid-South Region & Assistant Secretary
- M. A. Schiller, Regional District Manager
- M. R. Hindt, Regional District Manager
- R. A. Bean, District Manager
- M. C. Cuilik, District Manager
- H. D. Fletcher, District Manager
- D. W. Grey, District Manager
- G. A. Hassfurter, District Manager
- G. F. Jerabek, District Manager
- R. P. Lane, District Manager
- D. A. Luzier, District Manager
- R. A. McDonough, District Manager
- J. P. McLear, District Manager
- D. S. Mason, Jr., District Manager
- D. B. O'Connor, District Manager
- K. K. Prince, District Manager
- H. W. Reitz, District Manager
- R. E. Spencer, District Manager
- C. M. Curran, Assistant District Manager
- C. E. DuBois, Assistant District Manager
- P. J. Paul, Assistant District Manager
- D. J. Phillips, Assistant District Manager
- E. G. Ritchie, Assistant District Manager
- R. Burton, Senior Plant Manager
- D. A. Hoyt, Senior Plant Manager
- J. F. Roddy, Project Manager

I hereby certify that the above is a true copy of the Resolution unanimously approved by the Board of Directors of The Lane Construction Corporation effective August 23, 2012, and that the above vote has not been rescinded and stands in full force and effect as of this date.

October 23, 2012

Date

THE LANE CONSTRUCTION CORPORATION

Vincent J. Caiola

Assistant Secretary

State of Connecticut
 County of New Haven

October 23, 2012

Date

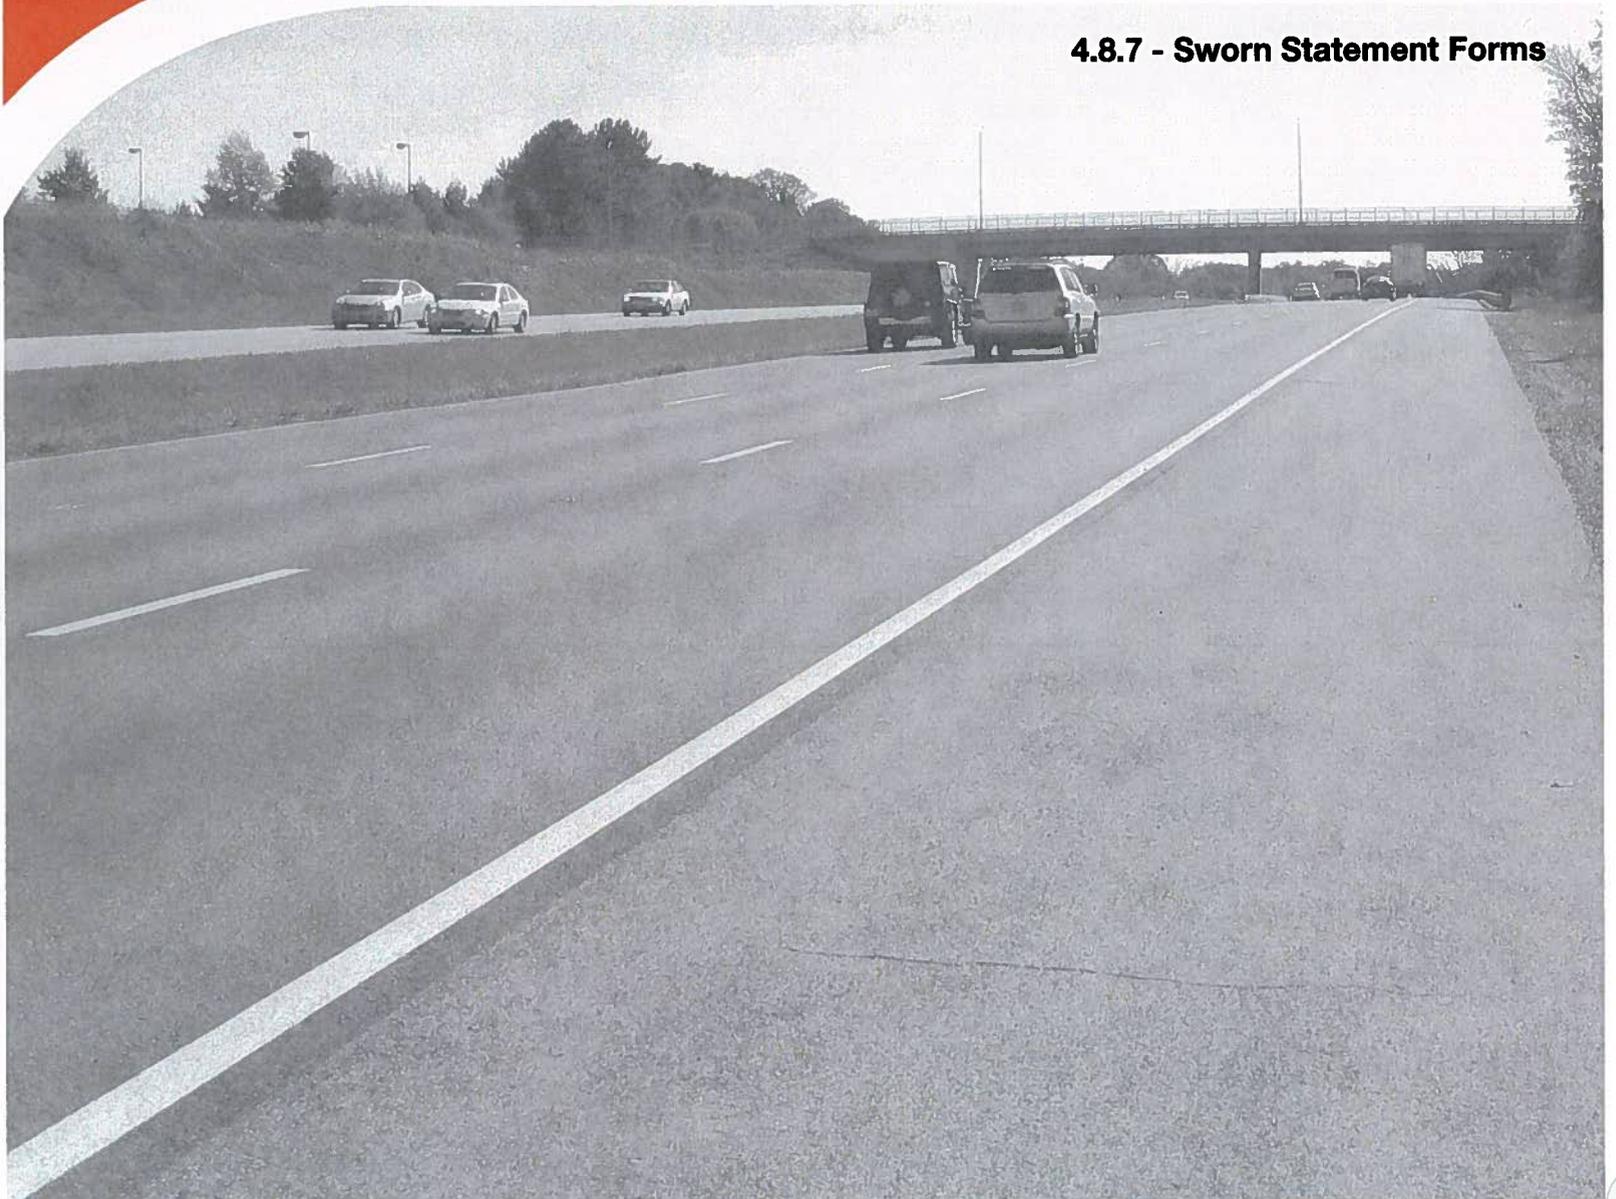
Personally appeared before me, Vincent J. Caiola, Assistant Secretary, and made oath that the above is a true copy of the minutes of the Board of Directors of The Lane Construction Corporation.

Patricia A. Deleka

Patricia A. Deleka, Notary Public
 My Commission Expires July 31, 2014



4.8.7 - Sworn Statement Forms



**COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION**

PROJECT: 0581-128-109, P101, RW201, C501, B627

FHWA: NH-581-5 (035)

This form must be completed, signed and returned with bid; and failure to do so may result in the rejection of your bid. **THE CONTRACTOR SHALL AFFIRM THE FOLLOWING STATEMENT EITHER BY SIGNING THE AFFIDAVIT AND HAVING IT NOTARIZED OR BY SIGNING THE UNSWORN DECLARATION UNDER PENALTY OF PERJURY UNDER THE LAWS OF THE UNITED STATES. A SEPARATE FORM MUST BE SUBMITTED BY EACH PRINCIPAL OF A JOINT VENTURE BID.**

STATEMENT. In preparation and submission of this bid, I, the firm, corporation or officers, agents or employees thereof did not, either directly or indirectly, enter into any combination or arrangement with any persons, firm or corporation or enter into any agreement, participate in any collusion, or otherwise take any action in the restraint of free, competitive bidding in violation of the Sherman Act (15 U.S.C. Section 1) or Article 1.1 or Chapter 12 of Title 18.2 (Virginia Governmental Frauds Act), Sections 59.1-9.1 through 59.1-9.17 or Sections 59.1-68.6 through 59.1-68.8 of the Code of Virginia.

AFFIDAVIT

The undersigned is duly authorized by the bidder to make the foregoing statement to be filed with bids submitted on behalf of the bidder for contracts to be let by the Commonwealth Transportation Board.

Signed at Fairfax (Chantilly), Virginia, this 5th day of November, 20 12
County (City), STATE
The LANE Construction Corporation By: [Signature] Regional Vice President,
(Name of Firm) (Signature) Mid-Atlantic Region
STATE of Virginia COUNTY (CITY) of Fairfax (Chantilly)
To-wit:

I Michael L. Howes, a Notary Public in and for the State and County(City) aforesaid, hereby certify that this day Joseph P. Lark

personally appeared before me and made oath that he is duly authorized to make the above statements and that such statements are true and correct.


Subscribed and sworn to before me this 5th day of November, 20 12
[Signature] My Commission expires May 31, 2016
Notary Public

**OR
UNSWORN DECLARATION**

The undersigned is duly authorized by the bidder to make the foregoing statement to be filed with bids submitted on behalf of the bidder for contracts to be let by the Commonwealth Transportation Board.

Signed at _____, this _____ day of _____, 20 ____
County (City), STATE

(Name of Firm) By: _____ (Signature) _____ Title (print)



COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
AFFIDAVIT

PROJECT: 0581-128-109, P101, RW201, C501, B627

FHWA: NH-581-5 (035)

This form must be completed, signed, notarized and returned with bid; and failure to do so, may result in the rejection of your bid. A separate form must be submitted by each principal of a joint venture bid.

1. I, the firm, corporation or officers, agents or employees thereof have neither directly nor indirectly entered into any combination or arrangement with any person, firm or corporation or entered into any agreement, participated in any collusion, or otherwise taken any action in restraint of free competitive bidding in connection with such contract, the effect of which is to prevent competition or increase the cost of construction or maintenance of roads or bridges.

During the preceding twelve months, I (we) have been a member of the following Highway Contractor's Associations, as defined in Section 33.1-336 of the Code of Virginia (1970). (If none, so state).

NAME	Location of Principal Office
<u>VTCA</u>	<u>Richmond, VA</u>
<u>ARTBA</u>	<u>Washington, D.C.</u>
<u>AGC of America</u>	<u>Washington, D.C.</u>

2. I (we) have , have not , participated in a previous contract or subcontract subject to the equal opportunity clause, as required by Executive Orders 10925, 11114, or 11246, and that I/We have , have not , filed with the joint Reporting Committee, the Director of the Office of Federal Contract Compliance, a Federal Government contracting or administering agency, or the former President's Committee on Equal Employment Opportunity, all reports due under the applicable filing requirements.

Note: The above certification is required by the Equal Employment Opportunity Regulations of the Secretary of Labor [41 CFR 60-1.7(b)(1)], and must be submitted by bidders and proposed subcontractors only in connection with contracts and subcontracts which are subject to the equal opportunity clause. Contracts and subcontracts which are exempt from the equal opportunity clause are set forth in 41 CFR 60-1.5. (Generally only contract or subcontracts of \$10,000 or under are exempt.)

Currently, Standard Form 100 (EEO-1) is the only report required by the Executive Orders or their implementing regulations.

Proposed prime contractors and subcontractors who have participated in a previous contract or subcontract subject to the Executive Orders and have not filed the required reports should note that 41 CFR 60-1.7(b) (1) prevents the award of contract and subcontract unless such contractor submits a report covering the delinquent period or such other period specified by the Federal Highway Administration or by the Director, Office of Federal Contract Compliance, U.S. Department of Labor.

(Continued)

ORDER NO.:
CONTRACT ID. NO.:

Form C-105
page 2

3. The bidder certifies to the best of its knowledge and belief, that it and its principals:
- (a) Are not presently debarred, suspended, proposed for debarment, declared ineligible or voluntarily excluded from covered transactions by any Federal department or agency;
 - (b) Have not within a three year period preceding this proposal been convicted of or had a civil judgement rendered against them for commission of fraud or a criminal offence in connection with obtaining, attempting to obtain, or performing a public (Federal, State or local) transaction or contract under a public transaction; violation of Federal or State antitrust statutes or commission of embezzlement, theft, forgery, bribery, falsification or destruction of records, making false statements, or receiving stolen property;
 - (c) Are not presently indicted for or otherwise criminally or civilly charged by a governmental entity (Federal, State or local) with commission of any of the offenses enumerated above; and
 - (d) Where the bidders is unable to certify to any of the statements in this certification, the bidder shall show an explanation below.

Explanations will not necessarily result in denial of award, but will be considered in determining bidder responsibility. For any explanation noted, indicate below to whom it applies, initiating agency, and dates of action. Providing false information may result in federal criminal prosecution or administration sanctions. The bidder shall provide immediate written notice to the Department if at any time the bidder learns that its certification was erroneous when submitted or has become erroneous by reason of change circumstances.

The undersigned is duly authorized by the bidder to make the foregoing statements to be filed with bids submitted on behalf of the bidder for contracts to be let by the Commonwealth Transportation Board.


Signed at Fairfax (Chantilly), Virginia, this 5th day of November, 20 12
County (City), STATE
The LANE Construction Corporation By: *Joseph P. Lark* Regional Vice President,
(Name of Firm) (Signature) Mid-Atlantic Region
STATE of Virginia COUNTY (CITY) of Fairfax (Chantilly)
To-wit:

I Michael L. Howes, a Notary Public in and for the State and
County(City) aforesaid, hereby certify that this day Joseph P. Lark

personally appeared before me and made oath that he is duly authorized to make the above statements and that such statements are true and correct.

Subscribed and sworn to before me this 5th day of November, 20 12
Michael L. Howes My Commission expires May 31, 2016

Notary Public



4.8.8 - Minimum DBE Requirements Form, and/or DBE Good Faith Effort Documentation Form, and Certification of Binding Agreement Form



**COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
MINIMUM DBE REQUIREMENTS**

PROJECT NO. 0581-128-109, P101, RW201, C501, B627

FHWA NO. NH-581-5 (035)

***** INSTRUCTIONS *****

THIS FORM CAN BE USED BY THE CONTRACTOR TO SUBMIT THE NAMES OF DBE FIRMS TO BE UTILIZED ON THE PROJECT. THE CONTRACTOR SHALL INDICATE THE DESCRIPTION OF THE CATEGORY (S, M, SP or H) AND THE TYPE OF WORK THAT EACH DBE WILL PERFORM AND THE ALLOWABLE CREDIT PER ITEM(S). ADDITIONAL SHEETS TO SHOW THE ALLOWABLE CREDIT PER ITEM MAY BE ATTACHED IF NECESSARY. **PLEASE NOTE:** THE AMOUNT OF ALLOWABLE CREDIT FOR A DBE SUPPLIER IS 60% OF THE TOTAL COST OF THE MATERIALS OR SUPPLIES OBTAINED AND 100% FOR A DBE MANUFACTURER OF THE MATERIALS AND SUPPLIES OBTAINED. A CONTRACTOR MAY COUNT 100% OF THE FEES PAID TO A DBE HAULER FOR THE DELIVERY OF MATERIALS AND SUPPLIES TO THE PROJECT SITE, BUT NOT FOR THE COST OF THE MATERIALS AND SUPPLIES THEMSELVES.

DBE REQUIREMENT 16 %

PERCENT ATTAINED BY BIDDER 16.0 %

NAMES(S) AND CERTIFICATION NO. OF DBE(S) TO BE USED	USED AS SUBCONTR. (S) MFG. (M) SUPPLIER (SP) HAULER (H)	TYPE OF WORK AND ITEM NO(S)	\$ AMOUNT OF ALLOWABLE CREDIT PER ITEM
<u>See attached listing</u>			

TOTAL \$ 6,156,392.00

TOTAL CONTRACT VALUE \$ 38,475,345.00 x REQUIRED DBE 16.0 % = \$ 6,156,055.00

I/WE CERTIFY THAT THE PROPOSED DBE(S) SUBMITTED WILL BE USED ON THIS CONTRACT AS STATED HEREON AND ASSURE THAT DURING THE LIFE OF THE CONTRACT. I/WE WILL MEET OR EXCEED THE PARTICIPATION ESTABLISHED HEREON BY THE DEPARTMENT.

The LANE Construction Corporation
BIDDER

BY
SIGNATURE

Regional V. P. Mid Atlantic Region
TITLE

BY November 5, 2012
DATE

The LANE Construction Corporation		I-581 / Valley View Boulevard Interchange Phase II		
90 Fieldstone Court		City of Roanoke, VA		
Cheshire, CT 06410		Project No. 0581-128-109, P101, RW201, C501, 627		
		Contract ID Number C00016595DB45		
		DBE Program		
Total Contract Value:	\$ 38,475,345	Attachment to C-111		
DBE Firm	Certification No.	Type of Work	Percent of Work	Amount of Allowable Credit
A&P Services, LLC	650392	Guardrail	0.6%	\$ 239,000
Sandra's Marking Co.	626529	Pavement Markings	1.0%	\$ 368,500
NXL Construction Services, Inc.	626437	Quality Assurance	3.9%	\$ 1,500,000
Thomas L. Brown Associates	MWAA Certified	Geotechnical Exploration & Engineering	1.0%	\$ 397,060
Accompong Engineering Group LLC	678765	Traffic Engineering	0.1%	\$ 50,000
DMY Inc.	687645	Pavement Design	0.0%	\$ 8,834
Mercado Consultants, Inc.	MWAA Certified	Sound Wall Design; Structural Engineering	0.2%	\$ 62,988
Cherry Contracting	MWAA Certified	Sound Walls	9.2%	\$ 3,530,000
			16.0%	\$ 6,156,382

COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
CERTIFICATION OF BINDING AGREEMENT
WITH
DISADVANTAGED BUSINESS ENTERPRISE FIRMS

Project No.: 0581-128-109, P101, RW201, C501, B627

Federal Project No.: NH-581-5 (035)

This form is to be submitted in accordance with the Department's Special Provision for Section 107.15.

It is hereby certified by the below signed Contractors that there exists a written quote, acceptable to the parties involved preliminary to a binding subcontract agreement stating the details concerning the work to be performed and the price which will be paid for the aforementioned work. This document is not intended to, nor should it be construed to, contain the entire text of the agreement between the contracting parties. This document does not take the place of, nor may it be substituted for, an official subcontracting agreement in those situations that may require such an agreement. A copy of the fully executed *subcontract agreement* shall be submitted to the Engineer within fourteen (14) business days after contract execution.


It is further certified that the aforementioned mutually acceptable quote and fully executed subcontract agreement represent the entire agreement between the parties involved and that no conversations, verbal agreements, or other forms of non-written representations shall serve to add to, delete, or modify the terms as stated.

The prime Contractor further represents that the aforementioned mutually acceptable quote and fully executed subcontract agreement shall remain on file for a period of not less than one year following completion of the prime's contract with the Department or for such longer period as provisions of governing Federal or State law or regulations may require. For purposes of this form, the term Prime Contractor shall refer to any Contractor utilizing a DBE subcontractor, regardless of tier, in which they are claiming DBE credit toward the contract goal.

Contractors further jointly and severally represent that said binding agreement is for the performance of a "commercially useful function" as that term is employed in 49 C.F.R. Part 26.55 (c), (d).

**TO BE SIGNED BY THE SUBCONTRACTOR TO THE PRIME CONTRACTOR, AND ANY LOWER TIER
SUBCONTRACTORS HAVING A CONTRACT WITH THE BELOW NAMED DBE FIRM**

Prime Contractor The LANE Construction Corporation

By: 
Signature

Regional V. P. Mid Atlantic Region
Title

Date: August 20, 2012

First Tier
Subcontractor if
Applicable

By: _____
Signature

Title

Date: _____

Second Tier
Subcontractor if
Applicable

By: _____
Signature Title
Date: _____

Third Tier
Subcontractor if
Applicable

By: _____
Signature Title
Date: _____

DBE Contractor

A.P. SERVICES, LLC

By:  _____
Signature Title
Date: 8-15-2012

CHIEF EXEC. MANAGER
Title

COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
CERTIFICATION OF BINDING AGREEMENT
WITH
DISADVANTAGED BUSINESS ENTERPRISE FIRMS

Project No.: 0581-128-109, P101, RW201, C501, B627

Federal Project No.: NH-581-5 (035)

This form is to be submitted in accordance with the Department's Special Provision for Section 107.15.

It is hereby certified by the below signed Contractors that there exists a written quote, acceptable to the parties involved preliminary to a binding subcontract agreement stating the details concerning the work to be performed and the price which will be paid for the aforementioned work. This document is not intended to, nor should it be construed to, contain the entire text of the agreement between the contracting parties. This document does not take the place of, nor may it be substituted for, an official subcontracting agreement in those situations that may require such an agreement. A copy of the fully executed *subcontract agreement* shall be submitted to the Engineer within fourteen (14) business days after contract execution.


It is further certified that the aforementioned mutually acceptable quote and fully executed subcontract agreement represent the entire agreement between the parties involved and that no conversations, verbal agreements, or other forms of non-written representations shall serve to add to, delete, or modify the terms as stated.

The prime Contractor further represents that the aforementioned mutually acceptable quote and fully executed subcontract agreement shall remain on file for a period of not less than one year following completion of the prime's contract with the Department or for such longer period as provisions of governing Federal or State law or regulations may require. For purposes of this form, the term Prime Contractor shall refer to any Contractor utilizing a DBE subcontractor, regardless of tier, in which they are claiming DBE credit toward the contract goal.

Contractors further jointly and severally represent that said binding agreement is for the performance of a "commercially useful function" as that term is employed in 49 C.F.R. Part 26.55 (c), (d).

**TO BE SIGNED BY THE SUBCONTRACTOR TO THE PRIME CONTRACTOR, AND ANY LOWER TIER
SUBCONTRACTORS HAVING A CONTRACT WITH THE BELOW NAMED DBE FIRM**

Prime Contractor The LANE Construction Corporation

By: 
Signature

Regional V. P. Mid Atlantic Region

Title

Date: August 20, 2012

First Tier
Subcontractor if
Applicable

By: _____
Signature

Title

Date: _____

Second Tier
Subcontractor if
Applicable

By: _____ Signature _____ Title
Date: _____

Third Tier
Subcontractor if
Applicable

By: _____ Signature _____ Title
Date: _____

DBE Contractor

Sandys Parking Co Inc
By: *Sandy Sullivan* Signature *President* Title
Date: *8-15-12*

COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
CERTIFICATION OF BINDING AGREEMENT
WITH
DISADVANTAGED BUSINESS ENTERPRISE FIRMS

Project No.: 0581-128-109, P101, RW201, C501, B627

Federal Project No.: NH-581-5 (035)

This form is to be submitted in accordance with the Department's Special Provision for Section 107.15.

It is hereby certified by the below signed Contractors that there exists a written quote, acceptable to the parties involved preliminary to a binding subcontract agreement stating the details concerning the work to be performed and the price which will be paid for the aforementioned work. This document is not intended to, nor should it be construed to, contain the entire text of the agreement between the contracting parties. This document does not take the place of, nor may it be substituted for, an official subcontracting agreement in those situations that may require such an agreement. A copy of the fully executed *subcontract agreement* shall be submitted to the Engineer within fourteen (14) business days after contract execution.


It is further certified that the aforementioned mutually acceptable quote and fully executed subcontract agreement represent the entire agreement between the parties involved and that no conversations, verbal agreements, or other forms of non-written representations shall serve to add to, delete, or modify the terms as stated.

The prime Contractor further represents that the aforementioned mutually acceptable quote and fully executed subcontract agreement shall remain on file for a period of not less than one year following completion of the prime's contract with the Department or for such longer period as provisions of governing Federal or State law or regulations may require. For purposes of this form, the term Prime Contractor shall refer to any Contractor utilizing a DBE subcontractor, regardless of tier, in which they are claiming DBE credit toward the contract goal.

Contractors further jointly and severally represent that said binding agreement is for the performance of a "commercially useful function" as that term is employed in 49 C.F.R. Part 26.55 (c), (d).

**TO BE SIGNED BY THE SUBCONTRACTOR TO THE PRIME CONTRACTOR, AND ANY LOWER TIER
SUBCONTRACTORS HAVING A CONTRACT WITH THE BELOW NAMED DBE FIRM**

Prime Contractor The LANE Construction Corporation

By: 
Signature

Regional V. P. Mid Atlantic Region
Title

Date: August 20, 2012

First Tier
Subcontractor if
Applicable

By: _____
Signature

_____ Title

Date: _____

Second Tier
Subcontractor if
Applicable

By: _____
Signature Title
Date: _____

Third Tier
Subcontractor if
Applicable

By: _____
Signature Title
Date: _____

DBE Contractor

NXL Construction Co., Inc.

By: William Killpat CFO
Signature Title
Date: 8/20/2012

COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
CERTIFICATION OF BINDING AGREEMENT
WITH

DISADVANTAGED BUSINESS ENTERPRISE FIRMS

Project No.: 0581-128-109, P101, RW201, C501, B627

Federal Project No.: NH-581-5 (035)

This form is to be submitted in accordance with the Department's Special Provision for Section 107.15.

It is hereby certified by the below signed Contractors that there exists a written quote, acceptable to the parties involved preliminary to a binding subcontract agreement stating the details concerning the work to be performed and the price which will be paid for the aforementioned work. This document is not intended to, nor should it be construed to, contain the entire text of the agreement between the contracting parties. This document does not take the place of, nor may it be substituted for, an official subcontracting agreement in those situations that may require such an agreement. A copy of the fully executed *subcontract agreement* shall be submitted to the Engineer within fourteen (14) business days after contract execution.

It is further certified that the aforementioned mutually acceptable quote and fully executed subcontract agreement represent the entire agreement between the parties involved and that no conversations, verbal agreements, or other forms of non-written representations shall serve to add to, delete, or modify the terms as stated.

The prime Contractor further represents that the aforementioned mutually acceptable quote and fully executed subcontract agreement shall remain on file for a period of not less than one year following completion of the prime's contract with the Department or for such longer period as provisions of governing Federal or State law or regulations may require. For purposes of this form, the term Prime Contractor shall refer to any Contractor utilizing a DBE subcontractor, regardless of tier, in which they are claiming DBE credit toward the contract goal.

Contractors further jointly and severally represent that said binding agreement is for the performance of a "commercially useful function" as that term is employed in 49 C.F.R. Part 26.55 (c), (d).

**TO BE SIGNED BY THE SUBCONTRACTOR TO THE PRIME CONTRACTOR, AND ANY LOWER TIER
SUBCONTRACTORS HAVING A CONTRACT WITH THE BELOW NAMED DBE FIRM**

Prime Contractor The LANE Construction Corporation

By: 

Signature


Regional V. P. Mid Atlantic Region

Title

Date: November 5, 2012

First Tier
Subcontractor if
Applicable

STV Incorporated

By: 

Signature

Vice President

Title

Date: November 5, 2012


Second Tier
Subcontractor if
Applicable

By: _____
Signature Title
Date: _____

Third Tier
Subcontractor if
Applicable

By: _____
Signature Title
Date: _____

DBE Contractor Thomas L. Brown Associates, P.C.

By:  _____
Signature Title
Date: October 31, 2012

COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
CERTIFICATION OF BINDING AGREEMENT
WITH
DISADVANTAGED BUSINESS ENTERPRISE FIRMS

Project No.: 0581-128-109, P101, RW201, C501, B627

Federal Project No.: NH-581-5 (035)

This form is to be submitted in accordance with the Department's Special Provision for Section 107.15.

It is hereby certified by the below signed Contractors that there exists a written quote, acceptable to the parties involved preliminary to a binding subcontract agreement stating the details concerning the work to be performed and the price which will be paid for the aforementioned work. This document is not intended to, nor should it be construed to, contain the entire text of the agreement between the contracting parties. This document does not take the place of, nor may it be substituted for, an official subcontracting agreement in those situations that may require such an agreement. A copy of the fully executed *subcontract agreement* shall be submitted to the Engineer within fourteen (14) business days after contract execution.


It is further certified that the aforementioned mutually acceptable quote and fully executed subcontract agreement represent the entire agreement between the parties involved and that no conversations, verbal agreements, or other forms of non-written representations shall serve to add to, delete, or modify the terms as stated.

The prime Contractor further represents that the aforementioned mutually acceptable quote and fully executed subcontract agreement shall remain on file for a period of not less than one year following completion of the prime's contract with the Department or for such longer period as provisions of governing Federal or State law or regulations may require. For purposes of this form, the term Prime Contractor shall refer to any Contractor utilizing a DBE subcontractor, regardless of tier, in which they are claiming DBE credit toward the contract goal.

Contractors further jointly and severally represent that said binding agreement is for the performance of a "commercially useful function" as that term is employed in 49 C.F.R. Part 26.55 (c), (d).

**TO BE SIGNED BY THE SUBCONTRACTOR TO THE PRIME CONTRACTOR, AND ANY LOWER TIER
SUBCONTRACTORS HAVING A CONTRACT WITH THE BELOW NAMED DBE FIRM**

Prime Contractor The LANE Construction Corporation

By: 

Signature


Regional V. P. Mid Atlantic Region

Title

Date: November 5, 2012

First Tier
Subcontractor if
Applicable

STV Incorporated

By: 

Signature

Vice President

Title

Date: November 5, 2012

Second Tier
Subcontractor if
Applicable


By: _____
Signature Title
Date: _____

Third Tier
Subcontractor if
Applicable

By: _____
Signature Title
Date: _____

DBE Contractor

ACCOMPONG ENGINEERING GROUP LLC

By:  _____
Signature President Title
Date: 11/4/12 _____

COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
CERTIFICATION OF BINDING AGREEMENT
WITH

DISADVANTAGED BUSINESS ENTERPRISE FIRMS

Project No.: 0581-128-109, P101, RW201, C501, B627

Federal Project No.: NH-581-5 (035)

This form is to be submitted in accordance with the Department's Special Provision for Section 107.15.

It is hereby certified by the below signed Contractors that there exists a written quote, acceptable to the parties involved preliminary to a binding subcontract agreement stating the details concerning the work to be performed and the price which will be paid for the aforementioned work. This document is not intended to, nor should it be construed to, contain the entire text of the agreement between the contracting parties. This document does not take the place of, nor may it be substituted for, an official subcontracting agreement in those situations that may require such an agreement. A copy of the fully executed *subcontract agreement* shall be submitted to the Engineer within fourteen (14) business days after contract execution.

It is further certified that the aforementioned mutually acceptable quote and fully executed subcontract agreement represent the entire agreement between the parties involved and that no conversations, verbal agreements, or other forms of non-written representations shall serve to add to, delete, or modify the terms as stated.

The prime Contractor further represents that the aforementioned mutually acceptable quote and fully executed subcontract agreement shall remain on file for a period of not less than one year following completion of the prime's contract with the Department or for such longer period as provisions of governing Federal or State law or regulations may require. For purposes of this form, the term Prime Contractor shall refer to any Contractor utilizing a DBE subcontractor, regardless of tier, in which they are claiming DBE credit toward the contract goal.

Contractors further jointly and severally represent that said binding agreement is for the performance of a "commercially useful function" as that term is employed in 49 C.F.R. Part 26.55 (c), (d).

**TO BE SIGNED BY THE SUBCONTRACTOR TO THE PRIME CONTRACTOR, AND ANY LOWER TIER
SUBCONTRACTORS HAVING A CONTRACT WITH THE BELOW NAMED DBE FIRM**

Prime Contractor The LANE Construction Corporation

By: 

Signature


Regional V. P. Mid Atlantic Region

Title

Date: November 5, 2012

First Tier
Subcontractor if
Applicable

STV Incorporated

By: 

Signature

Vice President

Title

Date: November 5, 2012

Second Tier
Subcontractor if
Applicable

By: _____
Signature Title

Date: _____

Third Tier
Subcontractor if
Applicable

By: _____
Signature Title

Date: _____

DBE Contractor DMY Inc.

By: _____
Signature President Title

Date: 11/01/2012

COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
CERTIFICATION OF BINDING AGREEMENT
WITH

DISADVANTAGED BUSINESS ENTERPRISE FIRMS

Project No.: 0581-128-109, P101, RW201, C501, B627

Federal Project No.: NH-581-5 (035)

This form is to be submitted in accordance with the Department's Special Provision for Section 107.15.

It is hereby certified by the below signed Contractors that there exists a written quote, acceptable to the parties involved preliminary to a binding subcontract agreement stating the details concerning the work to be performed and the price which will be paid for the aforementioned work. This document is not intended to, nor should it be construed to, contain the entire text of the agreement between the contracting parties. This document does not take the place of, nor may it be substituted for, an official subcontracting agreement in those situations that may require such an agreement. A copy of the fully executed *subcontract agreement* shall be submitted to the Engineer within fourteen (14) business days after contract execution.


It is further certified that the aforementioned mutually acceptable quote and fully executed subcontract agreement represent the entire agreement between the parties involved and that no conversations, verbal agreements, or other forms of non-written representations shall serve to add to, delete, or modify the terms as stated.

The prime Contractor further represents that the aforementioned mutually acceptable quote and fully executed subcontract agreement shall remain on file for a period of not less than one year following completion of the prime's contract with the Department or for such longer period as provisions of governing Federal or State law or regulations may require. For purposes of this form, the term Prime Contractor shall refer to any Contractor utilizing a DBE subcontractor, regardless of tier, in which they are claiming DBE credit toward the contract goal.

Contractors further jointly and severally represent that said binding agreement is for the performance of a "commercially useful function" as that term is employed in 49 C.F.R. Part 26.55 (c), (d).

**TO BE SIGNED BY THE SUBCONTRACTOR TO THE PRIME CONTRACTOR, AND ANY LOWER TIER
SUBCONTRACTORS HAVING A CONTRACT WITH THE BELOW NAMED DBE FIRM**

Prime Contractor The LANE Construction Corporation

By: 

Signature


Regional V. P. Mid Atlantic Region

Title

Date: November 5, 2012

First Tier
Subcontractor if
Applicable

STV Incorporated

By: 

Signature

Vice President

Title

Date: November 5, 2012

Second Tier
Subcontractor if
Applicable


By: _____
Signature Title
Date: _____

Third Tier
Subcontractor if
Applicable

By: _____
Signature Title
Date: _____

DBE Contractor

mercado consultants, inc.

By:  _____
Signature Title
Date: 11/1/17

COMMONWEALTH OF VIRGINIA
DEPARTMENT OF TRANSPORTATION
CERTIFICATION OF BINDING AGREEMENT
WITH
DISADVANTAGED BUSINESS ENTERPRISE FIRMS

Project No.: 0581-128-109, P101, RW201, C501, B627

Federal Project No.: NH-581-5 (035)

This form is to be submitted in accordance with the Department's Special Provision for Section 107.15.

It is hereby certified by the below signed Contractors that there exists a written quote, acceptable to the parties involved preliminary to a binding subcontract agreement stating the details concerning the work to be performed and the price which will be paid for the aforementioned work. This document is not intended to, nor should it be construed to, contain the entire text of the agreement between the contracting parties. This document does not take the place of, nor may it be substituted for, an official subcontracting agreement in those situations that may require such an agreement. A copy of the fully executed *subcontract agreement* shall be submitted to the Engineer within fourteen (14) business days after contract execution.


It is further certified that the aforementioned mutually acceptable quote and fully executed subcontract agreement represent the entire agreement between the parties involved and that no conversations, verbal agreements, or other forms of non-written representations shall serve to add to, delete, or modify the terms as stated.

The prime Contractor further represents that the aforementioned mutually acceptable quote and fully executed subcontract agreement shall remain on file for a period of not less than one year following completion of the prime's contract with the Department or for such longer period as provisions of governing Federal or State law or regulations may require. For purposes of this form, the term Prime Contractor shall refer to any Contractor utilizing a DBE subcontractor, regardless of tier, in which they are claiming DBE credit toward the contract goal.

Contractors further jointly and severally represent that said binding agreement is for the performance of a "commercially useful function" as that term is employed in 49 C.F.R. Part 26.55 (c), (d).

**TO BE SIGNED BY THE SUBCONTRACTOR TO THE PRIME CONTRACTOR, AND ANY LOWER TIER
SUBCONTRACTORS HAVING A CONTRACT WITH THE BELOW NAMED DBE FIRM**

Prime Contractor The LANE Construction Corporation

By: 
Signature

Regional V. P. Mid Atlantic Region

Title

Date: August 20, 2012

First Tier
Subcontractor if
Applicable

By: _____
Signature

_____ Title

Date: _____

Second Tier
Subcontractor if
Applicable

By: _____
Signature Title
Date: _____

Third Tier
Subcontractor if
Applicable

By: _____
Signature Title
Date: _____

DBE Contractor

Cherry Contracting, Inc / Cherry Project

By: *[Signature]*
Signature Title
Date: *5/15/12*



4.8.9 - Debarment Forms

ATTACHMENT 11.8.6(a)
CERTIFICATION REGARDING DEBARMENT
PRIMARY COVERED TRANSACTIONS

Project No.: 0581-128-109, P101, RW201, C501, B627

1) The prospective primary participant certifies to the best of its knowledge and belief, that it and its principals:

a) Are not presently debarred, suspended, proposed for debarment, declared ineligible, or voluntarily excluded from covered transactions by any Federal department or agency.

b) Have not within a three-year period preceding this proposal been convicted of or had a civil judgment rendered against them for commission of fraud or a criminal offense in connection with obtaining, attempting to obtain, or performing a public (Federal, State or local) transaction or contract under a public transaction; and have not been convicted of any violations of Federal or State antitrust statutes or commission of embezzlement, theft, forgery, bribery, falsification, or destruction of records, making false statements, or receiving stolen property;

c) Are not presently indicted for or otherwise criminally or civilly charged by a governmental entity (Federal, State or local) with commission of any of the offenses enumerated in paragraph 1) b) of this certification; and

d) Have not within a three-year period preceding this application/proposal had one or more public transactions (Federal, State or local) terminated for cause or default.

2) Where the prospective primary participant is unable to certify to any of the statements in this certification, such prospective participant shall attach an explanation to this proposal.

The undersigned makes the foregoing statements to be filed with the proposal submitted on behalf of the Offeror for contracts to be let by the Commonwealth Transportation Board.


Signature

November 5, 2012
Date

Regional Vice President,
Mid-Atlantic Region
Title

The LANE Construction Corporation
Name of Firm

ATTACHMENT 11.8.6(b)
CERTIFICATION REGARDING DEBARMENT
LOWER TIER COVERED TRANSACTIONS

Project No.: 0581-128-109, P101, RW201, C501, B627

- 1) The prospective lower tier participant certifies, by submission of this proposal, that neither it nor its principals is presently debarred, suspended, proposed for debarment, declared ineligible, or voluntarily excluded from participation in this transaction by any Federal department or agency.
- 2) Where the prospective lower tier participant is unable to certify to any of the statements in this certification, such prospective participant shall attach an explanation to this proposal.

The undersigned makes the foregoing statements to be filed with the proposal submitted on behalf of the Offeror for contracts to be let by the Commonwealth Transportation Board.


Signature _____ Date 8-15-12 Title CHIEF EXEC. MANAGER

A.P. SERVICES, LLC
Name of Firm

ATTACHMENT 11.8.6(b)
CERTIFICATION REGARDING DEBARMENT
LOWER TIER COVERED TRANSACTIONS

Project No.: 0581-128-109, P101, RW201, C501, B627

- 1) The prospective lower tier participant certifies, by submission of this proposal, that neither it nor its principals is presently debarred, suspended, proposed for debarment, declared ineligible, or voluntarily excluded from participation in this transaction by any Federal department or agency.
- 2) Where the prospective lower tier participant is unable to certify to any of the statements in this certification, such prospective participant shall attach an explanation to this proposal.

The undersigned makes the foregoing statements to be filed with the proposal submitted on behalf of the Offeror for contracts to be let by the Commonwealth Transportation Board.

Sandra Hopkins 8-15-12 President
Signature Date Title

Sandra's Trucking Co Inc
Name of Firm

ATTACHMENT 11.8.6(b)
CERTIFICATION REGARDING DEBARMENT
LOWER TIER COVERED TRANSACTIONS

Project No.: 0581-128-109, P101, RW201, C501, B627

- 1) The prospective lower tier participant certifies, by submission of this proposal, that neither it nor its principals is presently debarred, suspended, proposed for debarment, declared ineligible, or voluntarily excluded from participation in this transaction by any Federal department or agency.
- 2) Where the prospective lower tier participant is unable to certify to any of the statements in this certification, such prospective participant shall attach an explanation to this proposal.

The undersigned makes the foregoing statements to be filed with the proposal submitted on behalf of the Offeror for contracts to be let by the Commonwealth Transportation Board.

William Killpar 8/20/2012 CFO
Signature Date Title

NXL Construction Co., Inc.
Name of Firm

ATTACHMENT 11.8.6(b)
CERTIFICATION REGARDING DEBARMENT
LOWER TIER COVERED TRANSACTIONS

Project No.: 0581-128-109, P101, RW201, C501, B627

- 1) The prospective lower tier participant certifies, by submission of this proposal, that neither it nor its principals is presently debarred, suspended, proposed for debarment, declared ineligible, or voluntarily excluded from participation in this transaction by any Federal department or agency.
- 2) Where the prospective lower tier participant is unable to certify to any of the statements in this certification, such prospective participant shall attach an explanation to this proposal.

The undersigned makes the foregoing statements to be filed with the proposal submitted on behalf of the Offeror for contracts to be let by the Commonwealth Transportation Board.

 8/15/12 Vice President
Signature Date Title

Cherry Contracting, Inc. / Cherry Prasad
Name of Firm

ATTACHMENT NO. 3.2.5(b)

**CERTIFICATION REGARDING DEBARMENT
LOWER TIER COVERED TRANSACTIONS**

Project No.: 0581-128-109, P101, RW201, C501, B627

- 1) The prospective lower tier participant certifies, by submission of this proposal, that neither it nor its principals is presently debarred, suspended, proposed for debarment, declared ineligible, or voluntarily excluded from participation in this transaction by any Federal department or agency.
- 2) Where the prospective lower tier participant is unable to certify to any of the statements in this certification, such prospective participant shall attach an explanation to this proposal.

The undersigned makes the foregoing statements to be filed with the proposal submitted on behalf of the Offeror for contracts to be let by the Commonwealth Transportation Board.

Anna S. Flanagan

November 5, 2012

Vice President

Signature

Date

Title

STV Incorporated

Name of Firm

ATTACHMENT NO. 3.2.5(b)

**CERTIFICATION REGARDING DEBARMENT
LOWER TIER COVERED TRANSACTIONS**

Project No.: 0581-128-109, P101, RW201, C501, B627

1) The prospective lower tier participant certifies, by submission of this proposal, that neither it nor its principals is presently debarred, suspended, proposed for debarment, declared ineligible, or voluntarily excluded from participation in this transaction by any Federal department or agency.

2) Where the prospective lower tier participant is unable to certify to any of the statements in this certification, such prospective participant shall attach an explanation to this proposal.

The undersigned makes the foregoing statements to be filed with the proposal submitted on behalf of the Offeror for contracts to be let by the Commonwealth Transportation Board.

Carroll D. 11/4/12 President
Signature Date Title

Accompany Engineering Group
Name of Firm

ATTACHMENT NO. 3.2.5(b)

**CERTIFICATION REGARDING DEBARMENT
LOWER TIER COVERED TRANSACTIONS**

Project No.: 0581-128-109, P101, RW201, C501, B627

- 1) The prospective lower tier participant certifies, by submission of this proposal, that neither it nor its principals is presently debarred, suspended, proposed for debarment, declared ineligible, or voluntarily excluded from participation in this transaction by any Federal department or agency.
- 2) Where the prospective lower tier participant is unable to certify to any of the statements in this certification, such prospective participant shall attach an explanation to this proposal.

The undersigned makes the foregoing statements to be filed with the proposal submitted on behalf of the Offeror for contracts to be let by the Commonwealth Transportation Board.

William H. Benham 10/31/12

Signature

Date

Vice President of Transportation

Title

Anderson & Associates, Inc.

Name of Firm

ATTACHMENT NO. 3.2.5(b)


**CERTIFICATION REGARDING DEBARMENT
LOWER TIER COVERED TRANSACTIONS**

Project No.: 0581-128-109, P101, RW201, C501, B627

1) The prospective lower tier participant certifies, by submission of this proposal, that neither it nor its principals is presently debarred, suspended, proposed for debarment, declared ineligible, or voluntarily excluded from participation in this transaction by any Federal department or agency.

2) Where the prospective lower tier participant is unable to certify to any of the statements in this certification, such prospective participant shall attach an explanation to this proposal.

The undersigned makes the foregoing statements to be filed with the proposal submitted on behalf of the Offeror for contracts to be let by the Commonwealth Transportation Board.

	11/01/2012	President
Signature	Date	Title

DMY Inc.
Name of Firm

ATTACHMENT NO. 3.2.5(b)

**CERTIFICATION REGARDING DEBARMENT
LOWER TIER COVERED TRANSACTIONS**

Project No.: 0581-128-109, P101, RW201, C501, B627

1) The prospective lower tier participant certifies, by submission of this proposal, that neither it nor its principals is presently debarred, suspended, proposed for debarment, declared ineligible, or voluntarily excluded from participation in this transaction by any Federal department or agency.

2) Where the prospective lower tier participant is unable to certify to any of the statements in this certification, such prospective participant shall attach an explanation to this proposal.

The undersigned makes the foregoing statements to be filed with the proposal submitted on behalf of the Offeror for contracts to be let by the Commonwealth Transportation Board.



November 5, 2012

Chief Operating Officer

Signature

Date

Title

O.R. Colan Associates of Florida, LLC

Name of Firm

ATTACHMENT NO. 3.2.5(b)


**CERTIFICATION REGARDING DEBARMENT
LOWER TIER COVERED TRANSACTIONS**

Project No.: 0581-128-109, P101, RW201, C501, B627

- 1) The prospective lower tier participant certifies, by submission of this proposal, that neither it nor its principals is presently debarred, suspended, proposed for debarment, declared ineligible, or voluntarily excluded from participation in this transaction by any Federal department or agency.

- 2) Where the prospective lower tier participant is unable to certify to any of the statements in this certification, such prospective participant shall attach an explanation to this proposal.

The undersigned makes the foregoing statements to be filed with the proposal submitted on behalf of the Offeror for contracts to be let by the Commonwealth Transportation Board.

	11/05/2012	President
Signature	Date	Title

Thomas L. Brown Associates, P.C.

Name of Firm


ATTACHMENT NO. 3.2.5(b)

**CERTIFICATION REGARDING DEBARMENT
LOWER TIER COVERED TRANSACTIONS**

Project No.: 0581-128-109, P101, RW201, C501, B627

- 1) The prospective lower tier participant certifies, by submission of this proposal, that neither it nor its principals is presently debarred, suspended, proposed for debarment, declared ineligible, or voluntarily excluded from participation in this transaction by any Federal department or agency.
- 2) Where the prospective lower tier participant is unable to certify to any of the statements in this certification, such prospective participant shall attach an explanation to this proposal.

The undersigned makes the foregoing statements to be filed with the proposal submitted on behalf of the Offeror for contracts to be let by the Commonwealth Transportation Board.


Signature _____ Date 11/1/12 Title President
Mercado Consultants, Inc.
Name of Firm _____
